




BALL CORPORATION - ZEPHYR WIND PROJECT 2.0
North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Sep-20	617,000	710,596	228,314	239,356	242,926
Oct-20	956,000	850,601	284,918	272,587	293,096
Nov-20	1,107,000	1,330,282	442,746	426,184	461,352
Dec-20	1,098,000	1,263,339	421,761	411,065	430,513
Jan-21	1,251,000	798,530	263,091	267,336	268,103
Feb-21	1,044,000	1,137,529	368,454	371,784	397,291
Mar-21	1,119,000	1,351,254	441,435	433,777	476,042
Apr-21	1,116,000	941,559	301,517	305,193	334,849
May-21	876,000	755,823	246,357	249,062	260,404
Jun-21	637,000	667,180	226,175	213,521	227,484
Jul-21	518,000	423,089	144,295	141,912	136,882
Aug-21	448,000	407,609	139,023	132,947	135,639
Sep-21	617,000	957,074	321,730	316,478	318,866
Production 2021 (ytd) (kWh)	7,626,000	7,439,647	2,452,077	2,432,010	2,555,560
Total Production (kWh)*	10,787,000	10,883,869	3,601,502	3,541,846	3,740,521
Capacity Factor*	27.61%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

September-2021

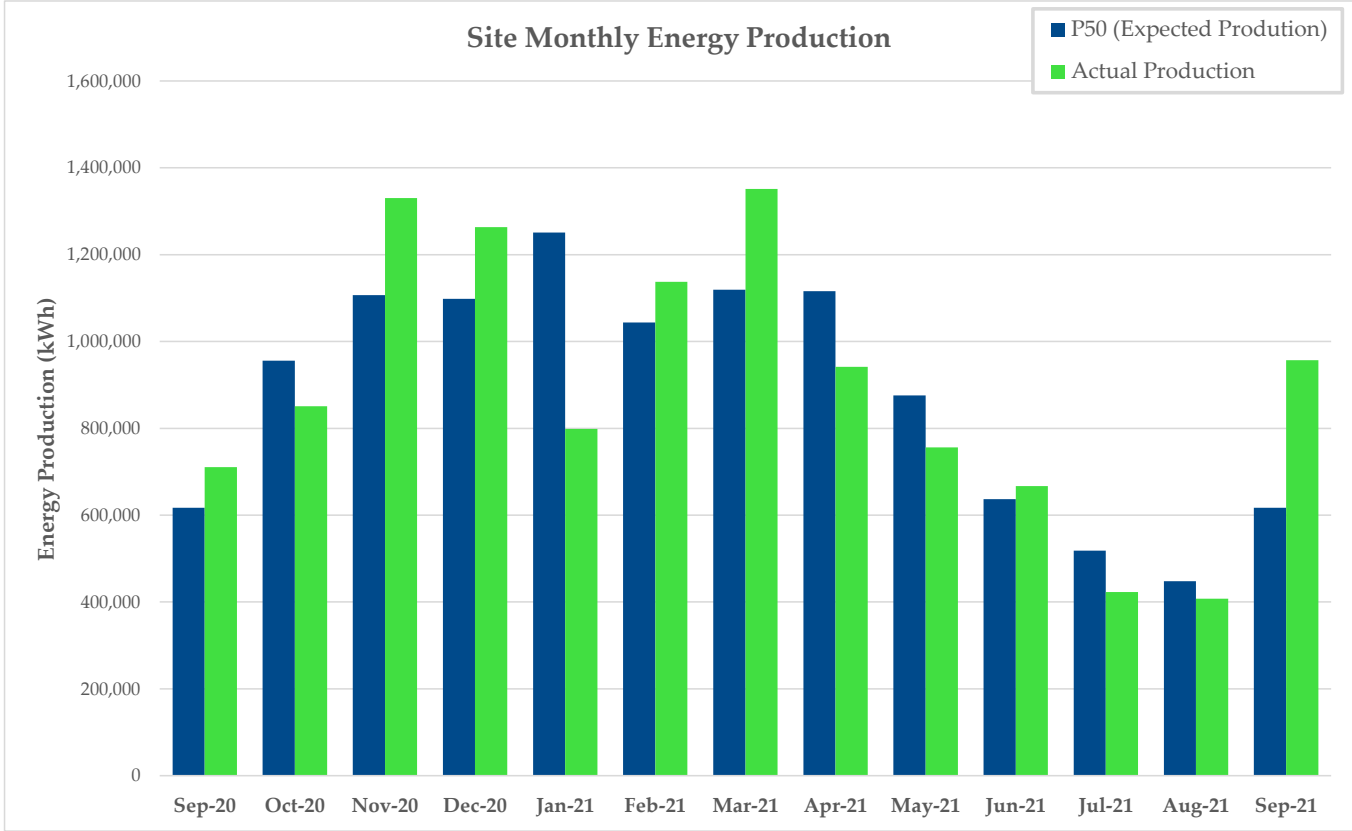

Monthly Report
September-2021



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2022	Goldwind 1.5 Year Maintenance	~8	Z4
March-2022	Goldwind 1.5 Year Maintenance	~8	Z5
March-2022	Goldwind 1.5 Year Maintenance	~8	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
9/7/2021	Goldwind 1 Year Maintenenance	Planned	4.22	Z4
9/8/2021	Goldwind 1 Year Maintenenance	Planned	4.17	Z5
9/10/2021	Goldwind 1 Year Maintenenance	Planned	3.85	Z6
9/29/2021	One Energy Annual Inspection	Unplanned	2.56	Z5
9/29/2021	One Energy Annual Inspection	Unplanned	2.11	Z6

F. Turbine Availability & Downtime*

Availability	This Month	Year To Date
Z4	100.00%	99.90%
Z5	100.00%	99.92%
Z6	99.97%	99.57%
Avg	99.99%	99.80%

Downtime (hr)	This Month	Year To Date
Z4	4.22	101.95
Z5	6.73	68.74
Z6	6.17	101.86
Total	17.12	272.55

G. Billed Data

Meter Reading (Date/Time)	9/17/2021 12:00 AM
Ball 2.0 Production (This Period)	533,299 kWh
Ball 2.0 Consumption (This Period)	3,593 kWh
Billed kWh	529,706 kWh
Next Meter Reading	10/16/2021 12:00 AM

H. Report Notes and Comments

*March downtime and availability under further review.
