



HARPSTER WIND PROJECT

Harpster, OH


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Sep-20	224,000	194,360
Oct-20	338,000	240,522
Nov-20	402,000	356,013
Dec-20	403,000	399,725
Jan-21	460,000	252,077
Feb-21	372,000	359,816
Mar-21	417,000	441,144
Apr-21	399,000	331,073
May-21	311,000	211,014
Jun-21	228,000	199,146
Jul-21	179,000	117,480
Aug-21	157,000	116,887
Sep-21	224,000	257,547
Production 2021 (ytd) (kWh)	2,747,000	2,286,184
Total Production (kWh)*	3,890,000	3,282,444
Capacity Factor*	24.98%	

*Value calculated over the last 12 months

B. Site Energy Production Graph

September-2021

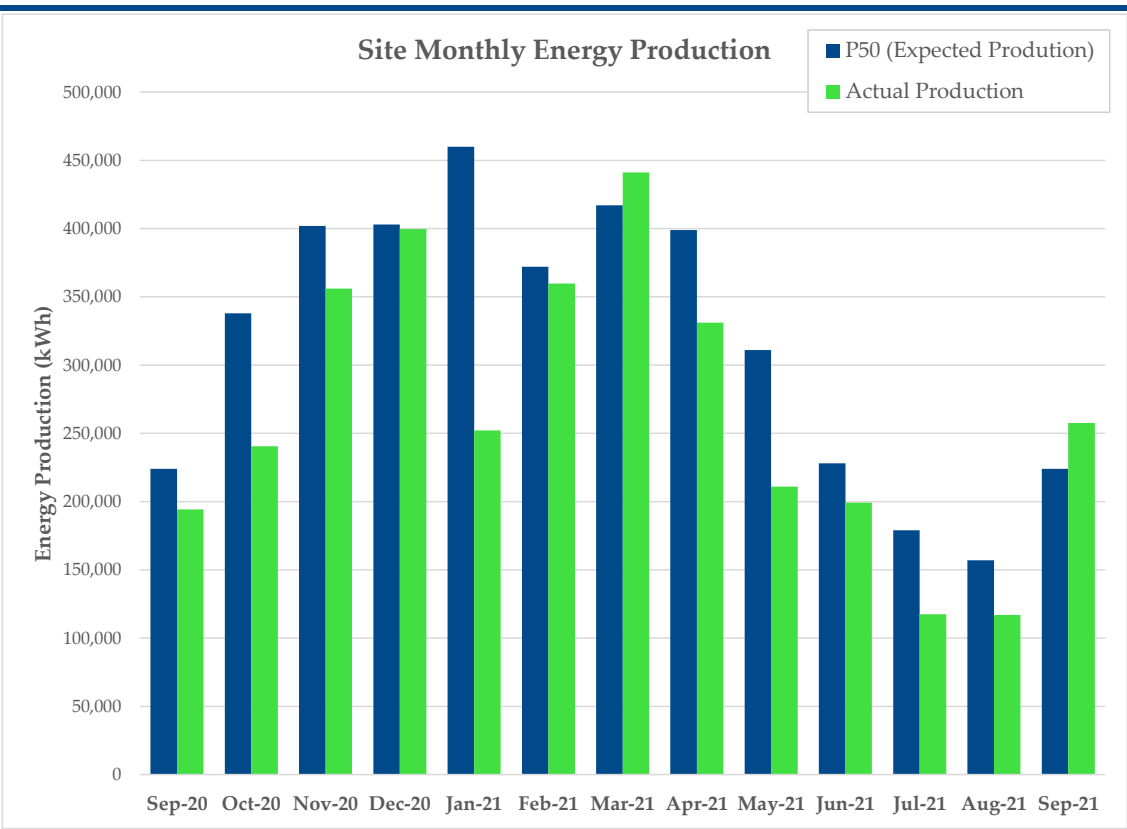

Monthly Report

September-2021



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2021	Goldwind 5.5 Year Maintenance	~8	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
9/30/2021	One Energy Annual Inspection	Unplanned	3.38	H1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
H1	100.00%	99.96%
Downtime (hr)	This Month	Year To Date
H1	5.85	65.27

G. Billed Data

Meter Reading (Date/Time)	9/24/2021 12:00 AM
Meter To Date Produced	18,234,100 kWh
Meter To Date Consumed	63,314 kWh
Last Reading Produced	18,032,778 kWh
Last Reading Consumed	62,290 kWh
Billed kWh	200,298 kWh
Next Meter Reading	10/23/2021 12:00 AM

H. Report Notes and Comments
