


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Nov-20	796,000	913,861	455,668	458,193
Dec-20	820,000	810,783	417,721	393,062
Jan-21	931,000	544,556	269,433	275,123
Feb-21	737,000	766,729	389,871	376,858
Mar-21	777,000	939,050	475,834	463,216
Apr-21	722,000	668,188	334,264	333,924
May-21	564,000	507,392	250,537	256,855
Jun-21	422,000	431,379	211,027	220,352
Jul-21	351,000	280,633	134,016	146,617
Aug-21	303,000	269,721	132,186	137,535
Sep-21	431,000	616,679	299,115	317,564
Oct-21	674,000	503,743	250,852	252,891
Nov-21	796,000	791,404	397,996	393,408
Production 2021 (ytd) (kWh)	6,708,000	6,319,474	3,145,131	3,174,343
Total Production (LTM) (kWh)	7,528,000	7,130,257	3,562,852	3,567,405
Capacity Factor (LTM)	27.13%			

B. Site Energy Production Graph

November-2021

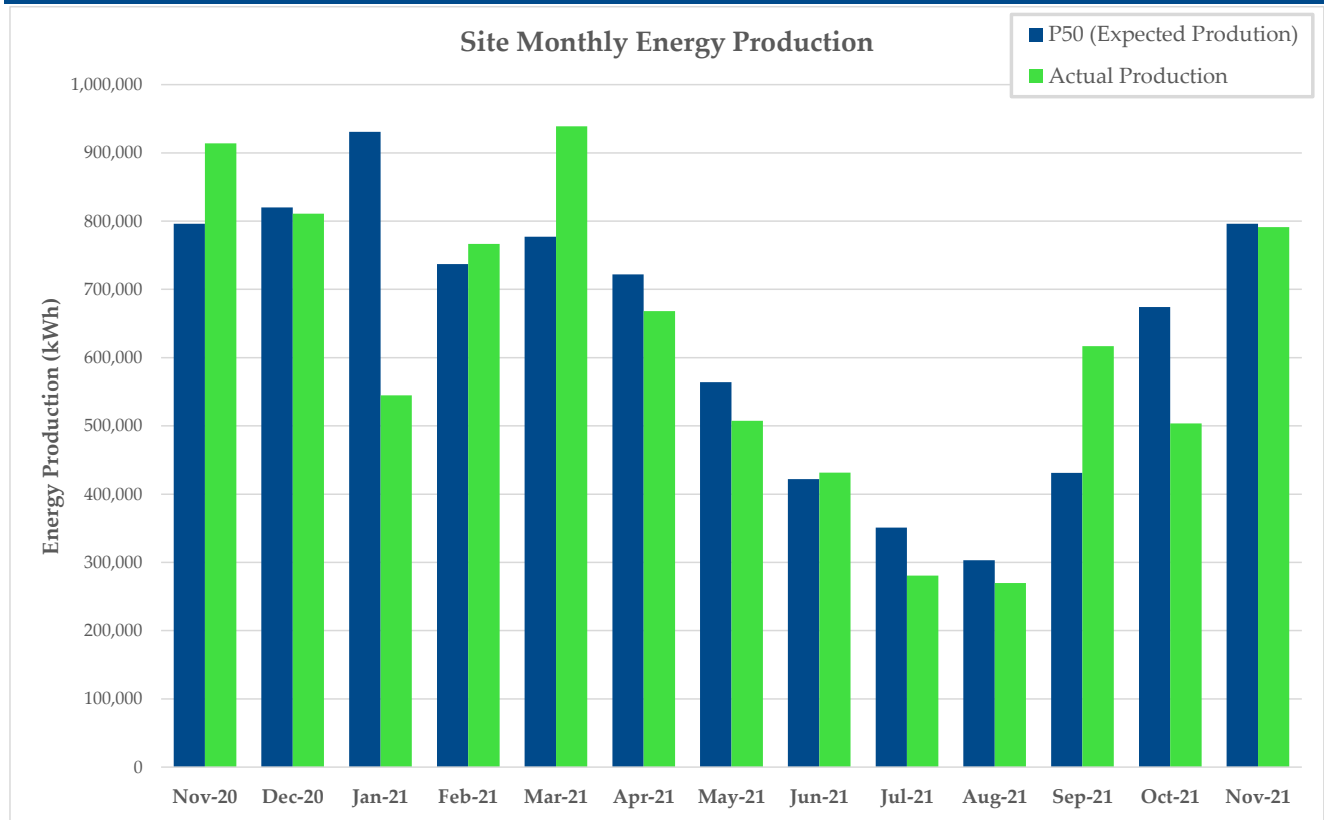

Monthly Report

November-2021



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-22	Goldwind 3.5 Year Maintenance	~8	V1
April-22	Goldwind 3.5 Year Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/4/2021	Goldwind 3 Year Maintenenance	Planned	4.39	V1
11/4/2021	Goldwind 3 Year Maintenenance	Planned	3.09	V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	99.78%
V2	100.00%	99.82%
Avg	100.00%	99.80%

Downtime (hr)	This Month	Year To Date
V1	4.39	97.94
V2	3.09	81.66
Total	7.48	179.60

G. Billed Data

Meter Reading (Date/Time)	12/1/2021 12:00 AM
Meter To Date Produced	22,812,113 kWh
Meter To Date Consumed	59,578 kWh
Last Reading Produced	22,038,660 kWh
Last Reading Consumed	58,494 kWh
Billed kWh	772,369 kWh
Next Meter Reading	1/1/2022 12:00 AM

H. Report Notes and Comments
