




BALL CORPORATION - ZEPHYR WIND PROJECT 2.0
North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Dec-20	1,098,000	1,263,339	421,761	411,065	430,513
Jan-21	1,251,000	798,530	263,091	267,336	268,103
Feb-21	1,044,000	1,137,529	368,454	371,784	397,291
Mar-21	1,119,000	1,351,254	441,435	433,777	476,042
Apr-21	1,116,000	941,559	301,517	305,193	334,849
May-21	876,000	755,823	246,357	249,062	260,404
Jun-21	637,000	667,180	226,175	213,521	227,484
Jul-21	518,000	423,089	144,295	141,912	136,882
Aug-21	448,000	407,609	139,023	132,947	135,639
Sep-21	617,000	957,074	321,730	316,478	318,866
Oct-21	956,000	739,181	243,855	238,641	256,685
Nov-21	1,107,000	1,150,429	384,301	366,844	399,284
Dec-21	1,098,000	1,141,220	374,435	374,888	391,897
Production 2021 (ytd) (kWh)	10,787,000	10,470,477	3,454,668	3,412,383	3,603,426
Total Production (kWh) (LTM)	10,787,000	10,470,477	3,454,668	3,412,383	3,603,426
Capacity Factor (LTM)	26.56%				

B. Site Energy Production Graph

December-2021

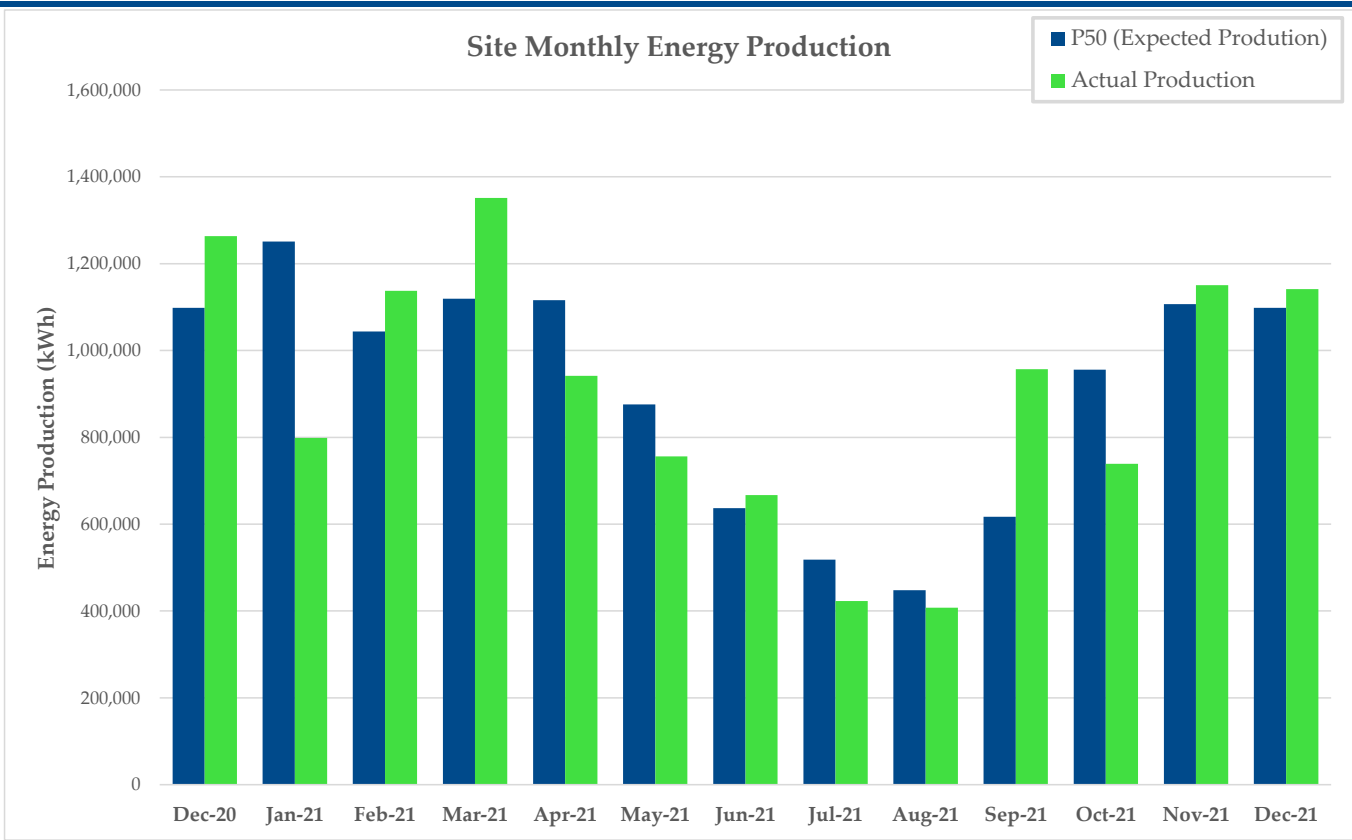

Monthly Report
December-2021



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2022	Goldwind 1.5 Year Maintenance	~8	Z4
March-2022	Goldwind 1.5 Year Maintenance	~8	Z5
March-2022	Goldwind 1.5 Year Maintenance	~8	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
12/11/2021	Weather Shutdown	Unplanned	7.25	Z4, Z5, Z6
12/24/2021	Plant Shutdown	Unplanned	11.32	Z4, Z5, Z6
12/28 - 29/2021	Weather Shutdown	Unplanned	17.53	Z4
12/28 - 29/2021	Weather Shutdown	Unplanned	17.23	Z5, Z6

F. Turbine Availability & Downtime*

Availability	This Month	Year To Date
Z4	100.00%	99.92%
Z5	99.92%	99.87%
Z6	100.00%	99.68%
Avg	99.97%	99.83%

Downtime (hr)	This Month	Year To Date
Z4	28.85	137.29
Z5	21.68	121.90
Z6	21.09	129.81
Total	71.62	389.00

G. Billed Data

Meter Reading (Date/Time)	12/17/2021 12:00 AM
Ball 2.0 Production (This Period)	1,352,738 kWh
Ball 2.0 Consumption (This Period)	1,869 kWh
Billed kWh	1,350,869 kWh
Next Meter Reading	1/20/2022 12:00 AM

H. Report Notes and Comments

*March downtime and availability under further review.
**December 2021 Downtime and Availability are pending review and will be confirmed in the January 2022 report.
