


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Jan-21	931,000	544,556	269,433	275,123
Feb-21	737,000	766,729	389,871	376,858
Mar-21	777,000	939,050	475,834	463,216
Apr-21	722,000	668,188	334,264	333,924
May-21	564,000	507,392	250,537	256,855
Jun-21	422,000	431,379	211,027	220,352
Jul-21	351,000	280,633	134,016	146,617
Aug-21	303,000	269,721	132,186	137,535
Sep-21	431,000	616,679	299,115	317,564
Oct-21	674,000	503,743	250,852	252,891
Nov-21	796,000	791,404	397,996	393,408
Dec-21	820,000	763,656	384,433	379,223
Jan-22	931,000	817,296	405,482	411,814
Production 2022 (ytd) (kWh)	931,000	817,296	405,482	411,814
Total Production (LTM) (kWh)	7,528,000	7,355,870	3,665,613	3,690,257
Capacity Factor (LTM)	27.99%			

B. Site Energy Production Graph

January-2022

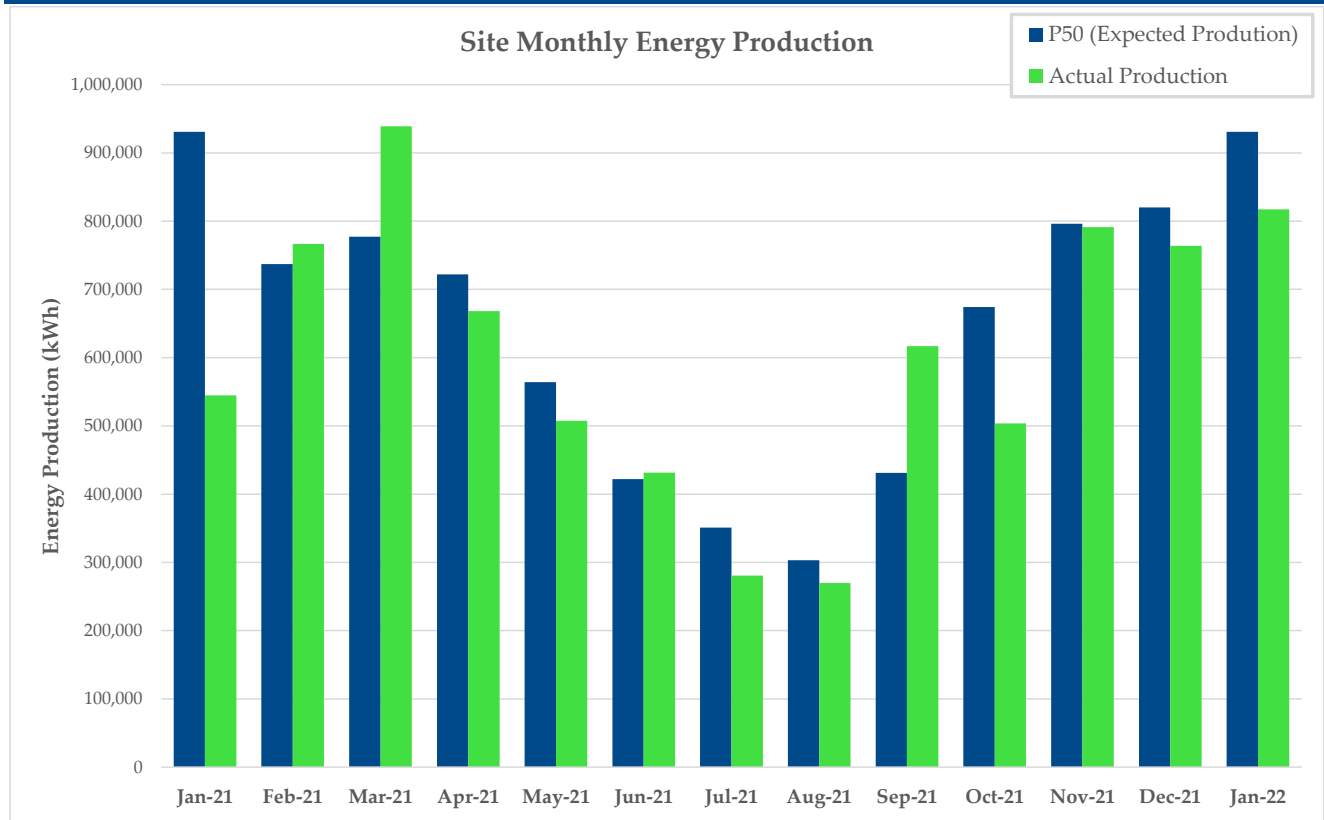

Monthly Report

January-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-22	Goldwind 3.5 Year Maintenance	~8	V1
April-22	Goldwind 3.5 Year Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/1/2022-1/3/2022	Weather Shutdown	Unplanned	31.96	V1
1/1/2022-1/3/2022	Weather Shutdown	Unplanned	31.59	V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	100.00%
V2	99.97%	99.97%
Avg	99.98%	99.98%

Downtime (hr)	This Month	Year To Date
V1	32.20	32.20
V2	31.59	31.59
Total	63.79	63.79

G. Billed Data

Meter Reading (Date/Time)	2/1/2022 12:00 AM
Meter To Date Produced	24,348,840 kWh
Meter To Date Consumed	63,346 kWh
Last Reading Produced	23,553,908 kWh
Last Reading Consumed	61,627 kWh
Billed kWh	793,213 kWh
Next Meter Reading	3/1/2022 12:00 AM

H. Report Notes and Comments

*January 2022 Downtime and Availability numbers are pending review and will be confirmed in the February 2022 report.
