



BALL CORPORATION - ZEPHYR WIND PROJECT 2.0


North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

		Energy Production (kWh)				
		Site		By Turbine		
		P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Jan-21		1,251,000	798,530	263,091	267,336	268,103
Feb-21		1,044,000	1,137,529	368,454	371,784	397,291
Mar-21		1,119,000	1,351,254	441,435	433,777	476,042
Apr-21		1,116,000	941,559	301,517	305,193	334,849
May-21		876,000	755,823	246,357	249,062	260,404
Jun-21		637,000	667,180	226,175	213,521	227,484
Jul-21		518,000	423,089	144,295	141,912	136,882
Aug-21		448,000	407,609	139,023	132,947	135,639
Sep-21		617,000	957,074	321,730	316,478	318,866
Oct-21		956,000	739,181	243,855	238,641	256,685
Nov-21		1,107,000	1,150,429	384,301	366,844	399,284
Dec-21		1,098,000	1,141,220	374,435	374,888	391,897
Jan-22		1,251,000	1,253,751	420,362	406,883	426,506
Production 2022 (ytd) (kWh)		1,251,000	1,253,751	420,362	406,883	426,506
Total Production (kWh) (LTM)		10,787,000	10,925,698	3,611,939	3,551,930	3,761,829
Capacity Factor (LTM)		27.72%				

B. Site Energy Production Graph

January-2022

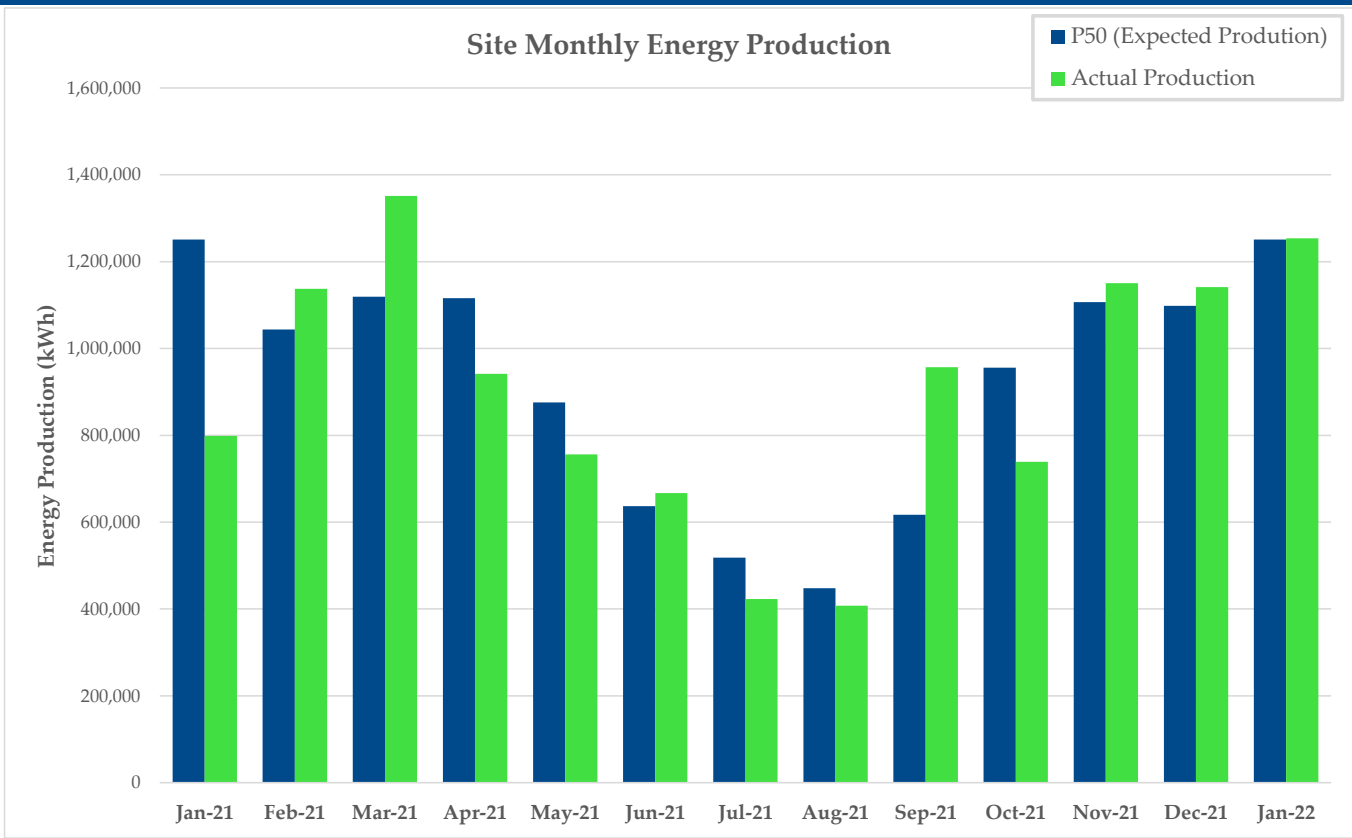

Monthly Report
January-2022



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2022	Goldwind 1.5 Year Maintenance	~8	Z4
March-2022	Goldwind 1.5 Year Maintenance	~8	Z5
March-2022	Goldwind 1.5 Year Maintenance	~8	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/2/2022-1/3/2022	Weather Shutdown	Unplanned	24.80	Z4
1/2/2022-1/3/2022	Weather Shutdown	Unplanned	24.23	Z5
1/2/2022-1/3/2022	Weather Shutdown	Unplanned	22.78	Z6
1/25/2022	Weather Shutdown	Unplanned	13.31	Z6

F. Turbine Availability & Downtime*

Availability	This Month	Year To Date
Z4	100.00%	100.00%
Z5	100.00%	100.00%
Z6	100.00%	100.00%
Avg	100.00%	100.00%

Downtime (hr)	This Month	Year To Date
Z4	24.8	24.80
Z5	27.8	27.80
Z6	32.82	32.82
Total	85.42	85.42

G. Billed Data

Meter Reading (Date/Time)	1/20/2022 12:00 AM
Ball 2.0 Production (This Period)	1,349,245 kWh
Ball 2.0 Consumption (This Period)	3,003 kWh
Billed kWh	1,346,243 kWh
Next Meter Reading	2/18/2022 12:00 AM

H. Report Notes and Comments

*March downtime and availability under further review.
**January Downtime and Availability are pending review and will be confirmed in the February 2022 report.
