


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Jan-21	875,000	568,442	288,651	279,791
Feb-21	917,000	760,836	386,235	374,601
Mar-21	802,000	962,627	490,998	471,629
Apr-21	951,000	667,905	338,467	329,438
May-21	601,000	509,680	262,275	247,405
Jun-21	425,000	479,735	244,261	235,474
Jul-21	390,000	298,836	152,425	146,411
Aug-21	399,000	297,535	152,628	144,907
Sep-21	337,000	665,033	337,170	327,863
Oct-21	637,000	518,984	262,835	256,149
Nov-21	834,000	849,882	425,765	424,117
Dec-21	1,015,000	821,418	415,630	405,788
Jan-22	875,000	857,334	429,640	427,694
Production 2022 (ytd) (kWh)	875,000	857,334	429,640	427,694
Total Production (kWh) (LTM)	8,183,000	7,689,805	3,898,329	3,791,476
Capacity Factor (LTM)	29.26%			

B. Site Energy Production Graph

January-2022

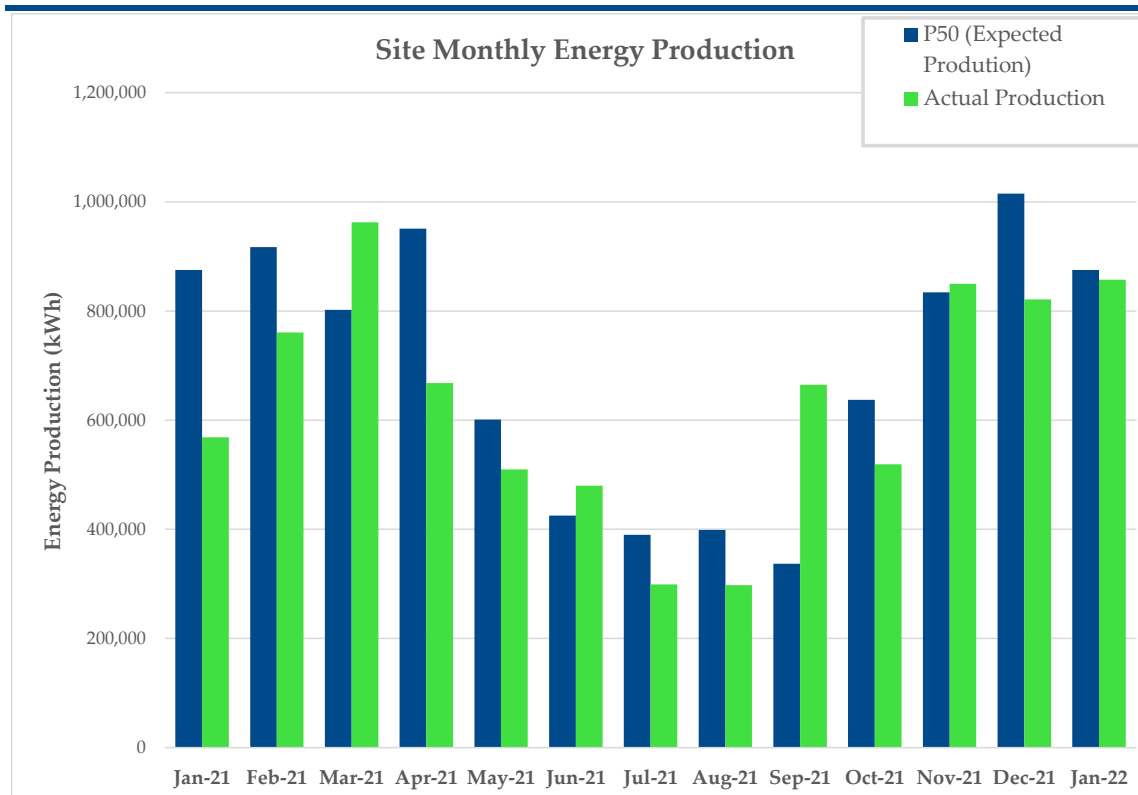

Monthly Report

January-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2022	Goldwind 6.5 Year Maintenance	~8	W1
May-2022	Goldwind 6.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	100.00%
W2	100.00%	100.00%
Avg	100.00%	100.00%

Downtime (hr)	This Month	Year To Date
W1	0	0.00
W2	0	0.00
Total	0	0.00

G. Billed Data

Meter Reading (Date/Time)	1/29/2022 12:00 AM
Meter To Date Produced	46,361,132 kWh
Meter To Date Consumed	92,547 kWh
Last Reading Produced	45,501,870 kWh
Last Reading Consumed	91,270 kWh
Billed kWh	857,985 kWh
Next Meter Reading	3/1/2022 12:00 AM

H. Report Notes and Comments

*January 2022 Downtime and Availability numbers are pending review and will be confirmed in the February 2022 report.
