


A. Site Energy Production Summary

Energy Production (kWh)						
Site		By Turbine				
	P50 (Expected Production)	Actual Production	W1	W2	W3	
Jan-21	1,306,000	661,923	220,641	220,641	220,641	**
Feb-21	1,137,000	896,420	308,413	291,691	296,316	***
Mar-21	1,134,000	1,290,867	437,185	424,582	429,100	
Apr-21	1,176,000	752,920	257,397	246,019	249,504	
May-21	927,000	646,261	217,827	210,837	217,597	
Jun-21	634,000	571,998	186,211	188,627	197,160	
Jul-21	527,000	318,063	107,885	100,155	110,023	
Aug-21	449,000	324,019	109,256	105,233	109,530	
Sep-21	610,000	740,131	243,253	241,498	255,380	
Oct-21	990,000	693,360	241,616	219,829	231,915	
Nov-21	1,123,000	976,482	349,225	311,053	316,204	
Dec-21	1,153,000	1,088,213	372,080	354,578	361,555	
Jan-22	1,306,000	845,320	315,868	177,718	351,734	
Production 2022 (ytd) (kWh)	1,306,000	845,320	315,868	177,718	351,734	
Total Production (kWh) (LTM)	11,166,000	9,144,054	3,146,216	2,871,820	3,126,018	
Capacity Factor (LTM)	23.20%					

B. Site Energy Production Graph

January-2022

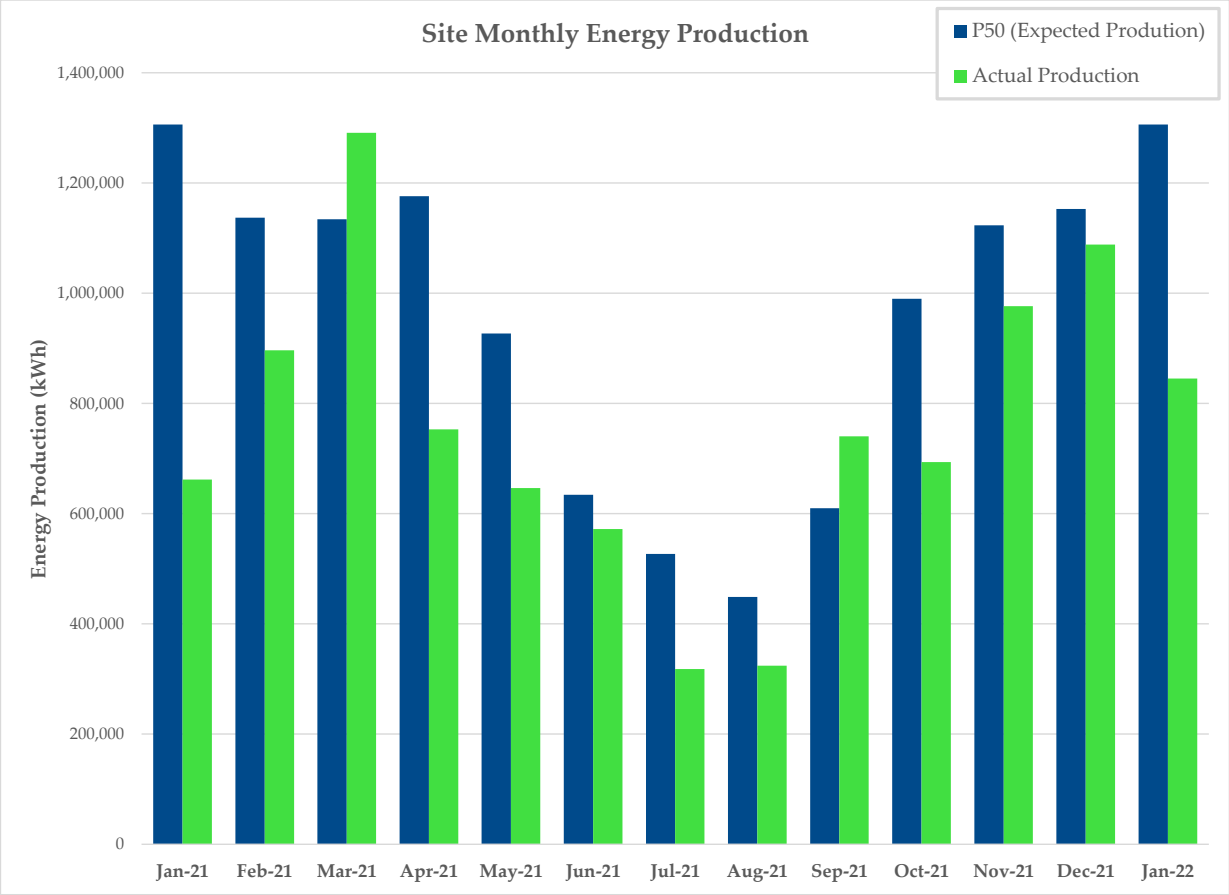

Monthly Report
January-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2022	Goldwind 4.5 Year Maintenance	~8	W1
May-2022	Goldwind 4.5 Year Maintenance	~8	W2
May-2022	Goldwind 4.5 Year Maintenance	~8	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/2/2022	Weather Shutdown	Unplanned	5.71	W1
1/2/2022	Weather Shutdown	Unplanned	5.3	W2
1/2/2022	Weather Shutdown	Unplanned	6.05	W3
1/4/2022	Weather Shutdown	Unplanned	4.03	W3
1/08/2022-1/11/2022	Transformer Fault	Unplanned	79.52	W1
1/08/2022-1/20/2022	Transformer Fault	Unplanned	290.70	W2
1/08/2022-1/11/2022	Transformer Fault	Unplanned	78.28	W3
1/17/2022	System Testing	Unplanned	4.10	W1
1/19/2022	System Testing	Unplanned	8.2	W1
1/19/2022	System Testing	Unplanned	8.41	W3
1/24/2022-1/25/2022	Weather Shutdown	Unplanned	16.86	W1
1/24/2022-1/25/2022	Weather Shutdown	Unplanned	17.33	W2
1/24/2022-1/25/2022	Weather Shutdown	Unplanned	17.32	W3
1/29/2022	Weather Shutdown	Unplanned	6.01	W2
1/29/2022	Weather Shutdown	Unplanned	6.02	W3

F. Turbine Availability & Downtime****

Availability	This Month	Year To Date
W1	99.98%	99.98%
W2	99.97%	99.97%
W3	99.90%	99.90%
Avg	99.95%	99.95%

Downtime (hr)	This Month	Year To Date
W1	116.67	116.67
W2	322.18	322.18
W3	126.05	126.05
Total	564.90	564.90

G. Billed Data

Meter Reading (Date/Time)	1/21/2022 12:00 AM
Meter To Date Produced	38,392,429 kWh
Meter To Date Consumed	118,039 kWh
Last Reading Produced	37,485,344 kWh
Last Reading Consumed	116,441 kWh
Billed kWh	905,487 kWh
Next Meter Reading	2/21/2022 12:00 AM

H. Report Notes and Comments

**January 2021 Production read from the meter due to communication issues and will be updated if SCADA data becomes available. Total metered production divided to estimate per turbine total.

***February 2021 Production is estimate due to communication issues.

****Year to date does not include January 2021 due to communication issue. April downtime and availability under further review.

*****January 2022 Downtime and Availability numbers are pending review and will be confirmed in the February 2022 report.
