



BALL CORPORATION - ZEPHYR WIND PROJECT 1.0
North Findlay Wind Campus, Findlay, OH

Monthly Report
February-2022




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Feb-21	1,310,000	1,112,551	384,385	376,283	351,883
Mar-21	1,140,000	1,328,761	439,843	458,260	430,658
Apr-21	1,359,000	930,702	327,011	316,411	287,280
May-21	856,000	723,486	251,234	238,571	233,681
Jun-21	599,000	668,103	237,234	223,304	207,565
Jul-21	549,000	406,084	144,149	134,124	127,811
Aug-21	559,000	401,761	142,351	132,538	126,872
Sep-21	482,000	926,810	324,892	307,203	294,715
Oct-21	916,000	726,057	254,792	242,990	228,275
Nov-21	1,203,000	1,191,103	418,962	401,518	370,623
Dec-21	1,475,000	1,163,071	403,095	393,380	366,596
Jan-22	1,260,000	1,252,569	435,949	420,553	396,067
Feb-22	1,310,000	1,354,099	469,778	464,716	419,606
Production 2022 (ytd) (kWh)	2,570,000	2,606,668	905,727	885,269	815,673
Total Production (LTM) (kWh)	11,708,000	11,072,606	3,849,290	3,733,568	3,489,749
Capacity Factor (LTM)	28.09%				

B. Site Energy Production Graph

February-2022

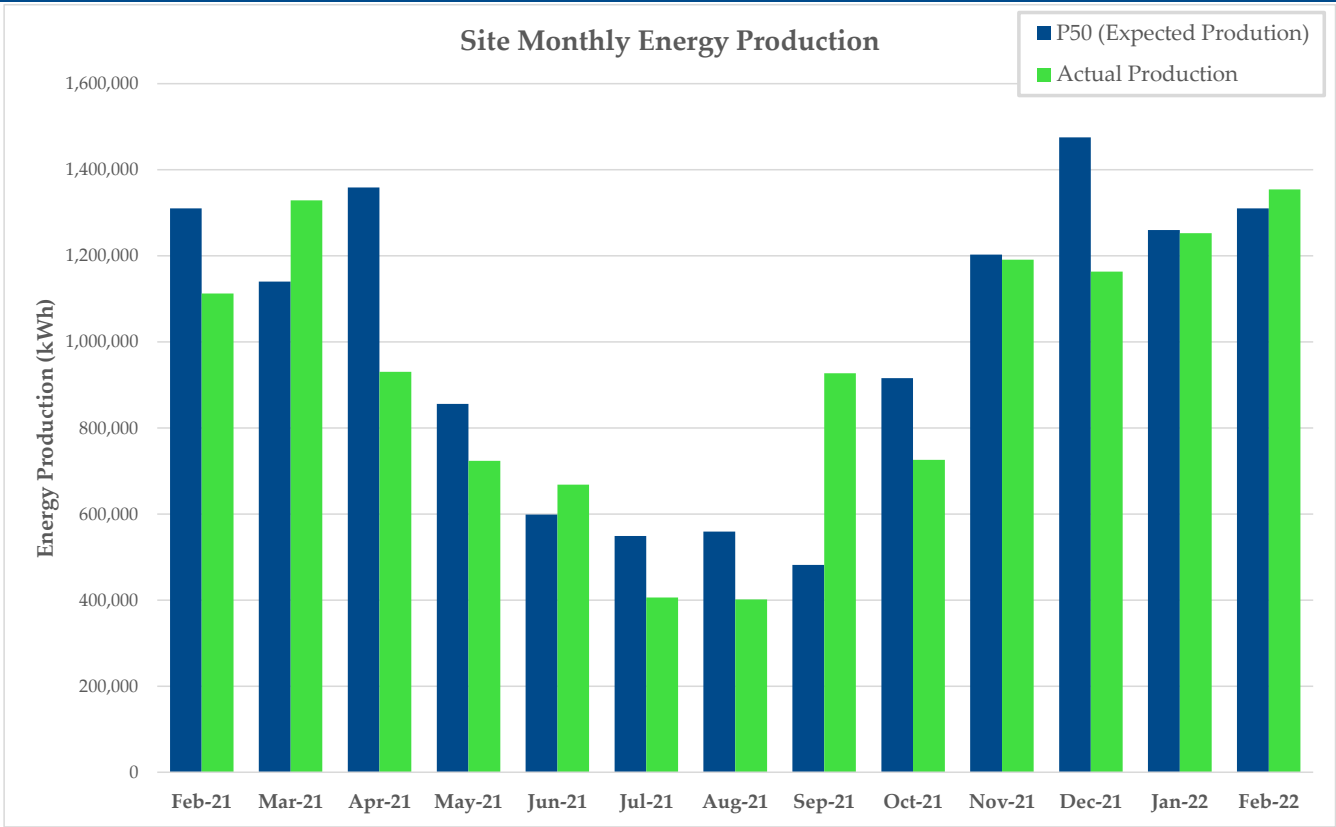

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2022	Goldwind 6 Year Maintenance	~15	Z1
April-2022	Goldwind 6 Year Maintenance	~15	Z2
April-2022	Goldwind 6 Year Maintenance	~15	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/17/2022-2/18/2022	Weather Shutdown	Unplanned	22.37	Z1
2/17/2022-2/18/2022	Weather Shutdown	Unplanned	22.38	Z2
2/17/2022-2/19/2022	Weather Shutdown	Unplanned	40.8	Z3
2/25/2022	Weather Shutdown	Unplanned	24.00	Z1, Z2, Z3
2/26/2022	Weather Shutdown	Unplanned	10.40	Z3

F. Turbine Availability & Downtime*

Availability	This Month	Year To Date
Z1	99.67%	99.83%
Z2	99.89%	99.91%
Z3	100.00%	100.00%
Avg	99.85%	99.91%

Downtime (hr)	This Month	Year To Date
Z1	48.86	60.17
Z2	47.22	59.09
Z3	78.63	107.29
Total	174.71	226.55

G. Billed Data

Meter Reading (Date/Time)	2/18/2022 12:00 AM
Ball 1.0 Production (This Period)	1,100,949 kWh
Ball 1.0 Consumption (This Period)	1,481 kWh
Billed kWh	1,099,468 kWh
Next Meter Reading	3/19/2022 12:00 AM

H. Report Notes and Comments

*February 2022 Downtime and Availability numbers are pending review and will be confirmed in the March 2022 report.

**February 2022 production includes estimates due to a SCADA server error.
