



BALL CORPORATION - ZEPHYR WIND PROJECT 2.0


North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

		Energy Production (kWh)			
		Site		By Turbine	
		P50 (Expected Production)	Actual Production	Z4	Z5
				Z6	
Feb-21	1,044,000	1,137,529	368,454	371,784	397,291
Mar-21	1,119,000	1,351,254	441,435	433,777	476,042
Apr-21	1,116,000	941,559	301,517	305,193	334,849
May-21	876,000	755,823	246,357	249,062	260,404
Jun-21	637,000	667,180	226,175	213,521	227,484
Jul-21	518,000	423,089	144,295	141,912	136,882
Aug-21	448,000	407,609	139,023	132,947	135,639
Sep-21	617,000	957,074	321,730	316,478	318,866
Oct-21	956,000	739,181	243,855	238,641	256,685
Nov-21	1,107,000	1,150,429	384,301	366,844	399,284
Dec-21	1,098,000	1,141,220	374,435	374,888	391,897
Jan-22	1,251,000	1,253,751	420,362	406,883	426,506
Feb-22	1,044,000	1,306,639	438,679	422,217	445,743
Production 2022 (ytd) (kWh)	2,295,000	2,560,390	859,041	829,100	872,249
Total Production (kWh) (LTM)	10,787,000	11,094,808	3,682,164	3,602,363	3,810,281
Capacity Factor (LTM)	28.15%				

B. Site Energy Production Graph

February-2022

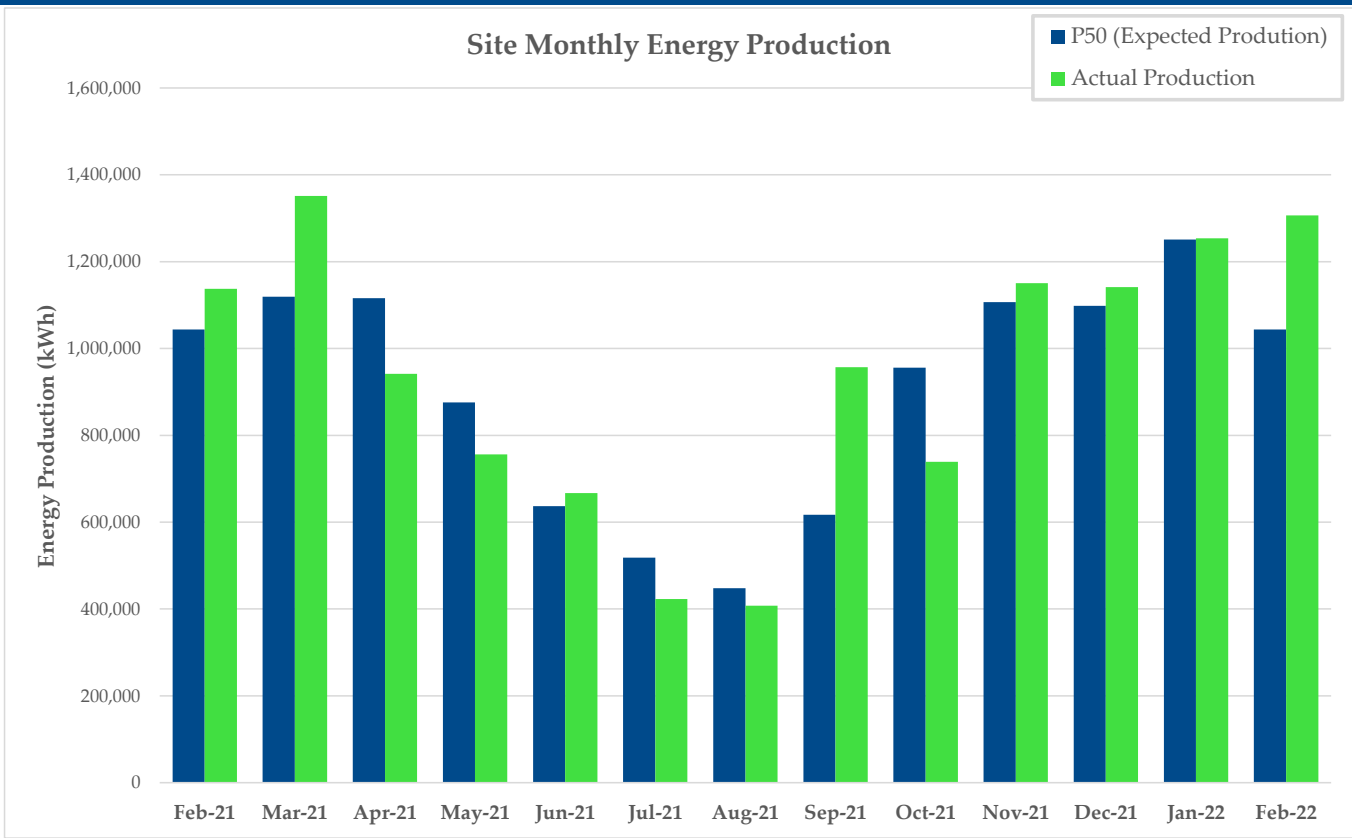

Monthly Report
February-2022



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2022	Goldwind 1.5 Year Maintenance	~8	Z4
March-2022	Goldwind 1.5 Year Maintenance	~8	Z5
March-2022	Goldwind 1.5 Year Maintenance	~8	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/12/2022-2/14/2022	Fault/Weather allocation	Unplanned	40.85	Z5
2/17/2022-2/19/2022	Weather Shutdown	Unplanned	39.22	Z4
2/17/2022-2/18/2022	Weather Shutdown	Unplanned	39.10	Z5
2/17/2022-2/19/2022	Weather Shutdown	Unplanned	39.63	Z6
2/21/2022	Fault	Unplanned	5.98	Z6
2/24/2022-2/26/2022	Weather Shutdown	Unplanned	39.22	Z4
2/24/2022-2/26/2022	Weather Shutdown	Unplanned	39.10	Z5
2/24/2022-2/26/2022	Weather Shutdown	Unplanned	39.63	Z6

F. Turbine Availability & Downtime*

Availability	This Month	Year To Date
Z4	99.94%	99.97%
Z5	100.00%	100.00%
Z6	99.20%	99.60%
Avg	99.71%	99.86%

Downtime (hr)	This Month	Year To Date
Z4	82.66	115.41
Z5	109.8	146.10
Z6	84.02	130.62
Total	276.48	392.13

H. Report Notes and Comments

*February 2022 Downtime and Availability are pending review and will be confirmed in the March 2022 report.

G. Billed Data

Meter Reading (Date/Time)	2/18/2022 12:00 AM
Ball 2.0 Production (This Period)	1,130,393 kWh
Ball 2.0 Consumption (This Period)	1,903 kWh
Billed kWh	1,128,490 kWh
Next Meter Reading	3/19/2022 12:00 AM
