


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Feb-21	478,000	404,742
Mar-21	422,000	513,464
Apr-21	499,000	370,891
May-21	318,000	262,656
Jun-21	222,000	267,226
Jul-21	201,000	157,870
Aug-21	211,000	138,271
Sep-21	182,000	352,762
Oct-21	341,000	280,589
Nov-21	445,000	429,438
Dec-21	537,000	446,947
Jan-22	455,000	449,235
Feb-22	478,000	481,534
Production 2022 (ytd) (kWh)	933,000	930,769
Total Production (LTM) (kWh)	4,311,000	4,150,883
Capacity Factor (LTM)	31.59%	

B. Site Energy Production Graph

February-2022

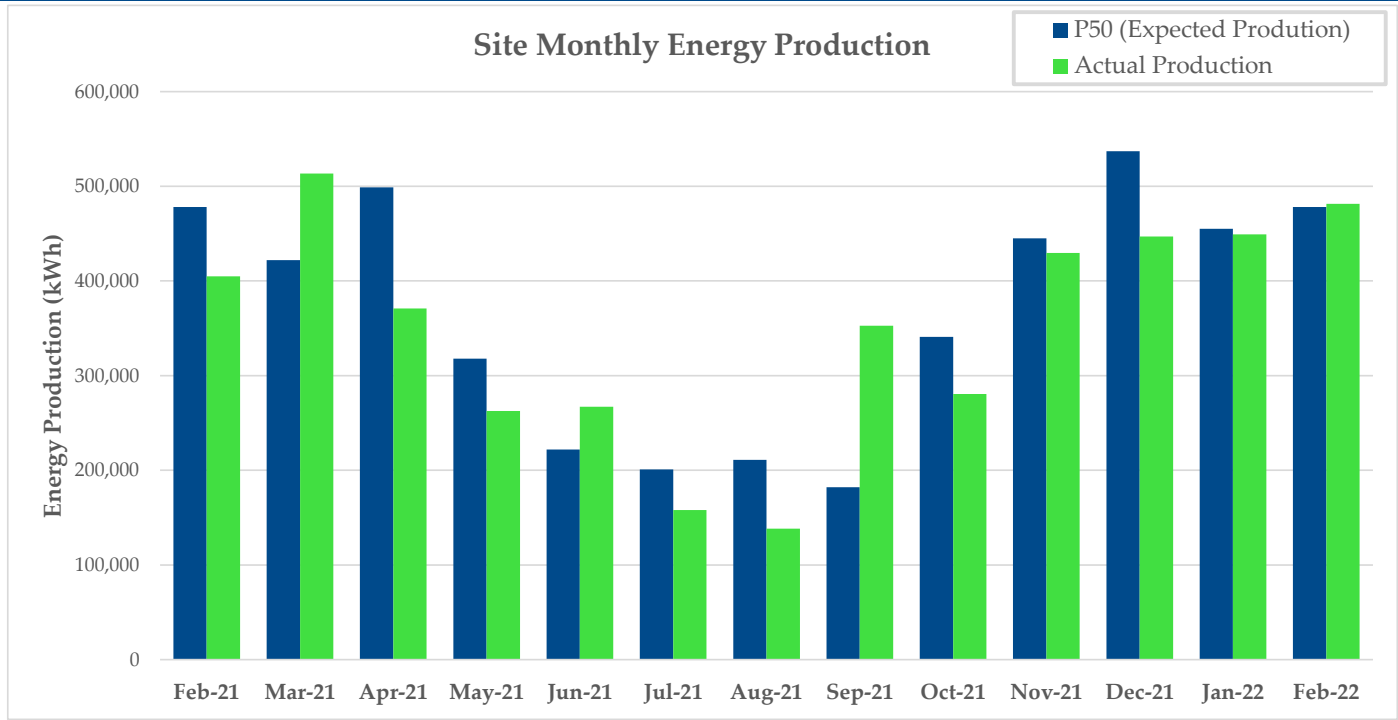

Monthly Report
February-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2022	Goldwind 4 Year Maintenance	~15	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/17/2022-2/19/2022	Weather Shutdown	Unplanned	40.71	W1
2/24/2022-2/26/2022	Weather Shutdown	Unplanned	39.32	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	100.00%
Downtime (hr)	This Month	Year To Date
W1	80.03	112.46

G. Billed Data

Meter Reading (Date/Time)	3/1/2022 12:00 AM
Meter To Date Produced	16,156,613 kWh
Meter To Date Consumed	72,764 kWh
Last Reading Produced	15,681,233 kWh
Last Reading Consumed	71,751 kWh
Billed kWh	474,367 kWh
Next Meter Reading	4/1/2022 12:00 AM

H. Report Notes and Comments

*February 2022 Downtime and Availability numbers are pending review and will be confirmed in the March 2022 report.
