


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Mar-21	1,119,000	1,351,254	441,435	433,777	476,042
Apr-21	1,116,000	941,559	301,517	305,193	334,849
May-21	876,000	755,823	246,357	249,062	260,404
Jun-21	637,000	667,180	226,175	213,521	227,484
Jul-21	518,000	423,089	144,295	141,912	136,882
Aug-21	448,000	407,609	139,023	132,947	135,639
Sep-21	617,000	957,074	321,730	316,478	318,866
Oct-21	956,000	739,181	243,855	238,641	256,685
Nov-21	1,107,000	1,150,429	384,301	366,844	399,284
Dec-21	1,098,000	1,141,220	374,435	374,888	391,897
Jan-22	1,251,000	1,253,751	420,362	406,883	426,506
Feb-22	1,044,000	1,306,639	438,679	422,217	445,743
Mar-22	1,119,000	1,335,480	443,031	438,839	453,610
Production 2022 (ytd) (kWh)	3,414,000	3,895,870	1,302,072	1,267,939	1,325,859
Total Production (kWh) (LTM)	10,787,000	11,079,034	3,683,760	3,607,425	3,787,849
Capacity Factor (LTM)	28.11%				

B. Site Energy Production Graph

March-2022

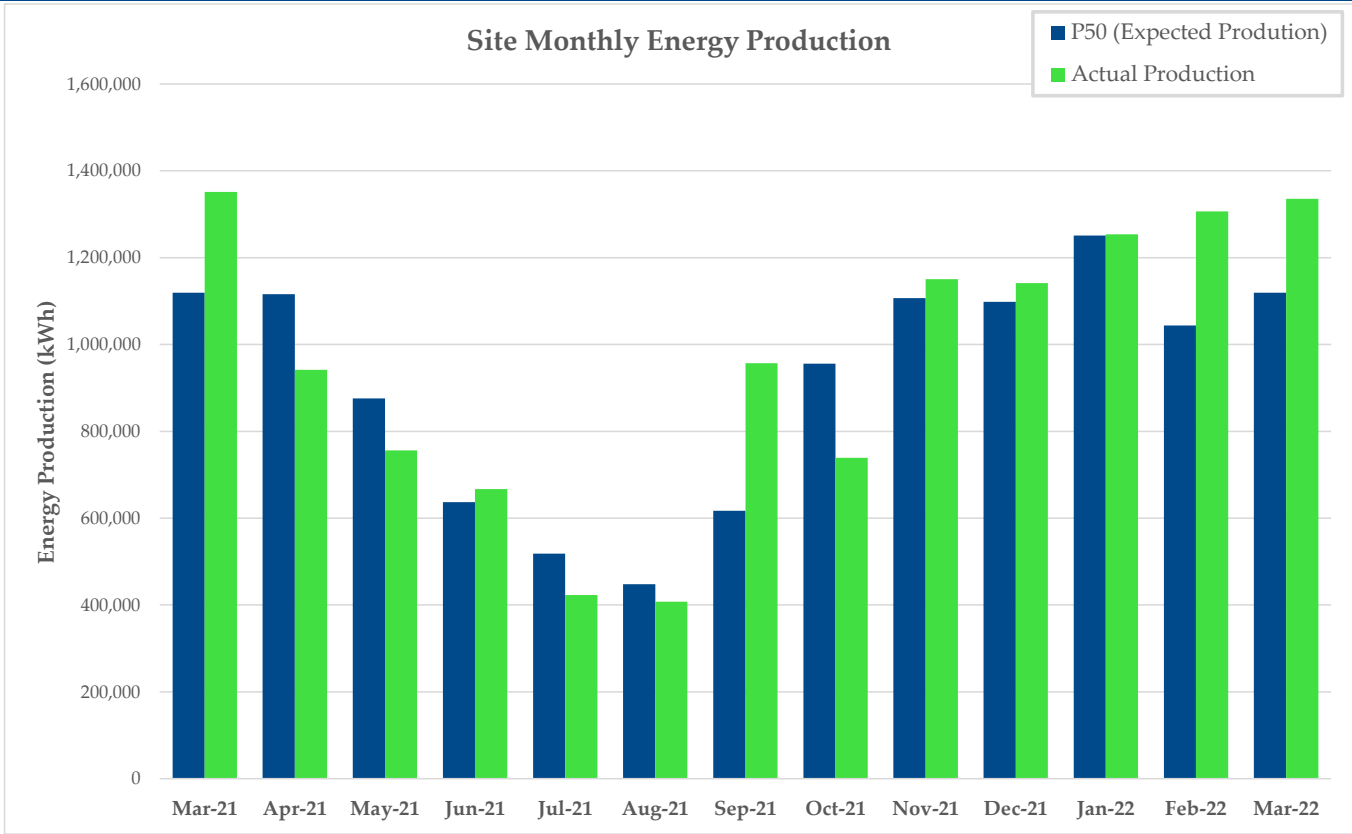

Monthly Report
March-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2022	Goldwind 2 Year Maintenance	~15	Z4
September-2022	Goldwind 2 Year Maintenance	~15	Z5
September-2022	Goldwind 2 Year Maintenance	~15	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/8/2022	Goldwind 1.5 Year Maintenance	Planned	3.42	Z4
3/9/2022	Goldwind 1.5 Year Maintenance	Planned	2.43	Z5
3/9/2022	Goldwind 1.5 Year Maintenance	Planned	3.92	Z6
3/24/2022	One Energy Semi-Annual Inspection	Unplanned	1.71	Z4
3/24/2022	One Energy Semi-Annual Inspection	Unplanned	1.93	Z5
3/25/2022	One Energy Semi-Annual Inspection	Unplanned	1.49	Z6
3/30/2022	Goldwind 1.5 Year Maintenance	Planned	0.62	Z4, Z5, Z6

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z4	100.00%	99.98%
Z5	100.00%	97.98%
Z6	100.00%	99.70%
Avg	100.00%	99.22%

Downtime (hr)	This Month	Year To Date
Z4	6.82	122.23
Z5	6.05	152.10
Z6	7.1	137.72
Total	19.97	412.05

G. Billed Data

Meter Reading (Date/Time)	3/19/2022 12:00 AM
Ball 2.0 Production (This Period)	1,106,231 kWh
Ball 2.0 Consumption (This Period)	2,674 kWh
Billed kWh	1,103,557 kWh
Next Meter Reading	4/20/2022 12:00 AM

H. Report Notes and Comments

*March 2022 production includes estimates due to a SCADA server error.
