


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Apr-21	722,000	668,188	334,264	333,924
May-21	564,000	507,392	250,537	256,855
Jun-21	422,000	431,379	211,027	220,352
Jul-21	351,000	280,633	134,016	146,617
Aug-21	303,000	269,721	132,186	137,535
Sep-21	431,000	616,679	299,115	317,564
Oct-21	674,000	503,743	250,852	252,891
Nov-21	796,000	791,404	397,996	393,408
Dec-21	820,000	763,656	384,433	379,223
Jan-22	931,000	817,296	405,482	411,814
Feb-22	737,000	838,853	421,431	417,422
Mar-22	777,000	942,768	455,809	486,959
Apr-22	722,000	794,963	403,811	391,152
Production 2022 (ytd) (kWh)	3,167,000	3,393,880	1,686,533	1,707,347
Total Production (LTM) (kWh)	7,528,000	7,558,487	3,746,695	3,811,792
Capacity Factor (LTM)	28.76%			

B. Site Energy Production Graph

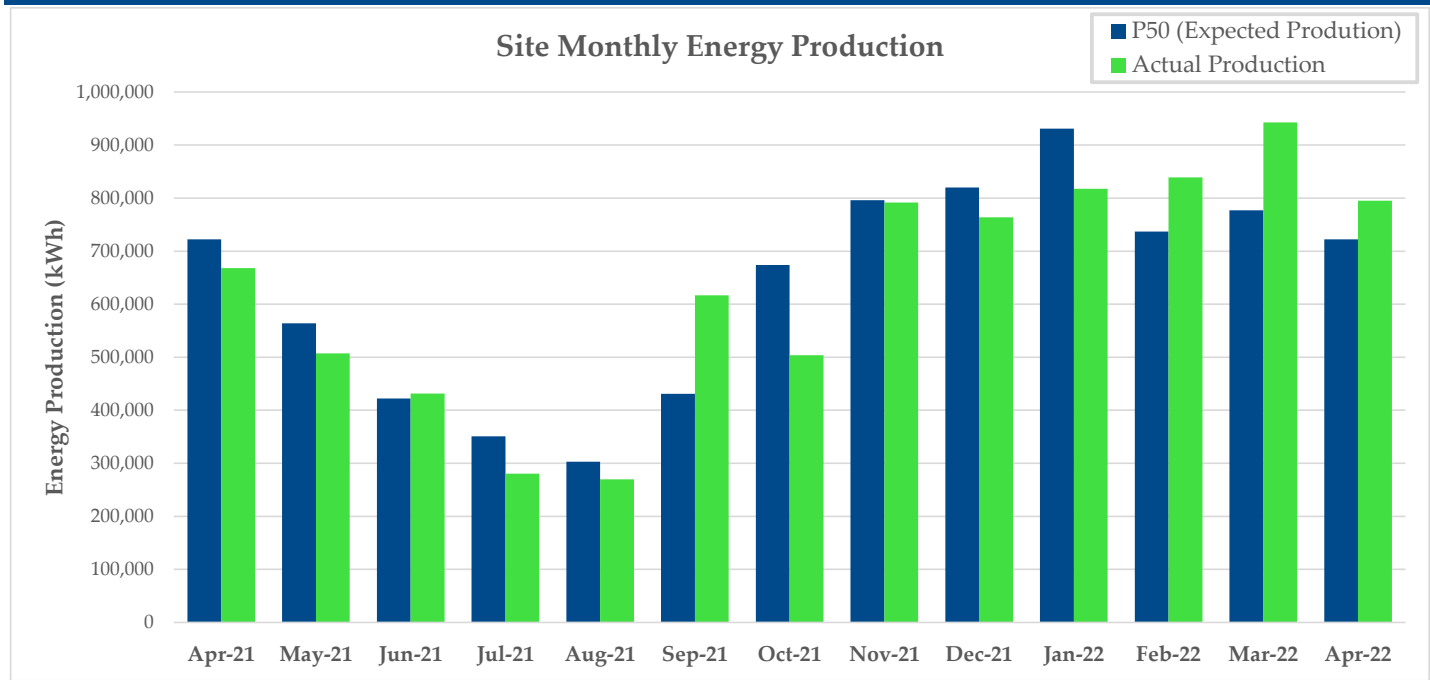

Monthly Report

April-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-22	Goldwind 4 Year Maintenance	~15	V1
October-22	Goldwind 4 Year Maintenance	~15	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/8/2022-4/9/2022	Turbine Fault	Unplanned	20.52	V2
4/29/2022	Goldwind 3.5 Year Maintenance	Planned	2.50	V1
4/29/2022	Goldwind 3.5 Year Maintenance	Planned	3.63	V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	98.72%
V2	97.12%	99.27%
Avg	98.56%	99.00%

Downtime (hr)	This Month	Year To Date
V1	2.50	143.07
V2	24.36	128.30
Total	26.86	271.37

G. Billed Data

Meter Reading (Date/Time)	5/1/2022 12:00 AM
Meter To Date Produced	26,854,117 kWh
Meter To Date Consumed	66,078 kWh
Last Reading Produced	26,083,603 kWh
Last Reading Consumed	65,307 kWh
Billed kWh	769,743 kWh
Next Meter Reading	6/1/2022 12:00 AM

H. Report Notes and Comments
