



BALL CORPORATION - ZEPHYR WIND PROJECT 1.0

North Findlay Wind Campus, Findlay, OH

Monthly Report

April-2022




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Apr-21	1,359,000	930,702	327,011	316,411	287,280
May-21	856,000	723,486	251,234	238,571	233,681
Jun-21	599,000	668,103	237,234	223,304	207,565
Jul-21	549,000	406,084	144,149	134,124	127,811
Aug-21	559,000	401,761	142,351	132,538	126,872
Sep-21	482,000	926,810	324,892	307,203	294,715
Oct-21	916,000	726,057	254,792	242,990	228,275
Nov-21	1,203,000	1,191,103	418,962	401,518	370,623
Dec-21	1,475,000	1,163,071	403,095	393,380	366,596
Jan-22	1,260,000	1,252,569	435,949	420,553	396,067
Feb-22	1,310,000	1,354,099	469,778	464,716	419,606
Mar-22	1,140,000	1,356,275	481,385	457,802	417,088
Apr-22	1,359,000	1,267,232	435,279	427,907	404,046
Production 2022 (ytd) (kWh)	5,069,000	5,230,175	1,822,391	1,770,978	1,636,807
Total Production (LTM) (kWh)	11,708,000	11,436,650	3,999,100	3,844,606	3,592,945
Capacity Factor (LTM)	29.01%				

B. Site Energy Production Graph

April-2022

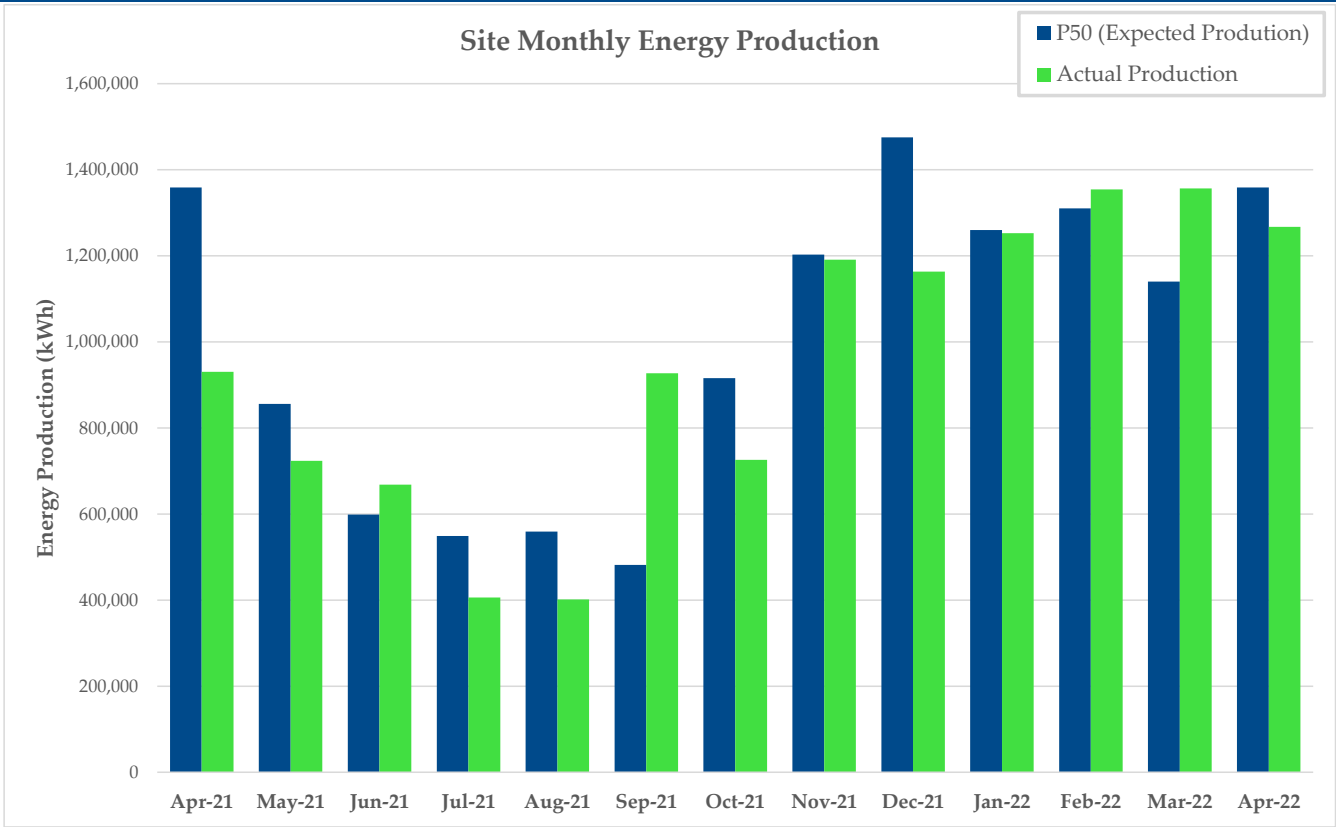

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2022	Goldwind 6.5 Year Maintenance	~8	Z1
October-2022	Goldwind 6.5 Year Maintenance	~8	Z2
October-2022	Goldwind 6.5 Year Maintenance	~8	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/1/2022	Turbine Fault	Unplanned	8.89	Z3
4/5/2022	Goldwind 6 Year Maintenance	Planned	3.33	Z3
4/12/2022	Goldwind 6 Year Maintenance	Planned	2.77	Z2
4/20/2022	Goldwind 6 Year Maintenance	Planned	2.91	Z1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z1	100.00%	99.90%
Z2	100.00%	99.89%
Z3	98.77%	99.68%
Avg	99.59%	99.83%

Downtime (hr)	This Month	Year To Date
Z1	4.74	49.05
Z2	4.61	49.77
Z3	14.06	153.27
Total	23.41	252.09

G. Billed Data

Meter Reading (Date/Time)	4/20/2022 12:00 AM
Ball 1.0 Production (This Period)	1,414,562 kWh
Ball 1.0 Consumption (This Period)	366 kWh
Billed kWh	1,414,196 kWh
Next Meter Reading	5/19/2022 12:00 AM

H. Report Notes and Comments

* February 2022 production includes estimates due to a SCADA server error.
**April 2022 production includes estimated due to a SCADA server error.
