




BALL CORPORATION - ZEPHYR WIND PROJECT 2.0
North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Apr-21	1,116,000	941,559	301,517	305,193	334,849
May-21	876,000	755,823	246,357	249,062	260,404
Jun-21	637,000	667,180	226,175	213,521	227,484
Jul-21	518,000	423,089	144,295	141,912	136,882
Aug-21	448,000	407,609	139,023	132,947	135,639
Sep-21	617,000	957,074	321,730	316,478	318,866
Oct-21	956,000	739,181	243,855	238,641	256,685
Nov-21	1,107,000	1,150,429	384,301	366,844	399,284
Dec-21	1,098,000	1,141,220	374,435	374,888	391,897
Jan-22	1,251,000	1,253,751	420,362	406,883	426,506
Feb-22	1,044,000	1,306,639	438,679	422,217	445,743
Mar-22	1,119,000	1,335,480	443,031	438,839	453,610
Apr-22	1,116,000	1,145,744	373,811	368,393	403,540
Production 2022 (ytd) (kWh)	4,530,000	5,041,614	1,675,883	1,636,332	1,729,399
Total Production (kWh) (LTM)	10,787,000	11,283,219	3,756,054	3,670,625	3,856,540
Capacity Factor (LTM)	28.62%				

B. Site Energy Production Graph

April-2022

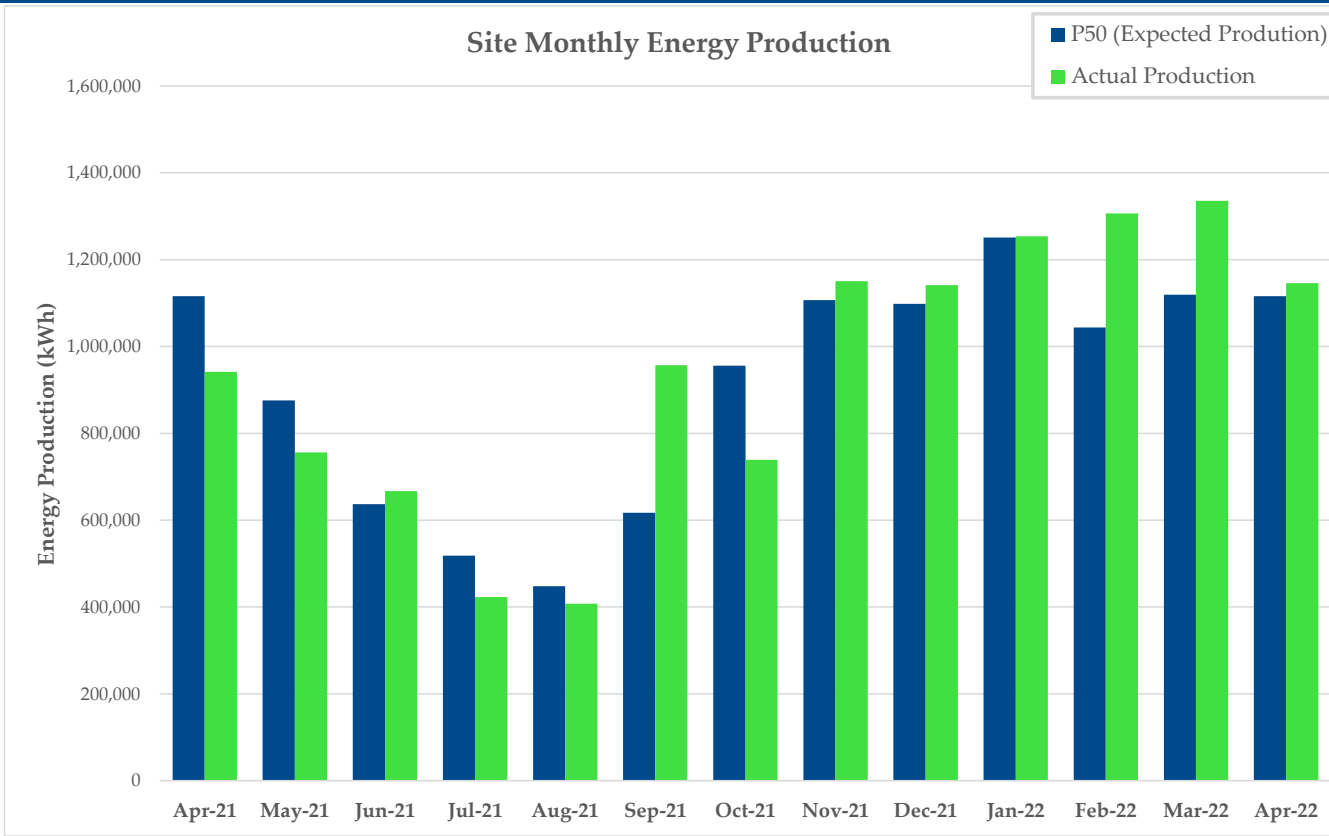

Monthly Report
April-2022



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2022	Goldwind 2 Year Maintenance	~15	Z4
September-2022	Goldwind 2 Year Maintenance	~15	Z5
September-2022	Goldwind 2 Year Maintenance	~15	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/1/2022	Weather shutdown	Unplanned	7.12	Z4,Z5,Z6
4/16-18/2022	Turbine Fault	Unplanned	38.65	Z5
4/22/2022	Goldwind 1.5 Year Maintenance	Planned	0.62	Z4,Z5,Z6

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z4	100.00%	99.98%
Z5	94.63%	97.14%
Z6	100.00%	99.78%
Avg	98.21%	98.97%

Downtime (hr)	This Month	Year To Date
Z4	8.06	130.29
Z5	46.71	198.81
Z6	8.06	145.78
Total	62.83	474.88

G. Billed Data

Meter Reading (Date/Time)	3/19/2022 12:00 AM
Ball 2.0 Production (This Period)	1,106,231 kWh
Ball 2.0 Consumption (This Period)	2,674 kWh
Billed kWh	1,103,557 kWh
Next Meter Reading	4/20/2022 12:00 AM

H. Report Notes and Comments

*March 2022 production includes estimates due to a SCADA server error.
**April 2022 Production and Availability numbers are pending review and will be confirmed in the May 2022 report.
