


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
May-21	601,000	509,680	262,275	247,405
Jun-21	425,000	479,735	244,261	235,474
Jul-21	390,000	298,836	152,425	146,411
Aug-21	399,000	297,535	152,628	144,907
Sep-21	337,000	665,033	337,170	327,863
Oct-21	637,000	518,984	262,835	256,149
Nov-21	834,000	849,882	425,765	424,117
Dec-21	1,015,000	821,418	415,630	405,788
Jan-22	875,000	857,334	429,640	427,694
Feb-22	917,000	861,229	467,908	393,321
Mar-22	802,000	991,707	500,106	491,601
Apr-22	951,000	795,380	402,642	392,738
May-22	601,000	614,219	307,353	306,866
Production 2022 (ytd) (kWh)	4,146,000	4,119,869	2,107,649	2,012,220
Total Production (kWh) (LTM)	8,183,000	8,051,292	4,098,363	3,952,929
Capacity Factor (LTM)	30.64%			

B. Site Energy Production Graph

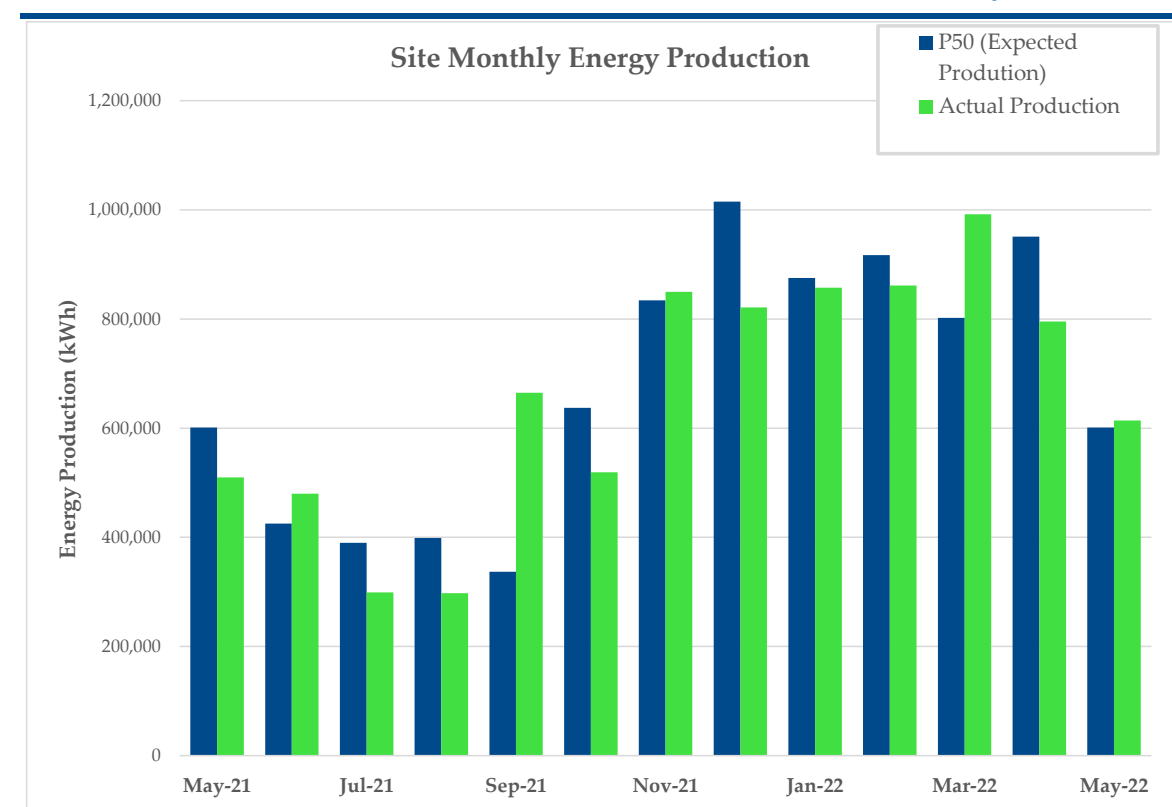

Monthly Report

May-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2022	Goldwind 7 Year Maintenance	~15	W1
November-2022	Goldwind 7 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/2/2022	Goldwind 6.5 Year Maintenance	Planned	3.07	W1
5/2/2022	Goldwind 6.5 Year Maintenance	Planned	2.63	W2
5/13/2022	Goldwind 6.5 Year Maintenance	Planned	0.76	W1
5/13/2022	Goldwind 6.5 Year Maintenance	Planned	0.75	W2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.85%	99.34%
W2	100.00%	99.99%
Avg	99.92%	99.67%

Downtime (hr)	This Month	Year To Date
W1	8.67	135.33
W2	5.88	176.06
Total	14.55	311.39

G. Billed Data

Meter Reading (Date/Time)	5/29/2022 12:00 AM
Meter To Date Produced	49,518,798 kWh
Meter To Date Consumed	96,355 kWh
Last Reading Produced	48,948,095 kWh
Last Reading Consumed	95,687 kWh
Billed kWh	570,035 kWh
Next Meter Reading	6/29/2022 12:00 AM

H. Report Notes and Comments
