


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	W1	W2	W3
May-21	927,000	646,261	217,827	210,837	217,597
Jun-21	634,000	571,998	186,211	188,627	197,160
Jul-21	527,000	318,063	107,885	100,155	110,023
Aug-21	449,000	324,019	109,256	105,233	109,530
Sep-21	610,000	740,131	243,253	241,498	255,380
Oct-21	990,000	693,360	241,616	219,829	231,915
Nov-21	1,123,000	976,482	349,225	311,053	316,204
Dec-21	1,153,000	1,088,213	372,080	354,578	361,555
Jan-22	1,306,000	845,320	315,868	177,718	351,734
Feb-22	1,137,000	1,182,964	407,437	382,881	392,646
Mar-22	1,134,000	1,341,048	444,624	443,527	452,897
Apr-22	1,176,000	1,079,664	374,895	351,597	353,172
May-22	927,000	861,830	293,507	271,102	297,221
Production 2022 (ytd) (kWh)	5,680,000	5,310,826	1,836,331	1,626,825	1,847,670
Total Production (kWh) (LTM)	11,166,000	10,023,092	3,445,857	3,147,798	3,429,437
Capacity Factor (LTM)	25.43%				

B. Site Energy Production Graph

May-2022

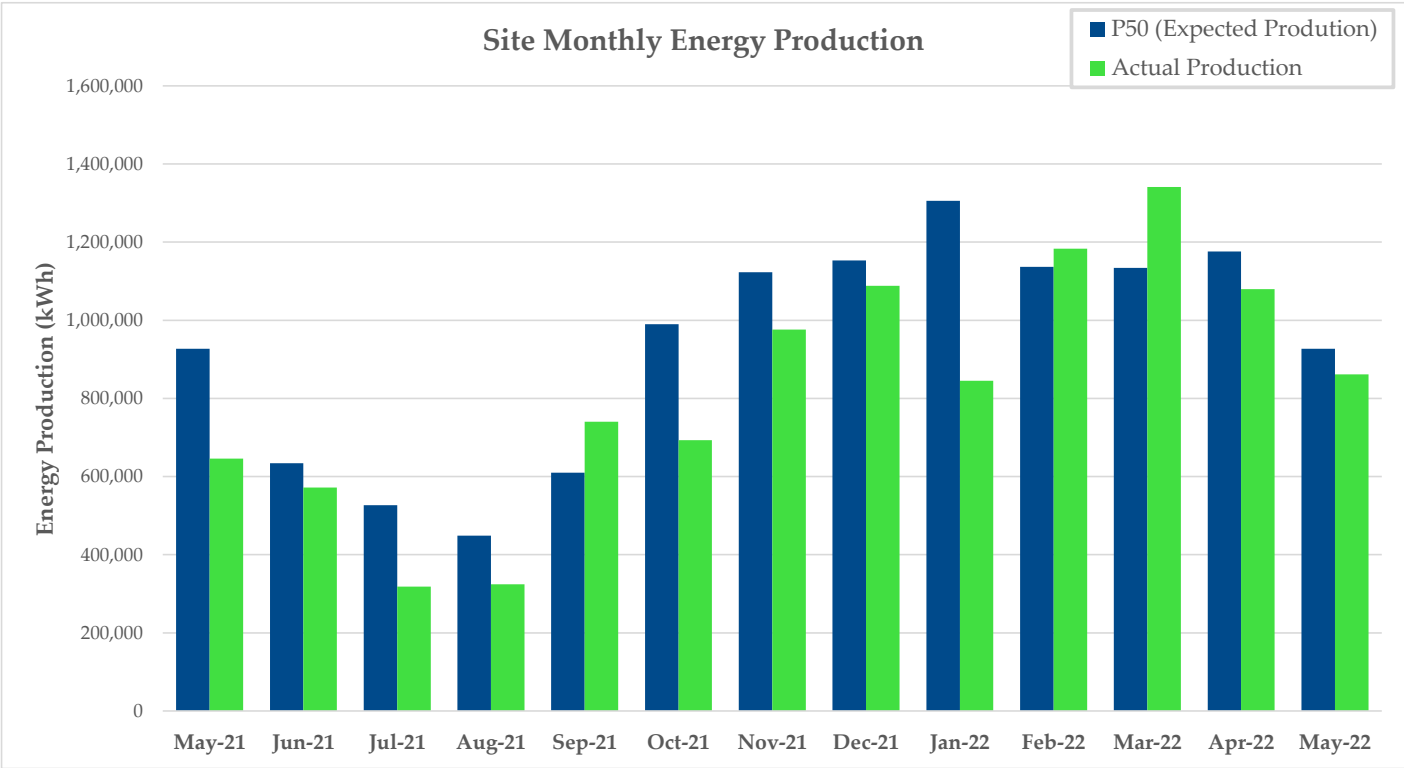

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2022	Goldwind 5 Year Maintenance	~15	W1
October-2022	Goldwind 5 Year Maintenance	~15	W2
October-2022	Goldwind 5 Year Maintenance	~15	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/7/2022	Turbine Fault	Unplanned	9.84	W2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.76%	99.38%
W2	98.68%	99.60%
W3	100.00%	99.95%
Avg	99.48%	99.64%

Downtime (hr)	This Month	Year To Date
W1	8.70	251.81
W2	17.31	463.87
W3	7.89	236.76
Total	33.90	952.44

G. Billed Data

Meter Reading (Date/Time)	5/21/2022 12:00 AM
Meter To Date Produced	42,697,719 kWh
Meter To Date Consumed	125,173 kWh
Last Reading Produced	41,859,115 kWh
Last Reading Consumed	123,504 kWh
Billed kWh	836,935 kWh
Next Meter Reading	6/21/2022 12:00 AM

H. Report Notes and Comments
