


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	L1	L2	L3
Aug-21	534,000	418,734	143,423	142,983	132,328
Sep-21	736,000	984,373	335,478	342,450	306,445
Oct-21	1,131,000	871,887	297,865	295,436	278,586
Nov-21	1,281,000	1,196,514	350,141	425,981	420,392
Dec-21	1,263,000	1,233,907	413,245	410,712	409,950
Jan-22	1,433,000	1,230,205	416,242	405,918	408,045
Feb-22	1,213,000	1,345,539	450,556	445,316	449,667
Mar-22	1,339,000	1,494,185	500,969	503,338	489,878
Apr-22	1,327,000	1,412,962	466,654	475,314	470,994
May-22	1,052,000	1,077,013	373,367	344,704	358,942
Jun-22	751,000	648,158	241,123	200,574	206,461
Jul-22	609,000	601,624	214,570	198,293	188,761
Aug-22	534,000	495,062	174,285	161,531	159,246
Production 2022 (ytd) (kWh)	8,258,000	8,304,748	2,837,766	2,734,988	2,731,994
Total Production (LTM) (kWh)	12,669,000	12,591,429	4,234,495	4,209,567	4,147,367
Capacity Factor (LTM)	31.94%				

B. Site Energy Production Graph

August-2022

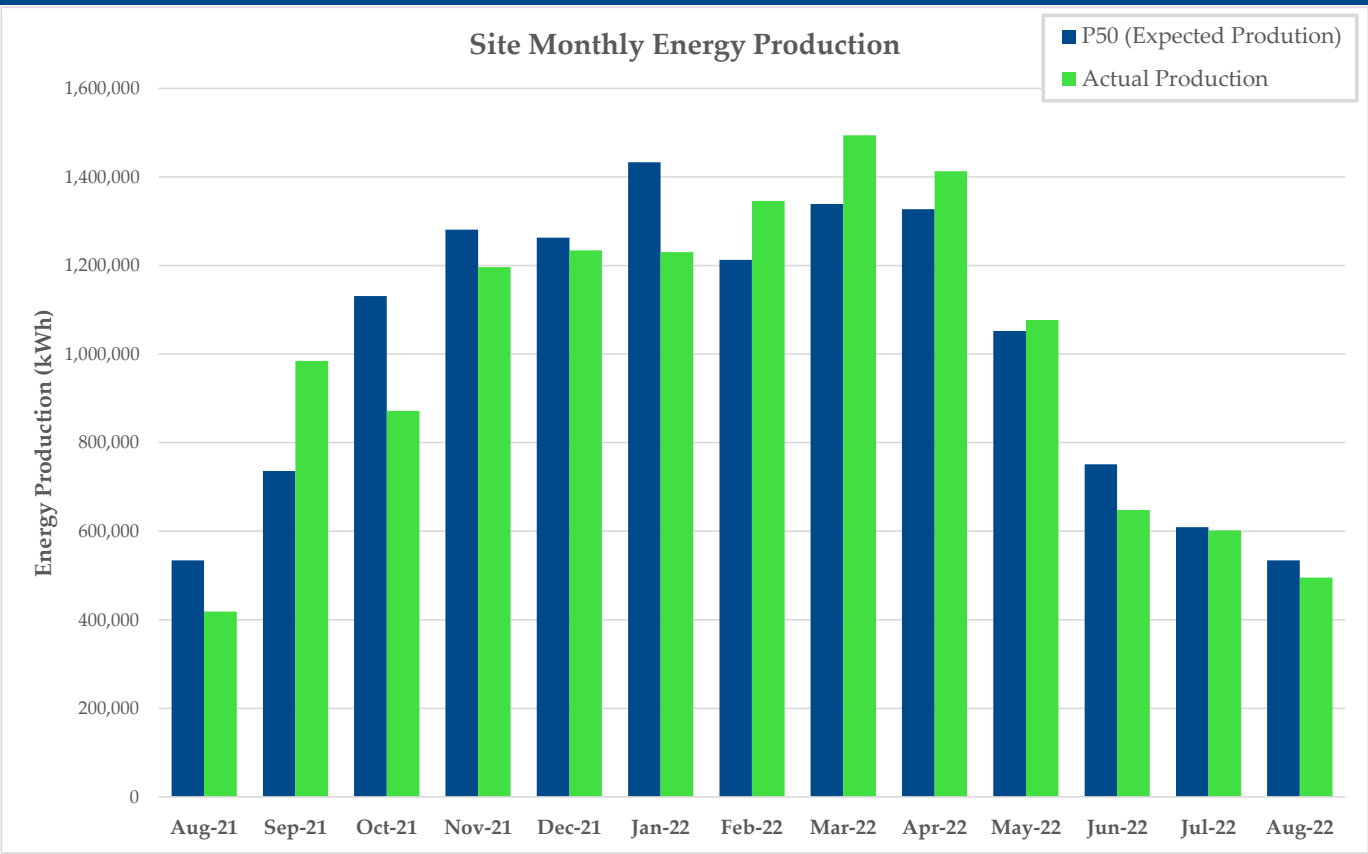

Monthly Report
August-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2022	Goldwind 2 Year Maintenance	~15	L1
September-2022	Goldwind 2 Year Maintenance	~15	L2
September-2022	Goldwind 2 Year Maintenance	~15	L3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
8/29/2022-8/30/2022	Turbine Fault	Unplanned	17.68	L2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
L1	100.00%	98.41%
L2	97.18%	98.28%
L3	100.00%	99.85%
Avg	99.06%	98.85%

Downtime (hr)	This Month	Year To Date
L1	1.87	151.19
L2	22.82	356.24
L3	1.87	169.39
Total	26.56	676.82

G. Billed Data

Meter Reading (Date/Time)	8/25/2022 12:00 AM
Meter To Date Produced	23,899,060 kWh
Meter To Date Consumed	76,609 kWh
Last Reading Produced	23,508,700 kWh
Last Reading Consumed	70,893 kWh
Billed kWh	384,644 kWh
Next Meter Reading	9/24/2022 12:00 AM

H. Report Notes and Comments
