



BALL CORPORATION - ZEPHYR WIND PROJECT 2.0


North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Sep-21	617,000	957,074	321,730	316,478	318,866
Oct-21	956,000	739,181	243,855	238,641	256,685
Nov-21	1,107,000	1,150,429	384,301	366,844	399,284
Dec-21	1,098,000	1,141,220	374,435	374,888	391,897
Jan-22	1,251,000	1,253,751	420,362	406,883	426,506
Feb-22	1,044,000	1,306,639	438,679	422,217	445,743
Mar-22	1,119,000	1,335,480	443,031	438,839	453,610
Apr-22	1,116,000	1,145,744	373,811	368,393	403,540
May-22	876,000	984,712	298,460	333,446	352,806
Jun-22	637,000	601,888	194,009	193,281	214,598
Jul-22	518,000	586,264	192,973	189,924	203,367
Aug-22	448,000	459,360	146,939	148,700	163,721
Sep-22	617,000	570,590	183,735	188,215	198,640
Production 2022 (ytd) (kWh)	7,626,000	8,244,428	2,691,999	2,689,898	2,862,531
Total Production (kWh) (LTM)	10,787,000	11,275,258	3,694,590	3,670,271	3,910,397
Capacity Factor (LTM)	28.60%				

B. Site Energy Production Graph

September-2022

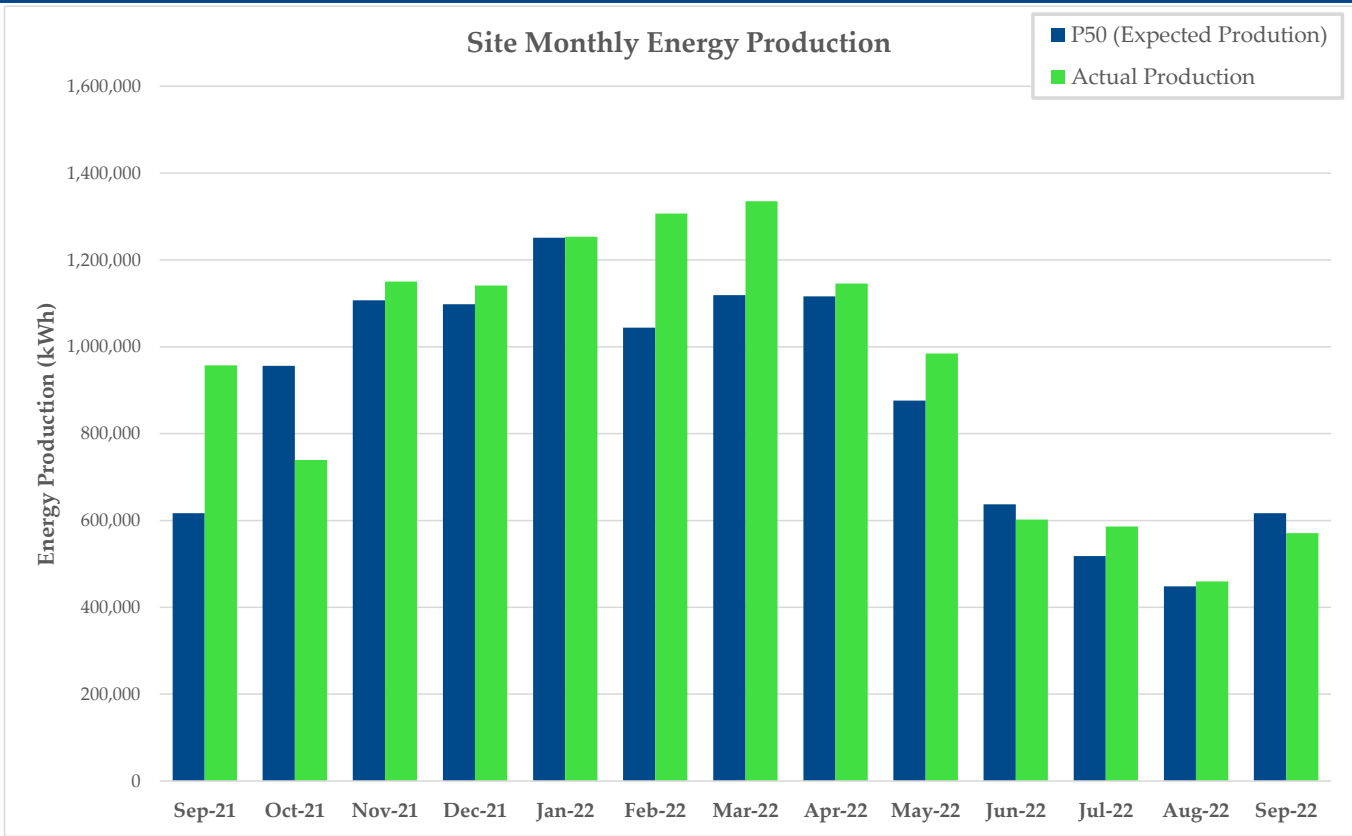

Monthly Report

September-2022



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2023	Goldwind 2.5 Year Maintenance	~8	Z4
April-2023	Goldwind 2.5 Year Maintenance	~8	Z5
April-2023	Goldwind 2.5 Year Maintenance	~8	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
9/9/2022	Customer Maintenance	Unplanned	6.73	Z4, Z5, Z6
9/13/2022	Goldwind 2 Year Maintenance	Planned	6.90	Z4
9/13/2022-9/14/2022	Goldwind 2 Year Maintenance	Planned	5.25	Z5
9/26/2022	Goldwind 2 Year Maintenance	Planned	1.12	Z5
9/16/2022	Goldwind 2 Year Maintenance	Planned	5.05	Z6

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z4	100.00%	99.99%
Z5	100.00%	98.45%
Z6	100.00%	99.90%
Avg	100.00%	99.45%

Downtime (hr)	This Month	Year To Date
Z4	16.09	160.08
Z5	17.63	248.72
Z6	16.22	175.12
Total	49.94	583.92

G. Billed Data

Meter Reading (Date/Time)	9/17/2022 12:00 AM
Ball 2.0 Production (This Period)	351,410 kWh
Ball 2.0 Consumption (This Period)	3,790 kWh
Billed kWh	347,620 kWh
Next Meter Reading	10/18/2022 12:00 AM

H. Report Notes and Comments

*March 2022 production includes estimates due to a SCADA server error.
