


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	W1	W2	W3
Sep-21	610,000	740,131	243,253	241,498	255,380
Oct-21	990,000	693,360	241,616	219,829	231,915
Nov-21	1,123,000	976,482	349,225	311,053	316,204
Dec-21	1,153,000	1,088,213	372,080	354,578	361,555
Jan-22	1,306,000	845,320	315,868	177,718	351,734
Feb-22	1,137,000	1,182,964	407,437	382,881	392,646
Mar-22	1,134,000	1,341,048	444,624	443,527	452,897
Apr-22	1,176,000	1,079,664	374,895	351,597	353,172
May-22	927,000	861,830	293,507	271,102	297,221
Jun-22	634,000	512,159	167,043	167,623	177,493
Jul-22	527,000	418,863	139,334	134,326	145,203
Aug-22	449,000	347,940	115,055	112,651	120,234
Sep-22	610,000	457,923	158,634	147,583	151,706
Production 2022 (ytd) (kWh)	7,900,000	7,047,711	2,416,397	2,189,008	2,442,306
Total Production (kWh) (LTM)	11,166,000	9,805,766	3,379,318	3,074,468	3,351,980
Capacity Factor (LTM)	24.88%				

B. Site Energy Production Graph

September-2022

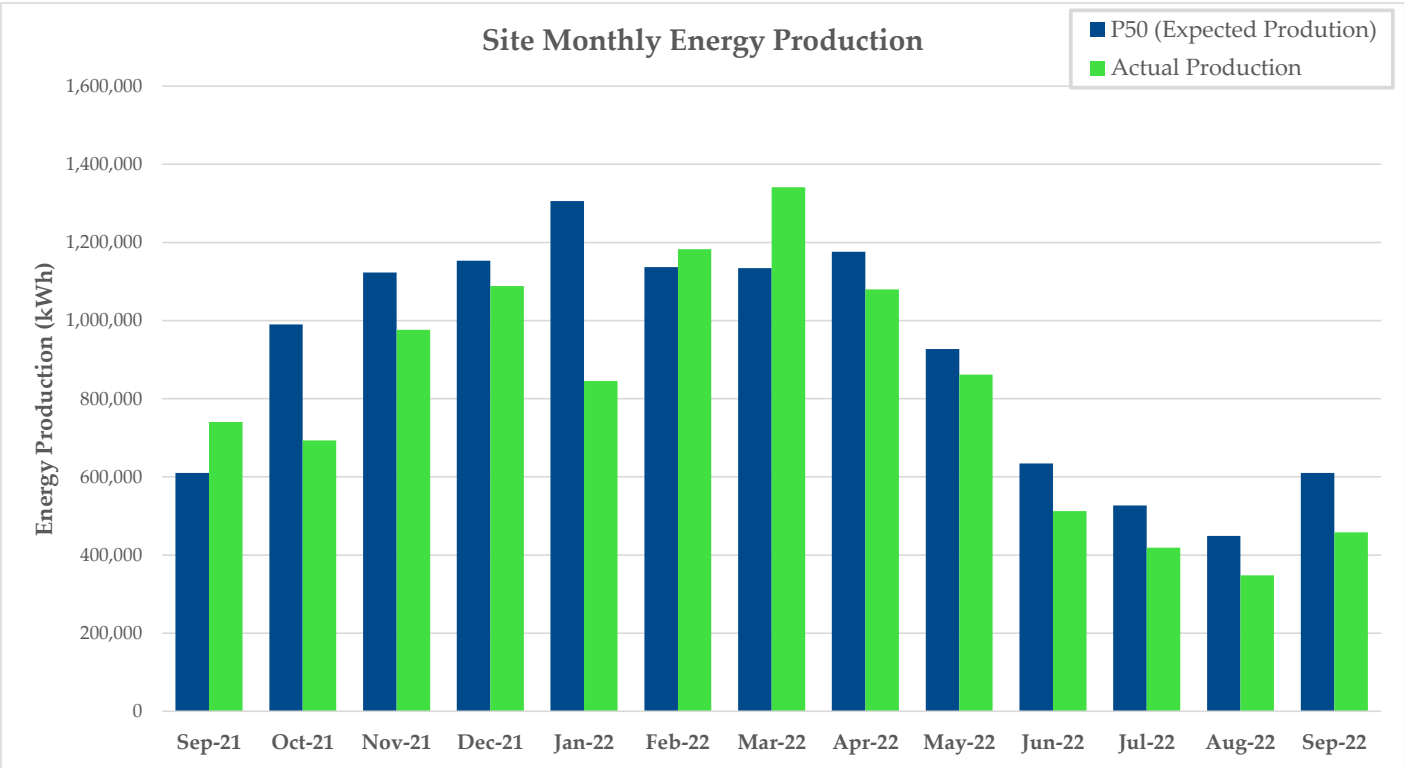

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2022	Goldwind 5 Year Maintenance	~15	W1
October-2022	Goldwind 5 Year Maintenance	~15	W2
October-2022	Goldwind 5 Year Maintenance	~15	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
9/29/2022-9/30/2022	Turbine Fault	Unplanned	28.96	W3

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.48%	99.07%
W2	100.00%	99.75%
W3	95.98%	99.51%
Avg	98.48%	99.44%

Downtime (hr)	This Month	Year To Date
W1	4.96	308.36
W2	0.75	482.38
W3	28.96	282.42
Total	34.67	1073.16

G. Billed Data

Meter Reading (Date/Time)	9/21/2022 12:00 AM
Meter To Date Produced	44,431,620 kWh
Meter To Date Consumed	138,633 kWh
Last Reading Produced	44,128,595 kWh
Last Reading Consumed	134,741 kWh
Billed kWh	299,133 kWh
Next Meter Reading	10/21/2022 12:00 AM

H. Report Notes and Comments
