



BALL CORPORATION - ZEPHYR WIND PROJECT 1.0

North Findlay Wind Campus, Findlay, OH

Monthly Report

October-2022




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Oct-21	916,000	726,057	254,792	242,990	228,275
Nov-21	1,203,000	1,191,103	418,962	401,518	370,623
Dec-21	1,475,000	1,163,071	403,095	393,380	366,596
Jan-22	1,260,000	1,252,569	435,949	420,553	396,067
Feb-22	1,310,000	1,354,099	469,778	464,716	419,606
Mar-22	1,140,000	1,356,275	481,385	457,802	417,088
Apr-22	1,359,000	1,267,232	435,279	427,907	404,046
May-22	856,000	899,215	304,468	311,170	283,577
Jun-22	599,000	572,841	206,791	192,580	173,470
Jul-22	549,000	552,201	195,618	183,810	172,773
Aug-22	559,000	437,708	156,192	146,109	135,407
Sep-22	482,000	520,541	181,453	173,959	165,128
Oct-22	916,000	1,182,514	413,378	402,621	366,515
Production 2022 (ytd) (kWh)	9,030,000	9,395,195	3,280,291	3,181,227	2,933,677
Total Production (LTM) (kWh)	11,708,000	11,749,369	4,102,348	3,976,125	3,670,896
Capacity Factor (LTM)	29.81%				

B. Site Energy Production Graph

October-2022

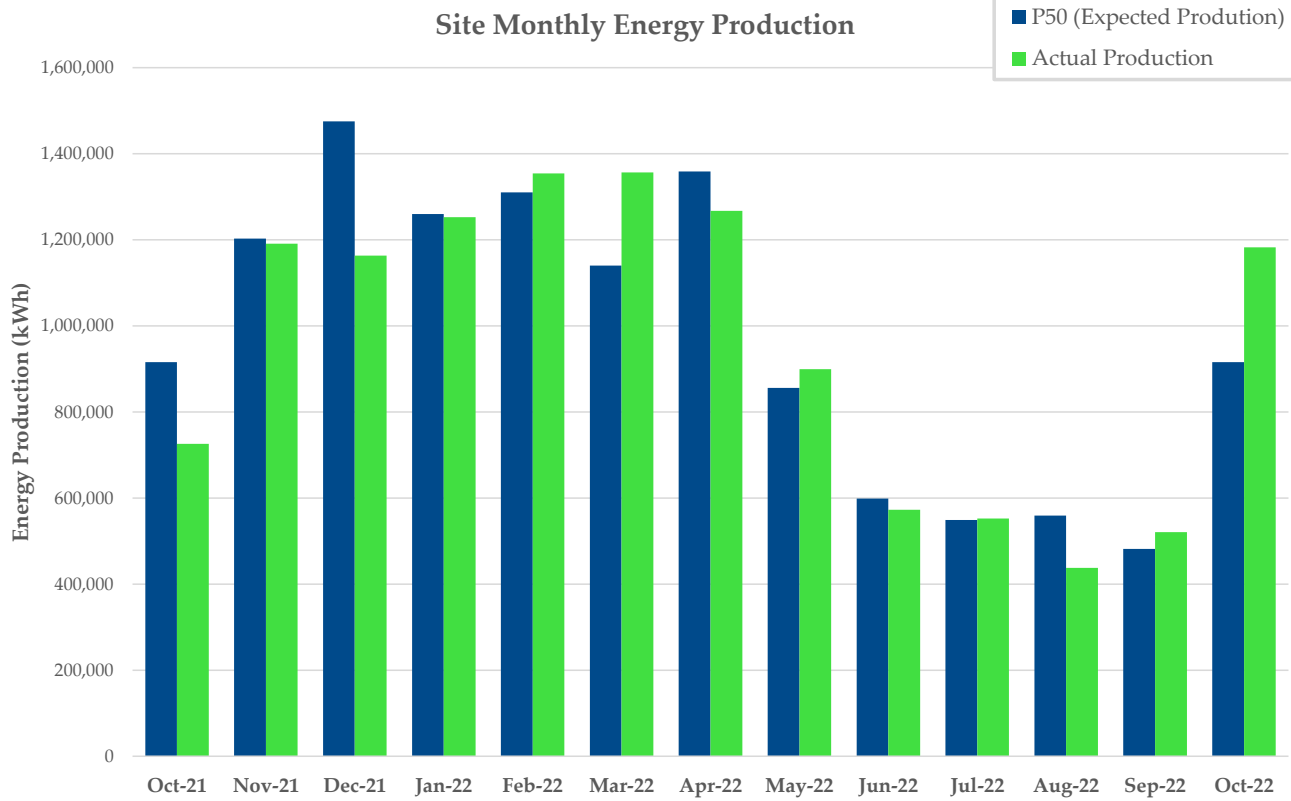

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2023	Goldwind 7 Year Maintenance	~15	Z1
April-2023	Goldwind 7 Year Maintenance	~15	Z2
April-2023	Goldwind 7 Year Maintenance	~15	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/20/2022	Goldwind 6.5 Year Maintenance	Planned	3.25	Z1
10/21/2022	Goldwind 6.5 Year Maintenance	Planned	3.18	Z2
10/25/2022	Goldwind 6.5 Year Maintenance	Planned	3.65	Z3

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z1	100.00%	99.92%
Z2	100.00%	99.94%
Z3	100.00%	99.86%
Avg	100.00%	99.90%

Downtime (hr)	This Month	Year To Date
Z1	3.25	71.43
Z2	3.18	69.03
Z3	3.65	172.83
Total	10.08	313.29

G. Billed Data

Meter Reading (Date/Time)	10/18/2022 12:00 AM
Ball 1.0 Production (This Period)	1,047,328 kWh
Ball 1.0 Consumption (This Period)	170 kWh
Billed kWh	1,047,158 kWh
Next Meter Reading	11/16/2022 12:00 AM

H. Report Notes and Comments

* February 2022 production includes estimates due to a SCADA server error.

**April 2022 production includes estimated due to a SCADA server error.

***September 2022 production includes estimates due to a SCADA server error.
