


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Oct-21	637,000	518,984	262,835	256,149
Nov-21	834,000	849,882	425,765	424,117
Dec-21	1,015,000	821,418	415,630	405,788
Jan-22	875,000	857,334	429,640	427,694
Feb-22	917,000	861,229	467,908	393,321
Mar-22	802,000	991,707	500,106	491,601
Apr-22	951,000	795,380	402,642	392,738
May-22	601,000	614,219	307,353	306,866
Jun-22	425,000	413,887	205,685	208,202
Jul-22	390,000	405,644	204,608	201,036
Aug-22	399,000	316,041	159,653	156,388
Sep-22	337,000	370,915	189,397	181,518
Oct-22	637,000	822,082	414,170	407,912
Production 2022 (ytd) (kWh)	6,334,000	6,448,438	3,281,162	3,167,276
Total Production (kWh) (LTM)	8,183,000	8,119,738	4,122,557	3,997,181
Capacity Factor (LTM)	30.90%			

B. Site Energy Production Graph

October-2022

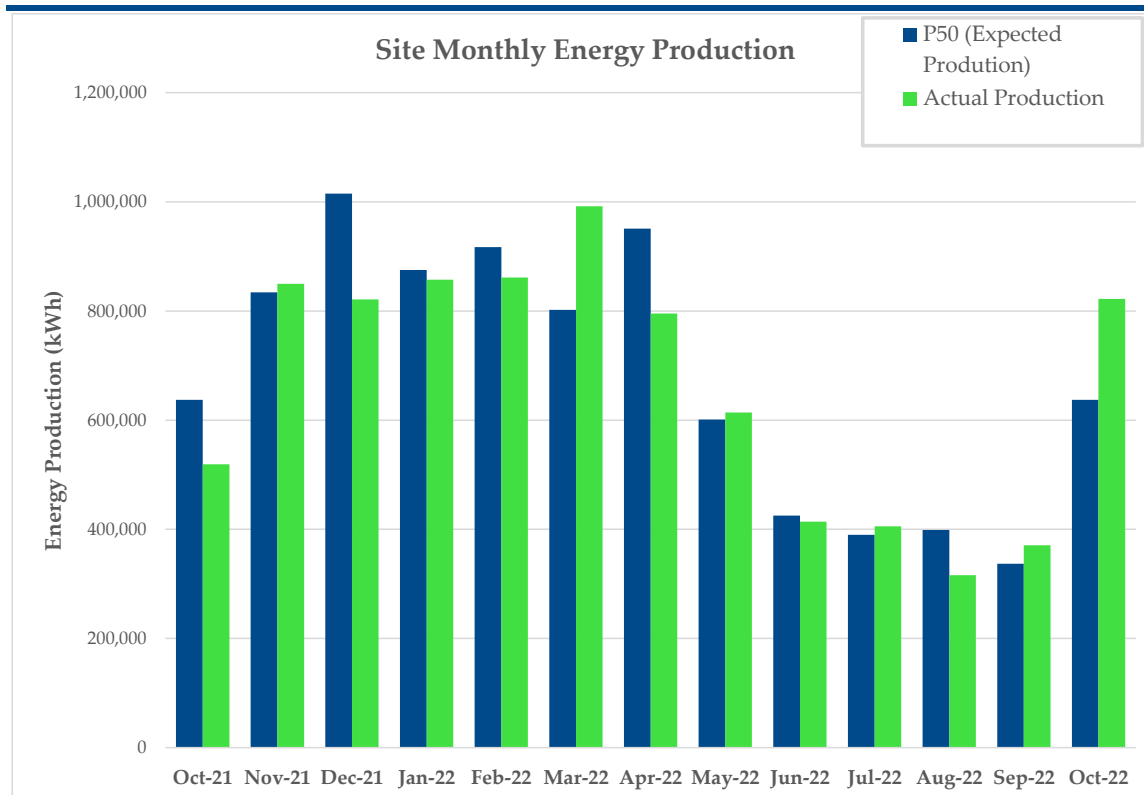

Monthly Report

October-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2022	Goldwind 7 Year Maintenance	~15	W1
November-2022	Goldwind 7 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/31/2022	Goldwind 7 Year Maintenance	Planned	5.58	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	98.95%
W2	100.00%	99.94%
Avg	100.00%	99.45%

Downtime (hr)	This Month	Year To Date
W1	5.58	245.10
W2	2.31	230.13
Total	7.89	475.23

G. Billed Data

Meter Reading (Date/Time)	10/29/2022 12:00 AM
Meter To Date Produced	51,874,155 kWh
Meter To Date Consumed	102,835 kWh
Last Reading Produced	51,054,437 kWh
Last Reading Consumed	102,480 kWh
Billed kWh	819,363 kWh
Next Meter Reading	11/29/2022 12:00 AM

H. Report Notes and Comments
