


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Oct-21	674,000	503,743	250,852	252,891
Nov-21	796,000	791,404	397,996	393,408
Dec-21	820,000	763,656	384,433	379,223
Jan-22	931,000	817,296	405,482	411,814
Feb-22	737,000	838,853	421,431	417,422
Mar-22	777,000	942,768	455,809	486,959
Apr-22	722,000	794,963	403,811	391,152
May-22	564,000	648,467	329,704	318,763
Jun-22	422,000	414,874	202,214	212,660
Jul-22	351,000	385,489	190,281	195,208
Aug-22	303,000	297,191	147,920	149,271
Sep-22	431,000	383,178	188,508	194,670
Oct-22	674,000	770,712	390,964	379,748
Production 2022 (ytd) (kWh)	5,912,000	6,293,791	3,136,124	3,157,667
Total Production (LTM) (kWh)	7,528,000	7,848,851	3,918,553	3,930,298
Capacity Factor (LTM)	29.87%			

B. Site Energy Production Graph

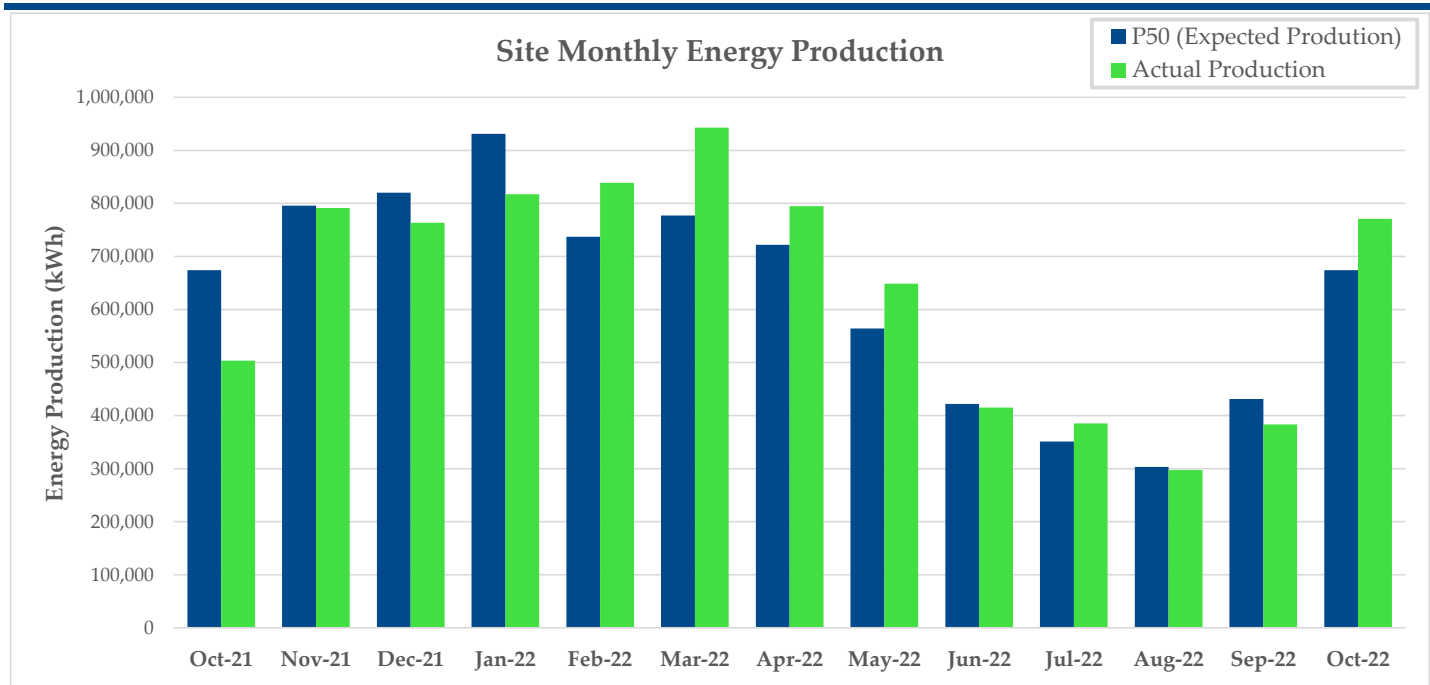

Monthly Report

October-2022



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2022	Goldwind 4 Year Maintenance	~15	V1
November-2022	Goldwind 4 Year Maintenance	~15	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	100.00%	99.47%
V2	100.00%	99.67%
Avg	100.00%	99.57%

Downtime (hr)	This Month	Year To Date
V1	-	159.78
V2	-	146.64
Total	-	306.42

G. Billed Data

Meter Reading (Date/Time)	11/1/2022 12:00 AM
Meter To Date Produced	29,663,474 kWh
Meter To Date Consumed	75,807 kWh
Last Reading Produced	28,915,422 kWh
Last Reading Consumed	74,990 kWh
Billed kWh	747,235 kWh
Next Meter Reading	12/1/2022 12:00 AM

H. Report Notes and Comments
