


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Nov-21	834,000	849,882	425,765	424,117
Dec-21	1,015,000	821,418	415,630	405,788
Jan-22	875,000	857,334	429,640	427,694
Feb-22	917,000	861,229	467,908	393,321
Mar-22	802,000	991,707	500,106	491,601
Apr-22	951,000	795,380	402,642	392,738
May-22	601,000	614,219	307,353	306,866
Jun-22	425,000	413,887	205,685	208,202
Jul-22	390,000	405,644	204,608	201,036
Aug-22	399,000	316,041	159,653	156,388
Sep-22	337,000	370,915	189,397	181,518
Oct-22	637,000	822,082	414,170	407,912
Nov-22	834,000	952,177	479,422	472,755
Production 2022 (ytd) (kWh)	7,168,000	7,400,615	3,760,584	3,640,031
Total Production (kWh) (LTM)	8,183,000	8,222,033	4,176,214	4,045,819
Capacity Factor (LTM)	31.29%			

B. Site Energy Production Graph

November-2022

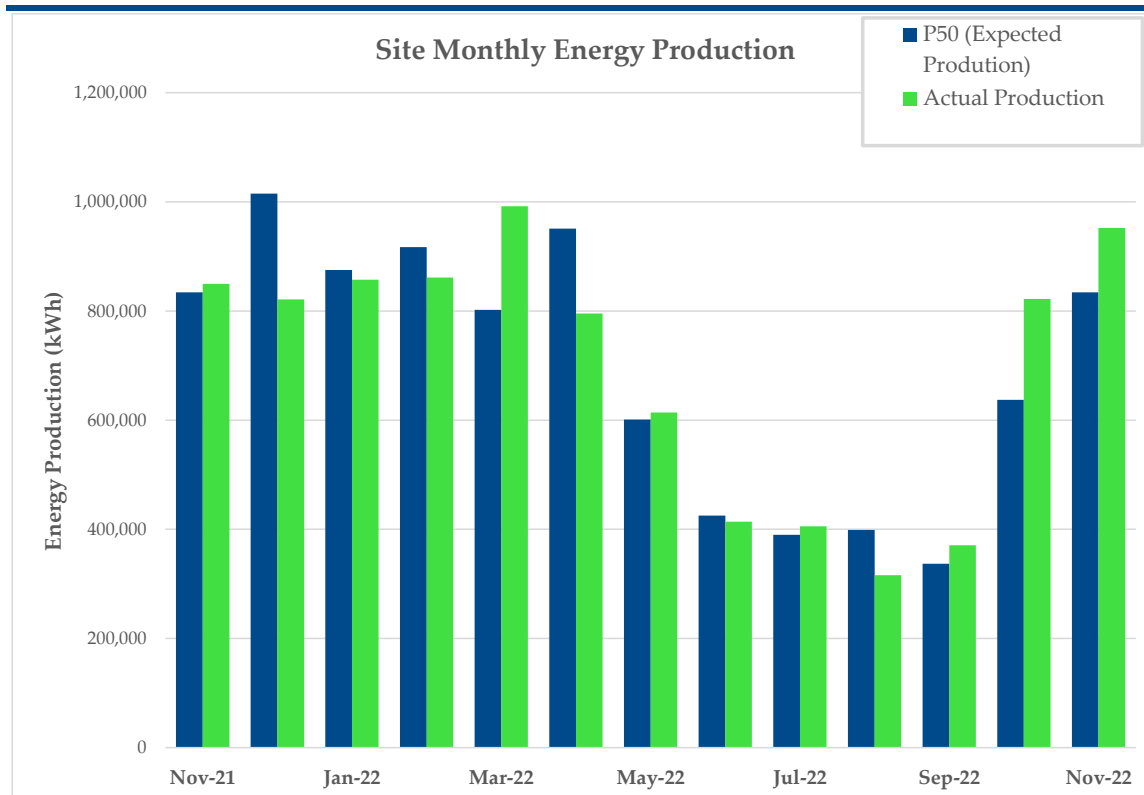

Monthly Report

November-2022

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2023	Goldwind 7.5 Year Maintenance	~8	W1
May-2023	Goldwind 7.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/1/2022	Goldwind 7 Year Maintenance	Planned	4.53	W2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.96%	99.04%
W2	99.99%	99.95%
Avg	99.98%	99.50%

Downtime (hr)	This Month	Year To Date
W1	3.10	248.20
W2	4.60	234.73
Total	7.70	482.93

G. Billed Data

Meter Reading (Date/Time)	11/29/2022 12:00 AM
Meter To Date Produced	52,743,786 kWh
Meter To Date Consumed	103,643 kWh
Last Reading Produced	51,874,155 kWh
Last Reading Consumed	102,835 kWh
Billed kWh	868,823 kWh
Next Meter Reading	12/29/2022 12:00 AM

H. Report Notes and Comments
