

A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Dec-21	1,015,000	821,418	415,630	405,788
Jan-22	875,000	857,334	429,640	427,694
Feb-22	917,000	861,229	467,908	393,321
Mar-22	802,000	991,707	500,106	491,601
Apr-22	951,000	795,380	402,642	392,738
May-22	601,000	614,219	307,353	306,866
Jun-22	425,000	413,887	205,685	208,202
Jul-22	390,000	405,644	204,608	201,036
Aug-22	399,000	316,041	159,653	156,388
Sep-22	337,000	370,915	189,397	181,518
Oct-22	637,000	822,082	414,170	407,912
Nov-22	834,000	952,177	479,422	472,755
Dec-22	1,015,000	920,397	460,812	459,585
Production 2022 (ytd) (kWh)	8,183,000	8,321,012	4,221,396	4,099,616
Total Production (kWh) (LTM)	8,183,000	8,321,012	4,221,396	4,099,616
Capacity Factor (LTM)	31.66%			

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events


Date	Event	Duration (hr)	Turbine
May-2023	Goldwind 7.5 Year Maintenance	~8	W1
May-2023	Goldwind 7.5 Year Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

B. Site Energy Production Graph

December-2022

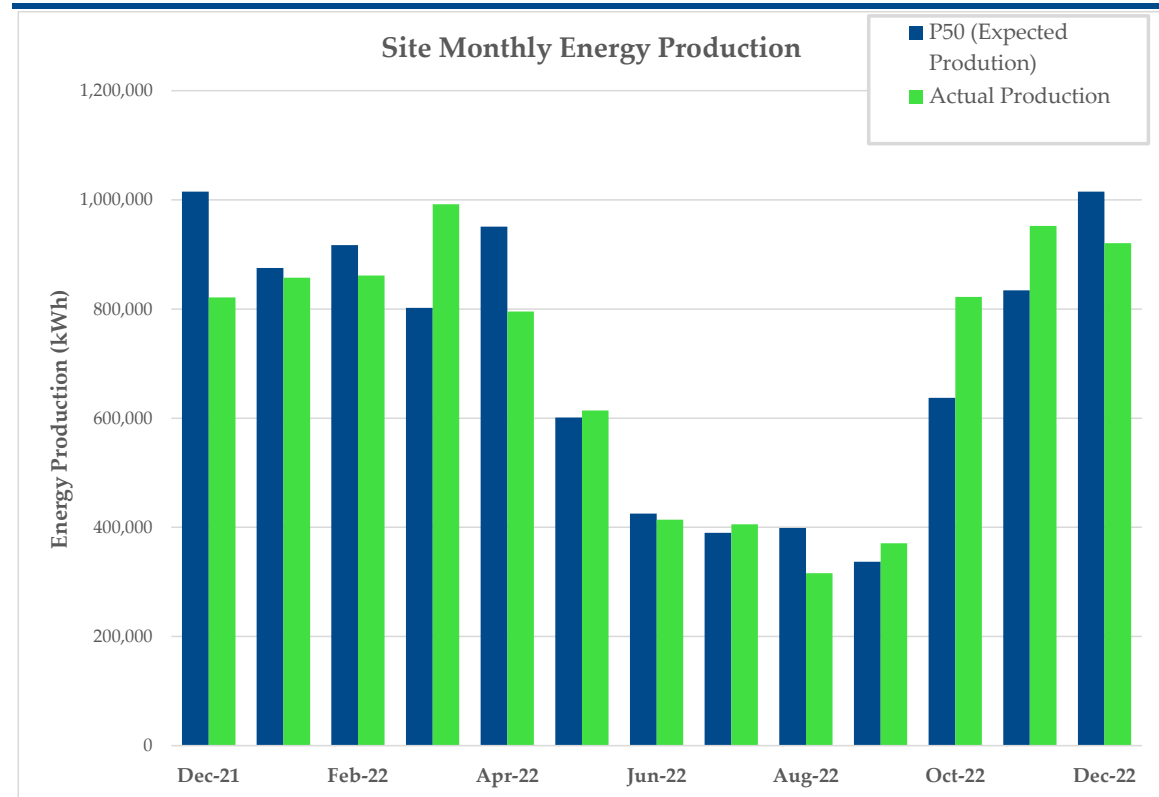

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	99.86%	99.11%
W2	100.00%	99.95%
Avg	99.93%	99.53%

Downtime (hr)	This Month	Year To Date
W1	1.05	249.25
W2		234.73
Total	1.05	483.98

G. Billed Data

Meter Reading (Date/Time)	12/29/2022 12:00 AM
Meter To Date Produced	53,625,493 kWh
Meter To Date Consumed	104,700 kWh
Last Reading Produced	52,743,786 kWh
Last Reading Consumed	103,643 kWh
Billed kWh	880,650 kWh
Next Meter Reading	1/29/2023 12:00 AM

H. Report Notes and Comments
