


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	W1	W2	W3
Dec-21	1,153,000	1,088,213	372,080	354,578	361,555
Jan-22	1,306,000	845,320	315,868	177,718	351,734
Feb-22	1,137,000	1,182,964	407,437	382,881	392,646
Mar-22	1,134,000	1,341,048	444,624	443,527	452,897
Apr-22	1,176,000	1,079,664	374,895	351,597	353,172
May-22	927,000	861,830	293,507	271,102	297,221
Jun-22	634,000	512,159	167,043	167,623	177,493
Jul-22	527,000	418,863	139,334	134,326	145,203
Aug-22	449,000	347,940	115,055	112,651	120,234
Sep-22	610,000	457,923	158,634	147,583	151,706
Oct-22	990,000	1,055,135	352,633	347,490	355,012
Nov-22	1,123,000	1,082,893	325,653	379,517	377,723
Dec-22	1,153,000	1,101,489	370,953	359,782	370,754
Production 2022 (ytd) (kWh)	11,166,000	10,287,228	3,465,636	3,275,797	3,545,795
Total Production (kWh) (LTM)	11,166,000	10,287,228	3,465,636	3,275,797	3,545,795
Capacity Factor (LTM)	26.10%				

B. Site Energy Production Graph

December-2022

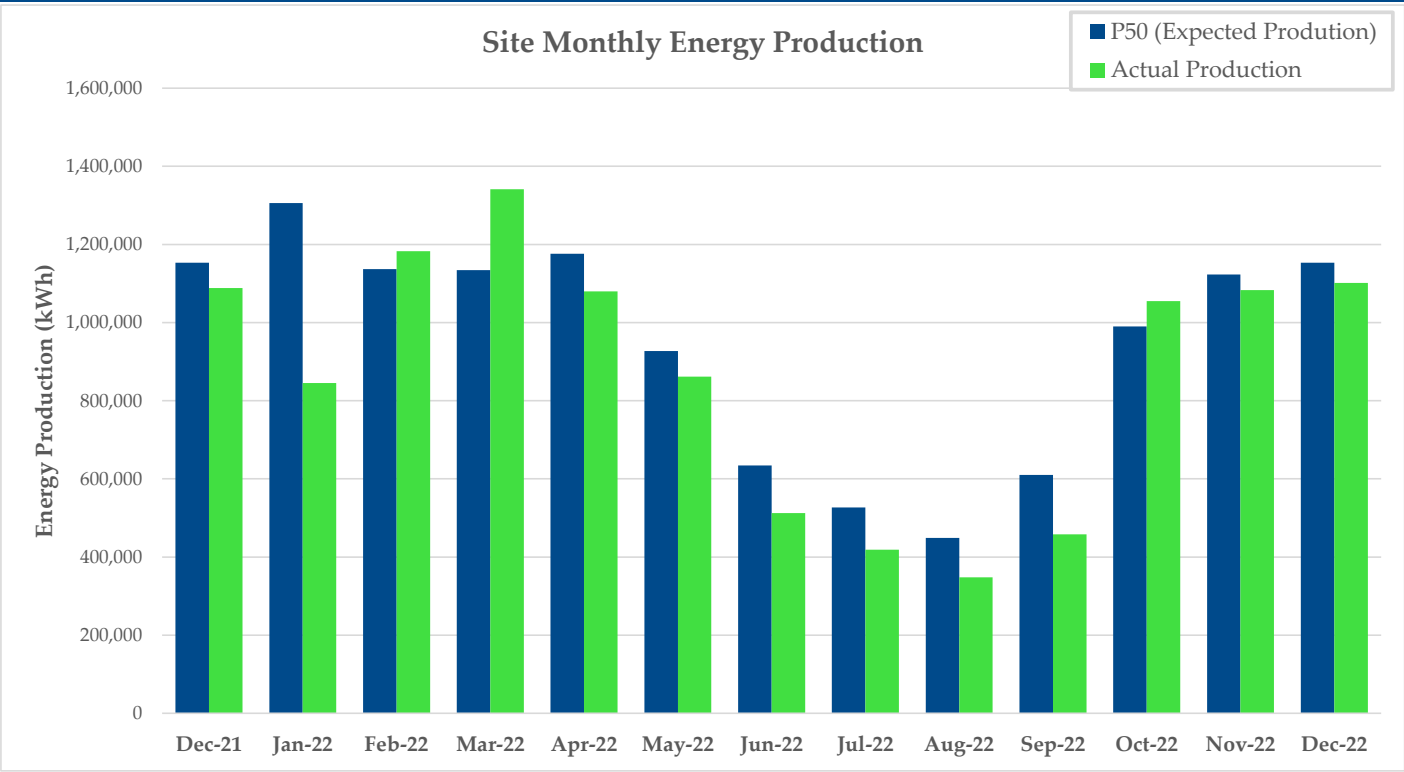

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2023	Goldwind 5.5 Year Maintenance	~8	W1
April-2023	Goldwind 5.5 Year Maintenance	~8	W2
April-2023	Goldwind 5.5 Year Maintenance	~8	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
12/11/2022	Turbine Fault	Unplanned	7.08	W1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	98.95%	98.69%
W2	99.97%	99.81%
W3	100.00%	99.00%
Avg	99.64%	99.17%

Downtime (hr)	This Month	Year To Date
W1	8.49	391.47
W2	0.63	488.48
W3	0.58	343.66
Total	9.70	1223.61

G. Billed Data

Meter Reading (Date/Time)	12/21/2022 12:00 AM
Meter To Date Produced	47,224,023 kWh
Meter To Date Consumed	143,090 kWh
Last Reading Produced	46,355,918 kWh
Last Reading Consumed	141,084 kWh
Billed kWh	866,099 kWh
Next Meter Reading	1/21/2023 12:00 AM

H. Report Notes and Comments
