




BALL CORPORATION - ZEPHYR WIND PROJECT 2.0
North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Feb-22	1,044,000	1,306,639	438,679	422,217	445,743
Mar-22	1,119,000	1,335,480	443,031	438,839	453,610
Apr-22	1,116,000	1,145,744	373,811	368,393	403,540
May-22	876,000	984,712	298,460	333,446	352,806
Jun-22	637,000	601,888	194,009	193,281	214,598
Jul-22	518,000	586,264	192,973	189,924	203,367
Aug-22	448,000	459,360	146,939	148,700	163,721
Sep-22	617,000	570,590	183,735	188,215	198,640
Oct-22	956,000	1,192,941	388,447	392,826	411,668
Nov-22	1,107,000	1,354,289	454,608	437,415	462,266
Dec-22	1,098,000	1,315,996	439,576	434,277	442,143
Jan-23	1,251,000	1,037,565	340,000	345,558	352,007
Feb-23	1,044,000	1,259,079	420,192	393,112	445,775
Production 2022 (ytd) (kWh)	2,295,000	2,296,644	760,192	738,670	797,782
Total Production (kWh) (LTM)	10,787,000	11,843,908	3,875,781	3,863,986	4,104,141
Capacity Factor (LTM)	30.05%				

B. Site Energy Production Graph

February-2023

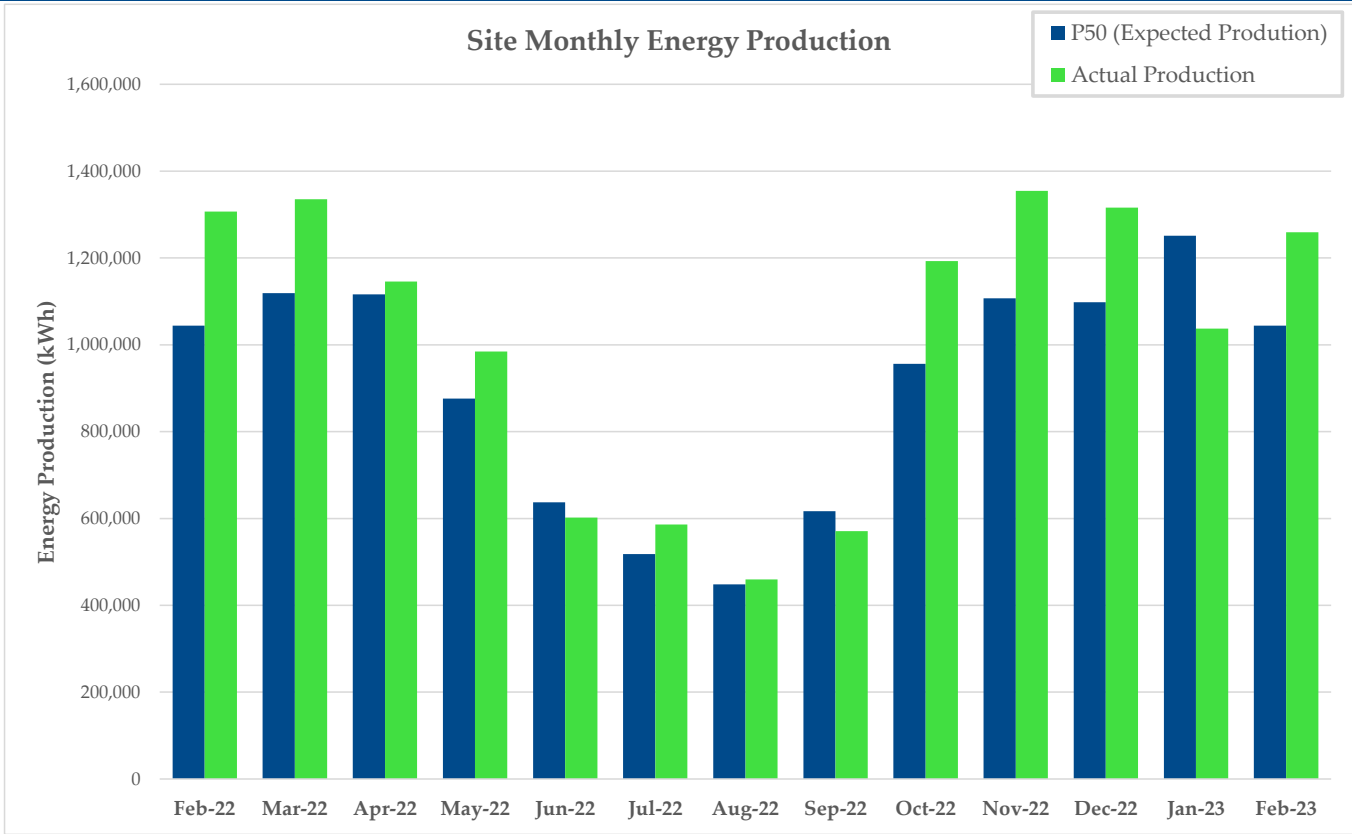

Monthly Report
February-2023



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2023	Goldwind 2.5 Year Maintenance	~8	Z4
March-2023	Goldwind 2.5 Year Maintenance	~8	Z5
March-2023	Goldwind 2.5 Year Maintenance	~8	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/5/2023-2/9/2023	Turbine Fault	Unplanned	63.10	Z5
2/22/2023	Weather Shutdown	Unplanned	16.12	Z4,Z5,Z6

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z4	100.00%	100.00%
Z5	90.59%	95.30%
Z6	100.00%	100.00%
Avg	96.86%	98.43%

Downtime (hr)	This Month	Year To Date
Z4	17.19	24.87
Z5	81.83	89.51
Z6	17.19	24.87
Total	116.21	139.25

G. Billed Data

Meter Reading (Date/Time)	2/18/2023 12:00 AM
Ball 2.0 Production (This Period)	1,222,440 kWh
Ball 2.0 Consumption (This Period)	2,195 kWh
Billed kWh	1,220,245 kWh
Next Meter Reading	3/21/2023 12:00 AM

H. Report Notes and Comments

*March 2022 production includes estimates due to a SCADA server error.
