

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	WG1	WG2	WG3
Feb-22	1,133,000	1,172,040	402,121	396,163	373,756
Mar-22	1,312,000	1,490,987	504,716	495,732	490,539
Apr-22	1,272,000	1,288,755	442,083	425,015	421,657
May-22	974,000	967,486	331,022	319,660	316,804
Jun-22	714,000	591,297	204,680	194,977	191,640
Jul-22	566,000	501,161	169,673	169,616	161,872
Aug-22	514,000	462,848	160,121	151,764	150,963
Sep-22	716,000	611,606	217,120	197,200	197,286
Oct-22	1,051,000	1,275,567	446,816	420,408	408,343
Nov-22	1,224,000	1,260,789	450,647	410,211	399,931
Dec-22	1,217,000	1,186,817	407,671	389,062	390,084
Jan-23	1,343,000	1,022,726	364,829	333,353	324,544
Feb-23	1,133,000	1,357,316	469,593	443,298	444,425
Production 2023 (ytd) (kWh)	2,476,000	2,380,042	834,422	776,651	768,969
Total Production (kWh) (LTM)	12,036,000	12,017,355	4,168,971	3,950,296	3,898,088
Capacity Factor (LTM)	30.49%				

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events


Date	Event	Duration (hr)	Turbine
May-2023	Goldwind 4.5 Year Maintenance	~8	WG 1
May-2023	Goldwind 4.5 Year Maintenance	~8	WG 2
May-2023	Goldwind 4.5 Year Maintenance	~8	WG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

B. Site Energy Production Graph

February-2023

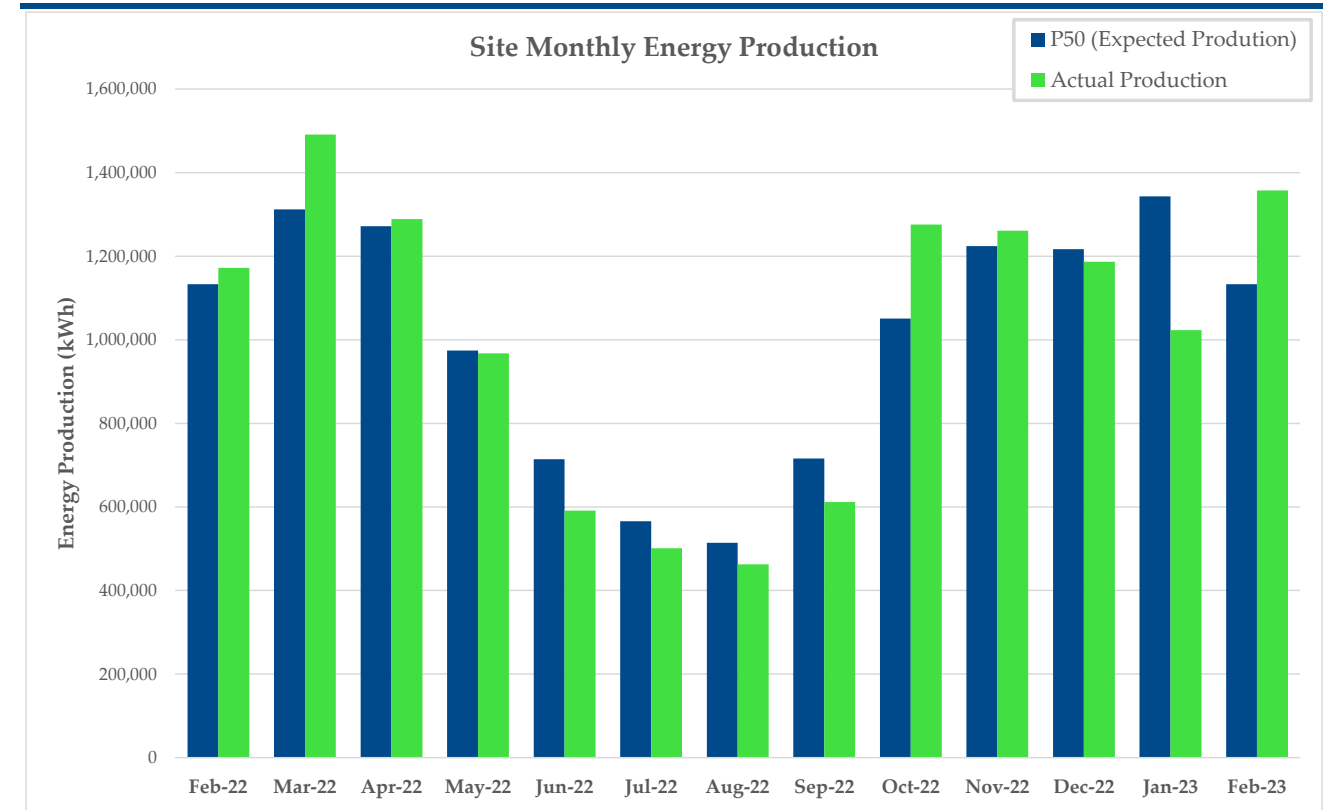

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
WG1	100.00%	100.00%
WG2	99.63%	99.82%
WG3	99.95%	99.94%
Avg	99.86%	99.92%

Downtime (hr)	This Month	Year To Date
WG1	-	40.18
WG2	2.48	31.55
WG3	0.36	24.01
Total	2.84	95.74

G. Billed Data

Meter Reading (Date/Time)	3/1/2023 12:00 AM
Meter To Date Produced	48,004,471 kWh
Meter To Date Consumed	170,410 kWh
Last Reading Produced	46,628,289 kWh
Last Reading Consumed	167,222 kWh
Billed kWh	1,372,994 kWh
Next Meter Reading	3/29/2023 12:00 AM

H. Report Notes and Comments
