



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Mar-22	417,000	465,731
Apr-22	399,000	374,215
May-22	311,000	282,400
Jun-22	228,000	182,539
Jul-22	179,000	154,343
Aug-22	157,000	131,637
Sep-22	224,000	180,602
Oct-22	338,000	363,631
Nov-22	402,000	396,713
Dec-22	403,000	314,804
Jan-23	460,000	327,622
Feb-23	372,000	401,881
Mar-23	417,000	361,885
Production 2023 (ytd) (kWh)	1,249,000	1,091,388
Total Production (kWh) (LTM)	3,890,000	3,472,272
Capacity Factor (LTM)	26.43%	

B. Site Energy Production Graph

March-2023

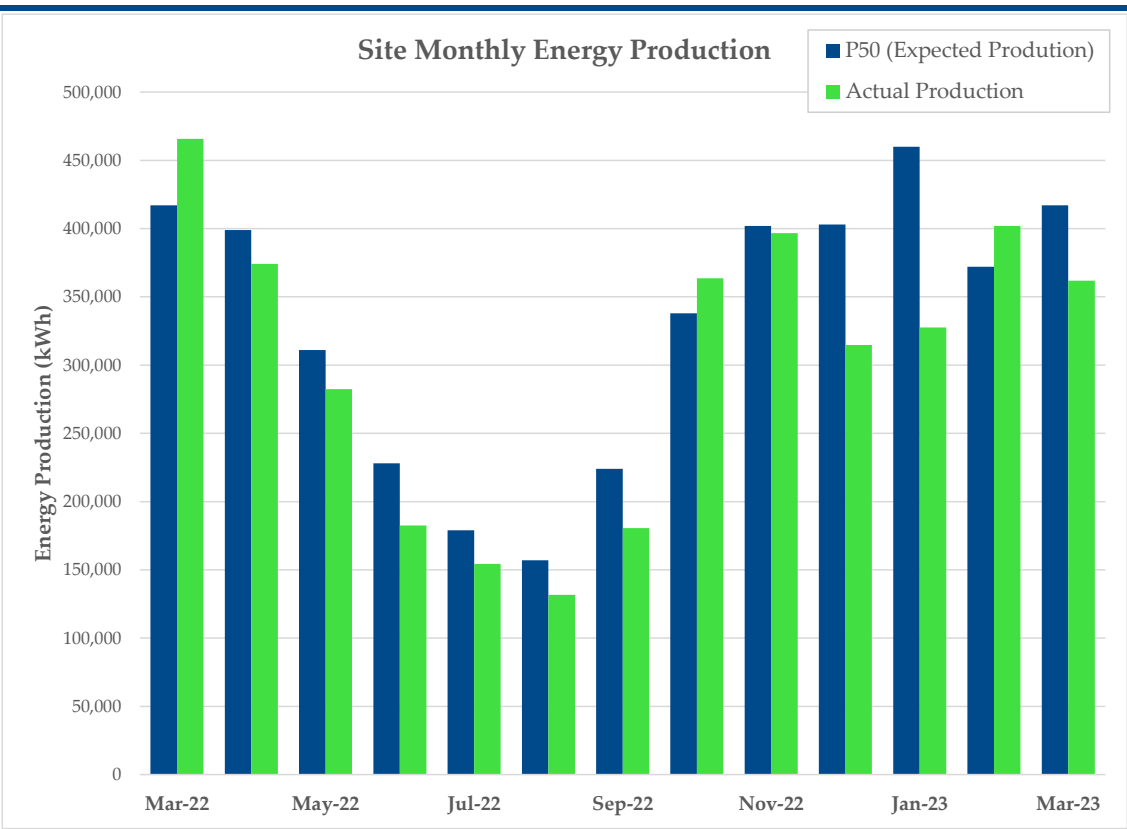

Monthly Report

March-2023



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2023	Goldwind 7 Year Maintenance	~15	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/4/2023-3/5/2023	Grid Fault	Unplanned	22.74	H1
3/16/2023	Turbine Fault	Unplanned	8.35	H1
3/25/2023-3/26/2023	Turbine Fault	Unplanned	24.95	H1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
H1	95.52%	98.41%
Downtime (hr)	This Month	Year To Date
H1	61.24	100.12

G. Billed Data

Meter Reading (Date/Time)	3/28/2023 12:00 AM
Meter To Date Produced	23,836,308 kWh
Meter To Date Consumed	76,245 kWh
Last Reading Produced	23,479,103 kWh
Last Reading Consumed	75,631 kWh
Billed kWh	356,591 kWh
Next Meter Reading	4/27/2023 12:00 AM

H. Report Notes and Comments
