



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Apr-22	399,000	374,215
May-22	311,000	282,400
Jun-22	228,000	182,539
Jul-22	179,000	154,343
Aug-22	157,000	131,637
Sep-22	224,000	180,602
Oct-22	338,000	363,631
Nov-22	402,000	396,713
Dec-22	403,000	314,804
Jan-23	460,000	327,622
Feb-23	372,000	401,881
Mar-23	417,000	361,885
Apr-23	399,000	272,556
Production 2023 (ytd) (kWh)	1,648,000	1,363,944
Total Production (kWh) (LTM)	3,890,000	3,370,613
Capacity Factor (LTM)	25.65%	

B. Site Energy Production Graph

April-2023

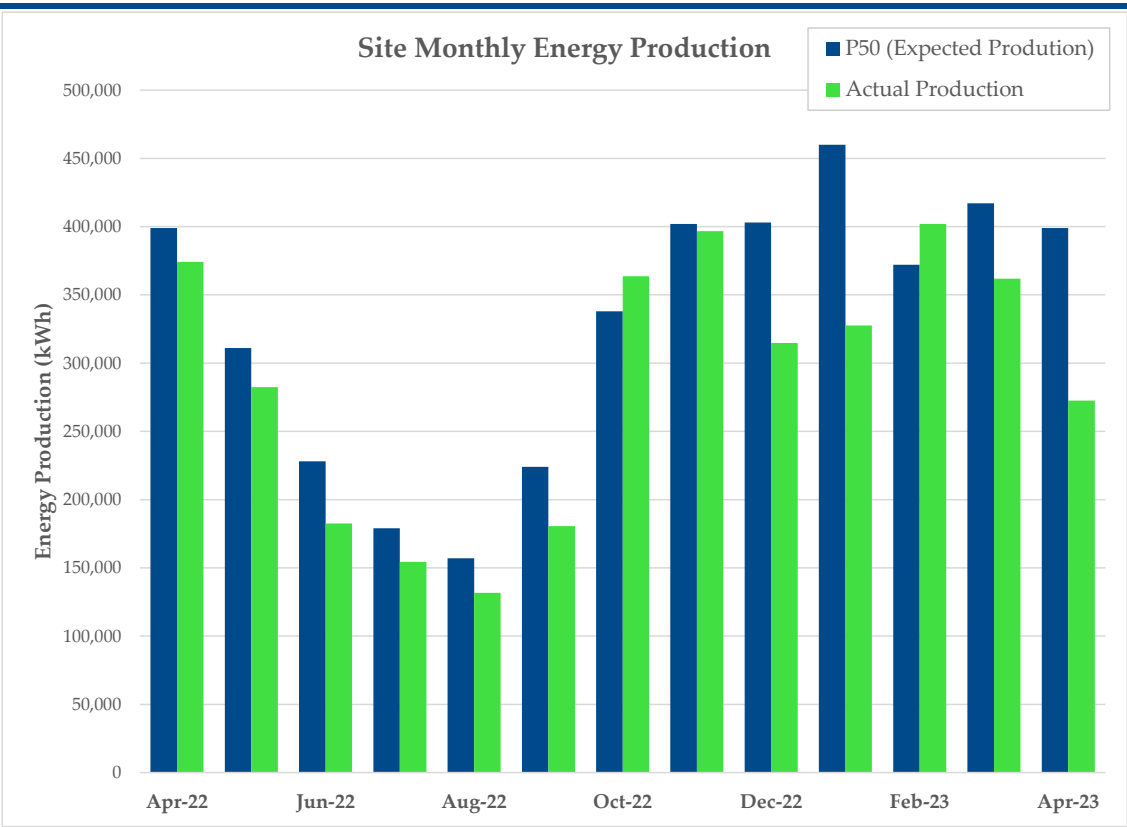

Monthly Report

April-2023



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2023	Goldwind 7.5 Year Maintenance	~8	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/1/2023-4/3/2023	Grid Event	Unplanned	50.52	H1
4/3/2023	Goldwind 7 Year Maintenance	Planned	0.77	H1
4/27/2023	Goldwind 7 Year Maintenance	Planned	3.46	H1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
H1	99.96%	98.80%
Downtime (hr)	This Month	Year To Date
H1	58.91	159.03

G. Billed Data

Meter Reading (Date/Time)	4/27/2023 12:00 AM
Meter To Date Produced	24,118,554 kWh
Meter To Date Consumed	77,093 kWh
Last Reading Produced	23,836,308 kWh
Last Reading Consumed	76,245 kWh
Billed kWh	281,398 kWh
Next Meter Reading	5/26/2023 12:00 AM

H. Report Notes and Comments
