



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
May-22	311,000	282,400
Jun-22	228,000	182,539
Jul-22	179,000	154,343
Aug-22	157,000	131,637
Sep-22	224,000	180,602
Oct-22	338,000	363,631
Nov-22	402,000	396,713
Dec-22	403,000	314,804
Jan-23	460,000	327,622
Feb-23	372,000	401,881
Mar-23	417,000	361,885
Apr-23	399,000	272,556
May-23	311,000	214,744
Production 2023 (ytd) (kWh)	1,959,000	1,578,688
Total Production (kWh) (LTM)	3,890,000	3,302,957
Capacity Factor (LTM)	25.14%	

B. Site Energy Production Graph

May-2023

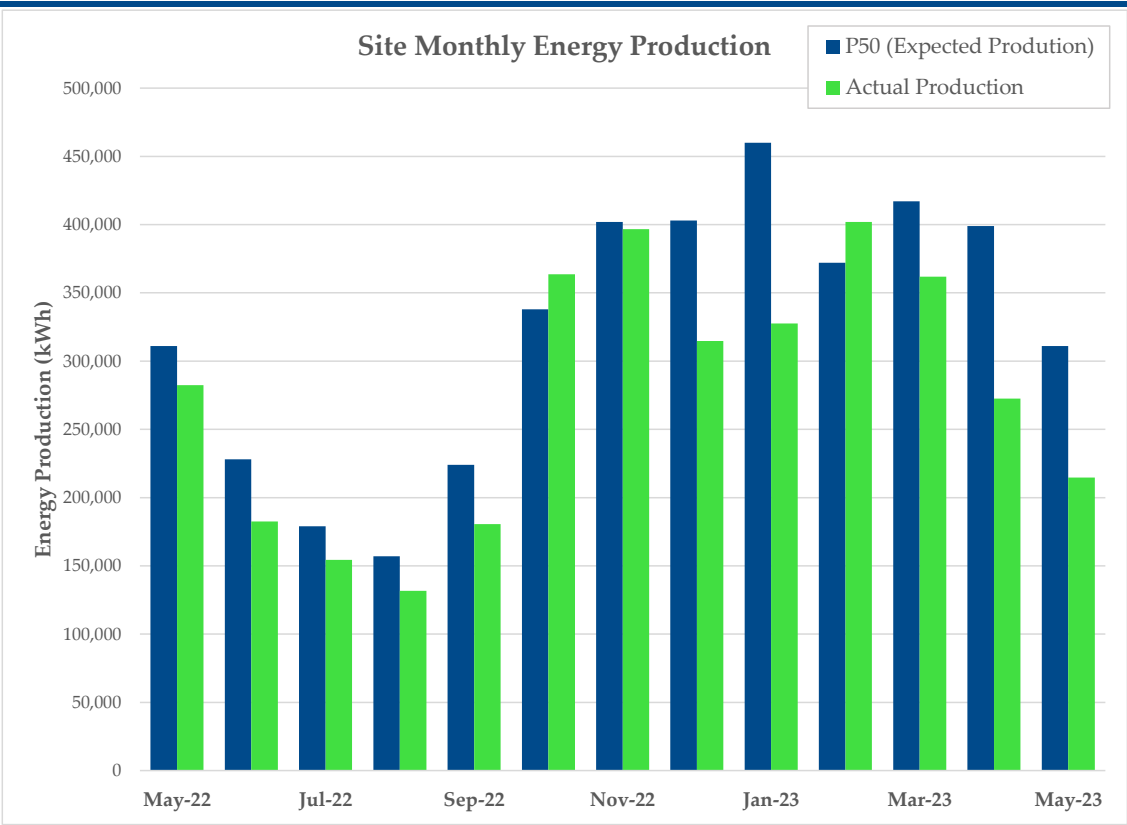

Monthly Report

May-2023



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2023	Goldwind 7.5 Year Maintenance	~8	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/2/2023-5/3/2023	Turbine Fault	Unplanned	12.11	H1
5/3/2023	Goldwind 7 Year Maintenance	Planned	2.48	H1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
H1	98.37%	98.71%
Downtime (hr)	This Month	Year To Date
H1	22.32	181.35

G. Billed Data

Meter Reading (Date/Time)	5/26/2023 12:00 AM
Meter To Date Produced	24,337,121 kWh
Meter To Date Consumed	77,897 kWh
Last Reading Produced	24,118,554 kWh
Last Reading Consumed	77,093 kWh
Billed kWh	217,763 kWh
Next Meter Reading	6/27/2023 12:00 AM

H. Report Notes and Comments
