


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Jun-22	425,000	413,887	205,685	208,202
Jul-22	390,000	405,644	204,608	201,036
Aug-22	399,000	316,041	159,653	156,388
Sep-22	337,000	370,915	189,397	181,518
Oct-22	637,000	822,082	414,170	407,912
Nov-22	834,000	952,177	479,422	472,755
Dec-22	1,015,000	920,397	460,812	459,585
Jan-23	875,000	703,088	359,790	343,298
Feb-23	917,000	890,580	449,499	441,081
Mar-23	802,000	918,289	462,488	455,801
Apr-23	951,000	686,249	342,823	343,426
May-23	601,000	541,021	268,754	272,267
Jun-23	425,000	413,801	210,347	203,454
Production 2023 (ytd) (kWh)	4,571,000	4,153,028	2,093,701	2,059,327
Total Production (kWh) (LTM)	8,183,000	7,940,284	4,001,763	3,938,521
Capacity Factor (LTM)	30.21%			

B. Site Energy Production Graph

June-2023

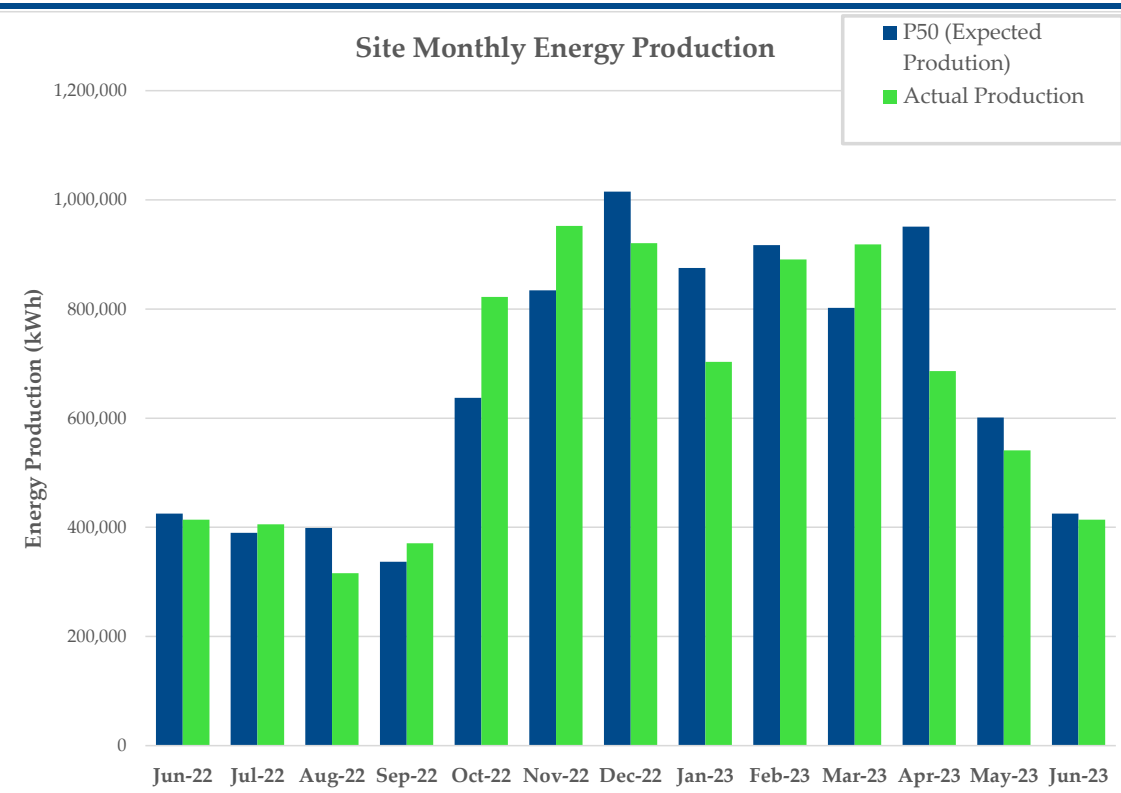

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2023	Goldwind 8 Year Maintenance	~15	W1
November-2023	Goldwind 8 Year Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
W1	100.00%	99.98%
W2	99.60%	99.90%
Avg	99.80%	99.94%

Downtime (hr)	This Month	Year To Date
W1	1.45	51.12
W2	3.43	49.77
Total	4.88	100.89

G. Billed Data

Meter Reading (Date/Time)	6/29/2023 12:00 AM
Meter To Date Produced	57,839,557 kWh
Meter To Date Consumed	111,270 kWh
Last Reading Produced	57,425,828 kWh
Last Reading Consumed	109,905 kWh
Billed kWh	412,364 kWh
Next Meter Reading	7/29/2023 12:00 AM

H. Report Notes and Comments
