


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Jul-22	351,000	385,489	190,281	195,208
Aug-22	303,000	297,191	147,920	149,271
Sep-22	431,000	383,178	188,508	194,670
Oct-22	674,000	770,712	390,964	379,748
Nov-22	796,000	889,743	458,319	431,424
Dec-22	820,000	853,742	430,989	422,753
Jan-23	931,000	675,941	335,912	340,029
Feb-23	737,000	890,155	447,488	442,667
Mar-23	777,000	897,476	445,429	452,047
Apr-23	722,000	669,323	334,035	335,288
May-23	564,000	550,907	281,748	269,159
Jun-23	422,000	414,035	207,507	206,528
Jul-23	351,000	239,451	127,232	112,219
Production 2023 (ytd) (kWh)	4,504,000	4,337,288	2,179,351	2,157,937
Total Production (LTM) (kWh)	7,528,000	7,531,854	3,796,051	3,735,803
Capacity Factor (LTM)	28.66%			

B. Site Energy Production Graph

July-2023

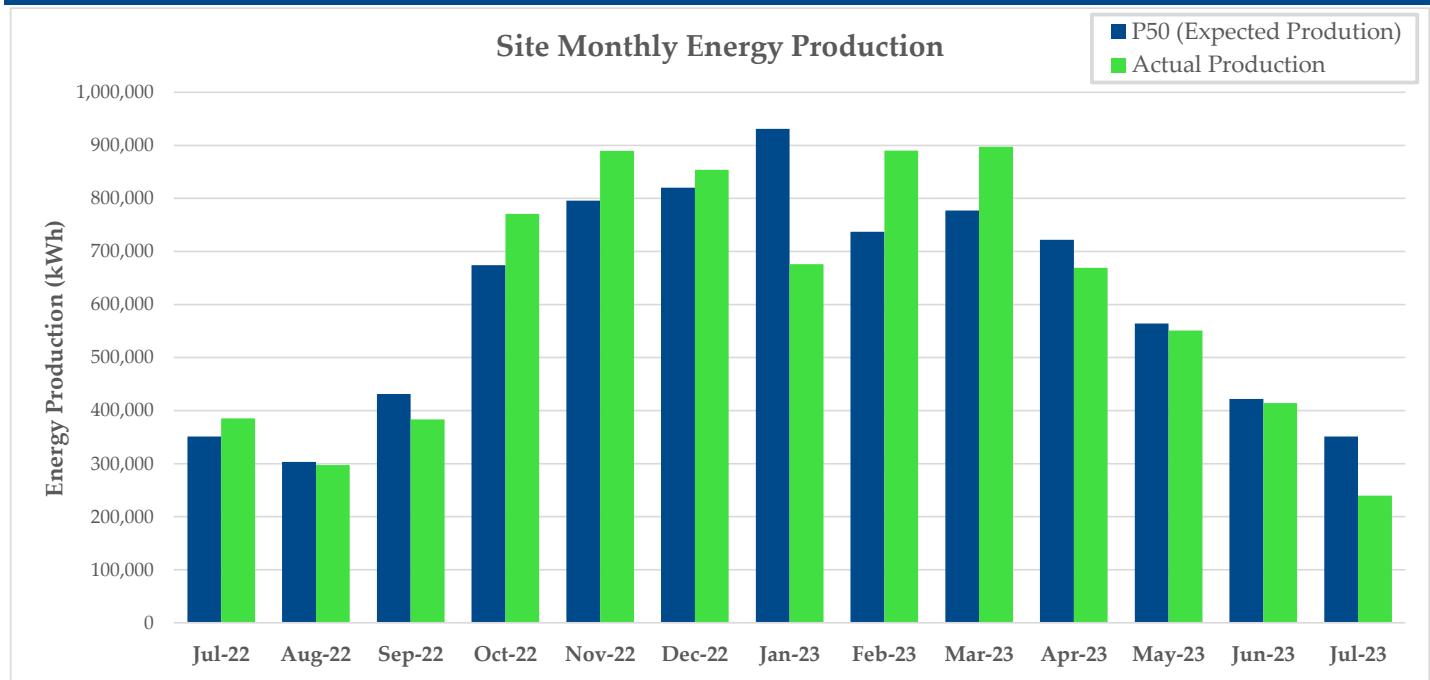

Monthly Report

July-2023

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2023	Goldwind 5 Year Maintenance	~15	V1
November-2023	Goldwind 5 Year Maintenance	~15	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
7/11/2023	V1 Troubleshooting	Unplanned	4.26	V1
7/11/2023-7/12/2023	Turbine Fault	Unplanned	30.05	V2
7/21/2023-7/22/2023	Turbine Fault	Unplanned	11.11	V2
7/23/2023-7/24/2023	Turbine Fault	Unplanned	37.1	V2

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
V1	99.41%	99.92%
V2	88.89%	97.97%
Avg	94.15%	98.94%

Downtime (hr)	This Month	Year To Date
V1	8.71	46.68
V2	86.95	149.77
Total	95.66	196.45

G. Billed Data

Meter Reading (Date/Time)	8/1/2023 12:00 AM
Meter To Date Produced	35,556,910 kWh
Meter To Date Consumed	90,286 kWh
Last Reading Produced	35,326,088 kWh
Last Reading Consumed	87,094 kWh
Billed kWh	227,630 kWh
Next Meter Reading	9/1/2023 12:00 AM

H. Report Notes and Comments
