



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Aug-22	157,000	131,637
Sep-22	224,000	180,602
Oct-22	338,000	363,631
Nov-22	402,000	396,713
Dec-22	403,000	314,804
Jan-23	460,000	327,622
Feb-23	372,000	401,881
Mar-23	417,000	361,885
Apr-23	399,000	272,556
May-23	311,000	214,744
Jun-23	228,000	169,424
Jul-23	179,000	116,572
Aug-23	157,000	139,977
Production 2023 (ytd) (kWh)	2,523,000	2,004,661
Total Production (kWh) (LTM)	3,890,000	3,260,411
Capacity Factor (LTM)	24.81%	

B. Site Energy Production Graph

August-2023

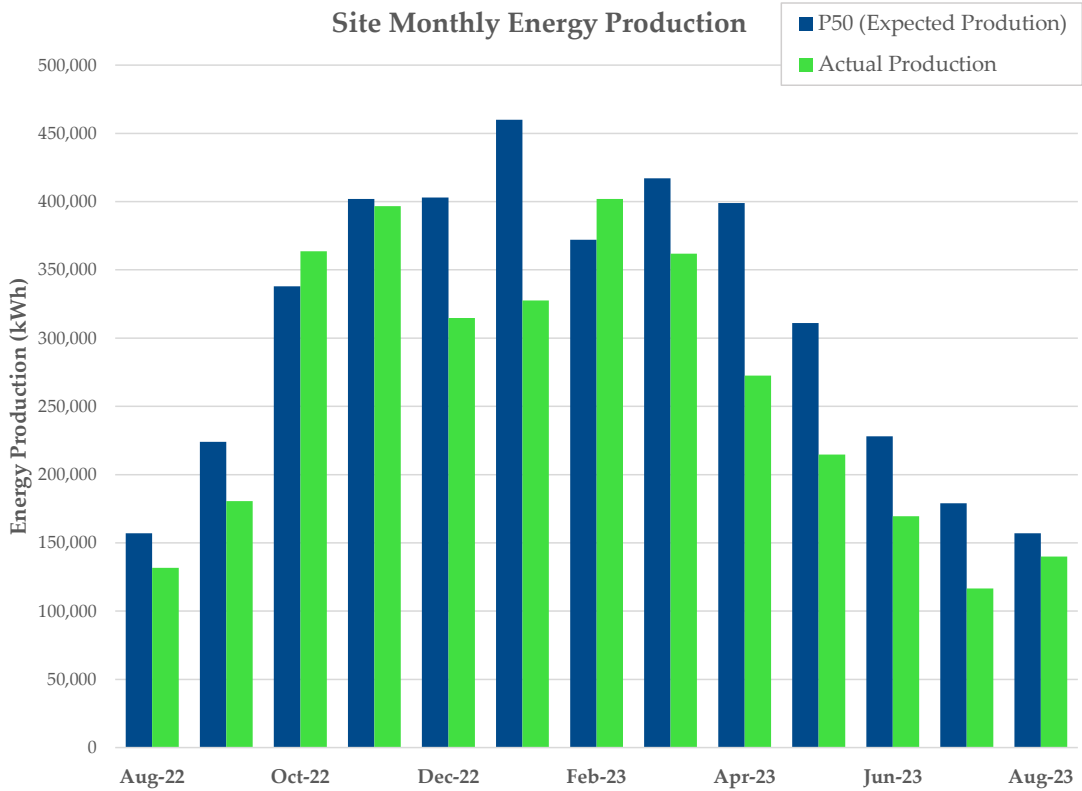

Monthly Report

August-2023



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2023	Goldwind 7.5 Year Maintenance	~8	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
H1	100.00%	99.19%
Downtime (hr)	This Month	Year To Date
H1	8.97	204.58

G. Billed Data

Meter Reading (Date/Time)	8/25/2023 12:00 AM
Meter To Date Produced	24,760,788 kWh
Meter To Date Consumed	81,323 kWh
Last Reading Produced	24,630,021 kWh
Last Reading Consumed	80,156 kWh
Billed kWh	129,600 kWh
Next Meter Reading	9/26/2023 12:00 AM

H. Report Notes and Comments
