

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	WG1	WG2	WG3
Oct-22	1,051,000	1,275,567	446,816	420,408	408,343
Nov-22	1,224,000	1,260,789	450,647	410,211	399,931
Dec-22	1,217,000	1,186,817	407,671	389,062	390,084
Jan-23	1,343,000	1,022,726	364,829	333,353	324,544
Feb-23	1,133,000	1,357,316	469,593	443,298	444,425
Mar-23	1,312,000	1,397,327	483,104	451,227	462,996
Apr-23	1,272,000	971,079	347,951	314,716	308,412
May-23	974,000	666,913	244,432	206,831	215,650
Jun-23	714,000	586,809	200,667	193,800	192,342
Jul-23	566,000	447,128	154,258	148,599	144,271
Aug-23	514,000	508,391	179,206	161,643	167,542
Sep-23	716,000	353,349	120,898	111,723	120,728
Oct-23	1,051,000	833,613	294,717	274,789	264,107
Production 2023 (ytd) (kWh)	9,595,000	8,144,651	2,859,655	2,639,979	2,645,017
Total Production (LTM) (kWh)	12,036,000	10,592,257	3,717,973	3,439,252	3,435,032
Capacity Factor (LTM)	26.87%				

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events


Date	Event	Duration (hr)	Turbine
November-2023	5 Year Maintenance	~15	WG 1
November-2023	5 Year Maintenance	~15	WG 2
November-2023	5 Year Maintenance	~15	WG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
10/9/2023-10/10/2023	Turbine Fault	Unplanned	21.11	WG 3

B. Site Energy Production Graph

October-2023

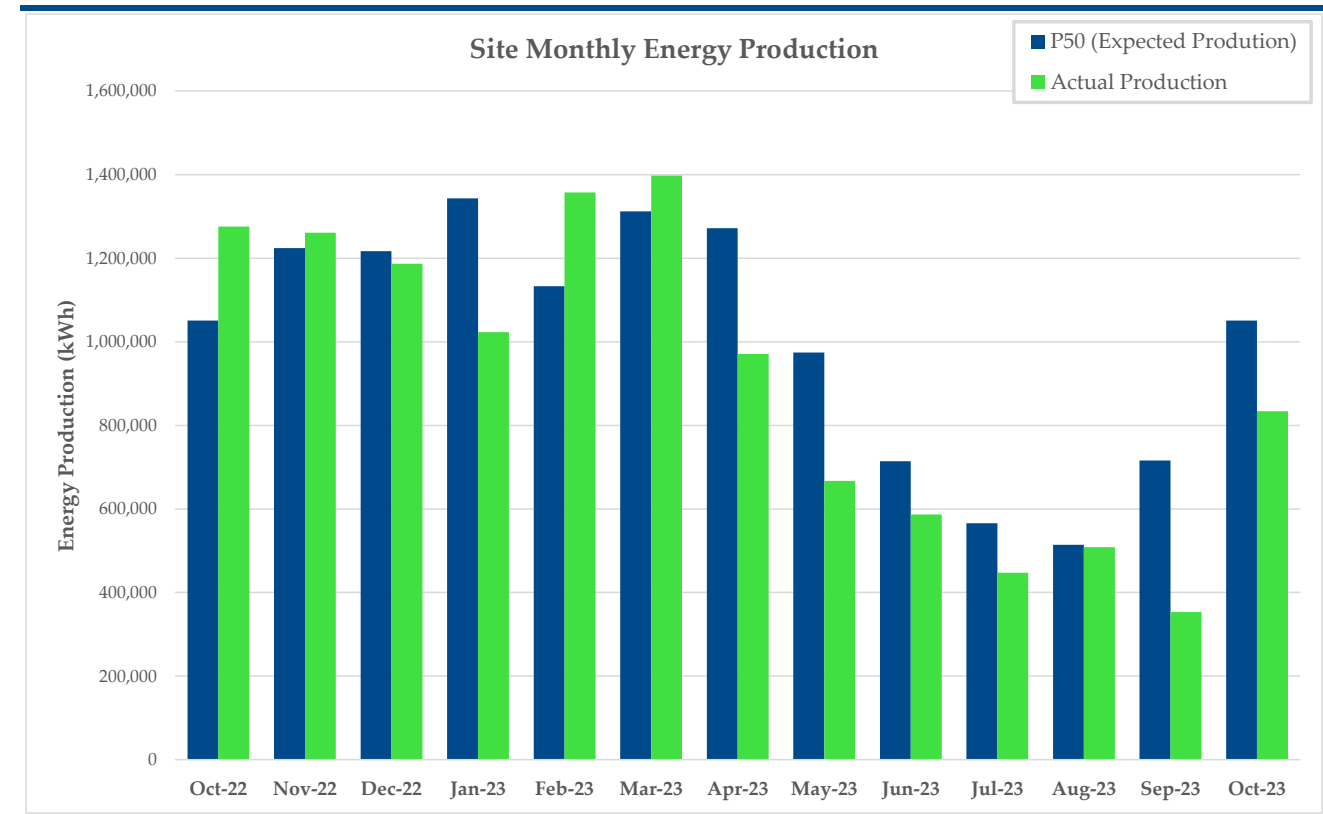

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
WG1	100.00%	100.00%
WG2	100.00%	99.32%
WG3	96.94%	98.46%
Avg	98.98%	99.26%

Downtime (hr)	This Month	Year To Date
WG1	0.54	74.14
WG2	0.43	119.12
WG3	23.04	169.35
Total	24.01	362.61

G. Billed Data

Meter Reading (Date/Time)	10/29/2023 12:00 AM
Meter To Date Produced	53,644,919 kWh
Meter To Date Consumed	199,915 kWh
Last Reading Produced	52,878,940 kWh
Last Reading Consumed	196,708 kWh
Billed kWh	762,772 kWh
Next Meter Reading	11/29/2023 12:00 AM

H. Report Notes and Comments
