




BALL CORPORATION - ZEPHYR WIND PROJECT 2.0
North Findlay Wind Campus, Findlay, Ohio

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
Nov-22	1,107,000	1,354,289	454,608	437,415	462,266
Dec-22	1,098,000	1,315,996	439,576	434,277	442,143
Jan-23	1,251,000	1,037,565	340,000	345,558	352,007
Feb-23	1,044,000	1,259,079	420,192	393,112	445,775
Mar-23	1,119,000	1,327,802	443,370	431,527	452,905
Apr-23	1,116,000	979,332	324,138	323,000	332,194
May-23	876,000	854,422	270,909	283,285	300,228
Jun-23	637,000	690,482	226,931	231,165	232,387
Jul-23	518,000	381,255	124,683	125,868	130,704
Aug-23	448,000	542,148	181,375	178,264	182,509
Sep-23	617,000	359,251	114,733	121,644	122,874
Oct-23	956,000	879,647	289,457	284,843	305,347
Nov-23	1,107,000	1,168,998	394,642	378,664	395,692
Production 2023 (ytd) (kWh)	9,689,000	9,479,981	3,130,430	3,096,930	3,252,622
Total Production (LTM) (kWh)	10,787,000	10,795,977	3,570,006	3,531,207	3,694,765
Capacity Factor (LTM)	27.39%				

B. Site Energy Production Graph

November-2023

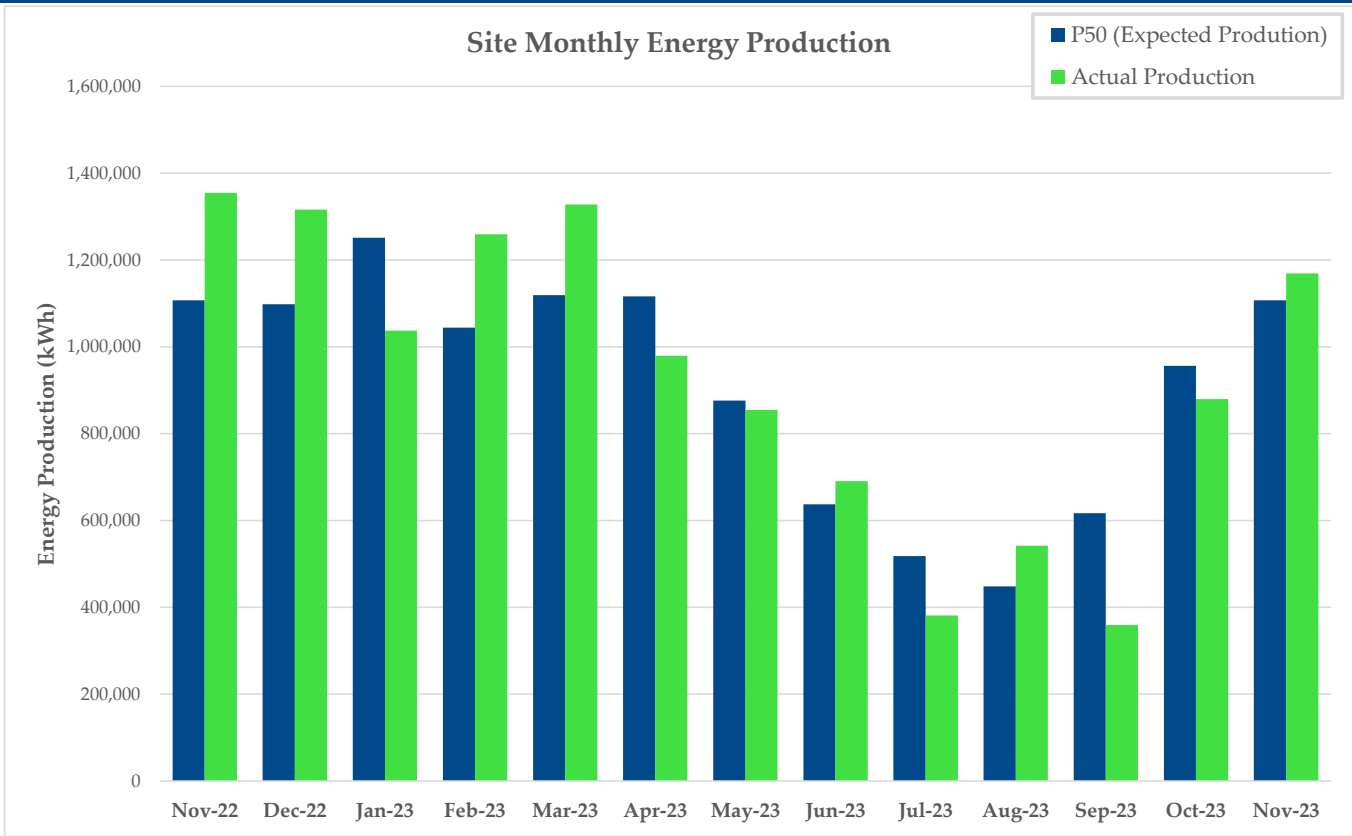

Monthly Report
November-2023



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2024	Goldwind 3.5 Year Maintenance	~8	Z4
March-2024	Goldwind 3.5 Year Maintenance	~8	Z5
March-2024	Goldwind 3.5 Year Maintenance	~8	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
11/23/2023-11/25/2023	Plant Shutdown	Unplanned	36.03	Z4
11/23/2023-11/25/2023	Plant Shutdown	Unplanned	36.03	Z5
11/23/2023-11/25/2023	Plant Shutdown	Unplanned	36.03	Z6

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z4	100.00%	99.99%
Z5	100.00%	98.65%
Z6	100.00%	100.00%
Avg	100.00%	99.54%

Downtime (hr)	This Month	Year To Date
Z4	36.42	115.12
Z5	37.99	228.21
Z6	36.5	112.44
Total	110.91	455.77

G. Billed Data

Meter Reading (Date/Time)	11/16/2023 12:00 AM
Ball 2.0 Production (This Period)	929,191 kWh
Ball 2.0 Consumption (This Period)	1,099 kWh
Billed kWh	928,092 kWh
Next Meter Reading	12/19/2023 12:00 AM

H. Report Notes and Comments

*June 23 - June 25 Production is an estimate due to a SCADA server error.
