


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	V1	V2
Nov-22	796,000	889,743	458,319	431,424
Dec-22	820,000	853,742	430,989	422,753
Jan-23	931,000	675,941	335,912	340,029
Feb-23	737,000	890,155	447,488	442,667
Mar-23	777,000	897,476	445,429	452,047
Apr-23	722,000	669,323	334,035	335,288
May-23	564,000	550,907	281,748	269,159
Jun-23	422,000	414,035	207,507	206,528
Jul-23	351,000	239,451	127,232	112,219
Aug-23	303,000	352,751	170,780	181,971
Sep-23	431,000	226,645	110,485	116,160
Oct-23	674,000	582,309	277,729	304,580
Nov-23	796,000	809,264	396,263	413,001
Production 2023 (ytd) (kWh)	6,708,000	6,308,257	3,134,608	3,173,649
Total Production (LTM) (kWh)	7,528,000	7,161,999	3,565,597	3,596,402
Capacity Factor (LTM)	27.25%			

B. Site Energy Production Graph

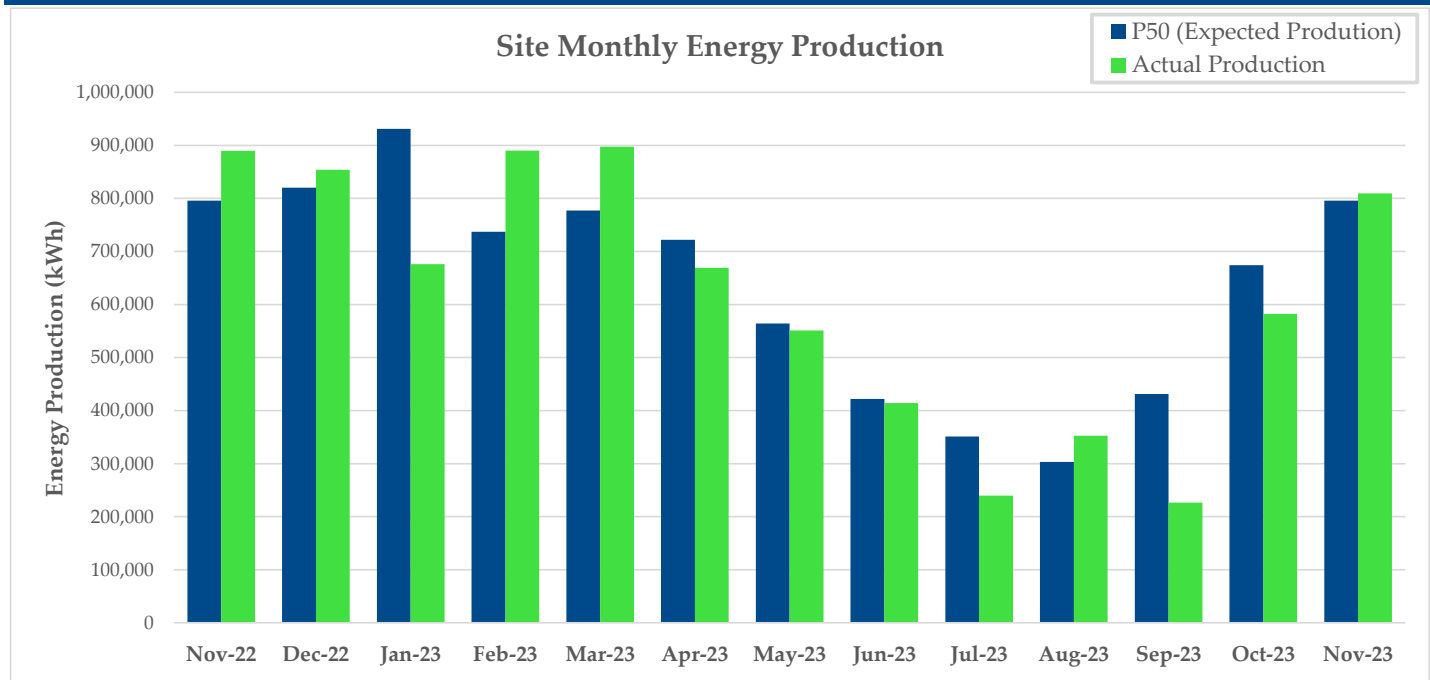

Monthly Report

November-2023



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2023	5 Year Maintenance	~15	V1
November-2023	5 Year Maintenance	~15	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Availability & Downtime*

Availability	This Month	Year To Date
V1	100.00%	99.88%
V2	100.00%	98.61%
Avg	100.00%	99.25%

Downtime (hr)	This Month	Year To Date
V1	0.21	78.12
V2	0.36	164.36
Total	0.57	242.48

G. Billed Data

Meter Reading (Date/Time)	12/1/2023 12:00 AM
Meter To Date Produced	37,459,909 kWh
Meter To Date Consumed	97,091 kWh
Last Reading Produced	36,677,261 kWh
Last Reading Consumed	96,279 kWh
Billed kWh	781,836 kWh
Next Meter Reading	1/1/2024 12:00 AM

H. Report Notes and Comments

* Due to expiration of the OEM warranty, turbine availability and downtime reporting will no longer include warrantied availability. Downtime will be categorized appropriately.
