



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Jan-23	460,000	327,622
Feb-23	372,000	401,881
Mar-23	417,000	361,885
Apr-23	399,000	272,556
May-23	311,000	214,744
Jun-23	228,000	169,424
Jul-23	179,000	116,572
Aug-23	157,000	139,977
Sep-23	224,000	93,945
Oct-23	338,000	245,587
Nov-23	402,000	324,788
Dec-23	403,000	257,014
Jan-24	460,000	266,509
Production 2024 (ytd) (kWh)	460,000	266,509
Total Production (LTM) (kWh)	3,890,000	2,864,882
Capacity Factor (LTM)	21.80%	

B. Site Energy Production Graph

January-2024

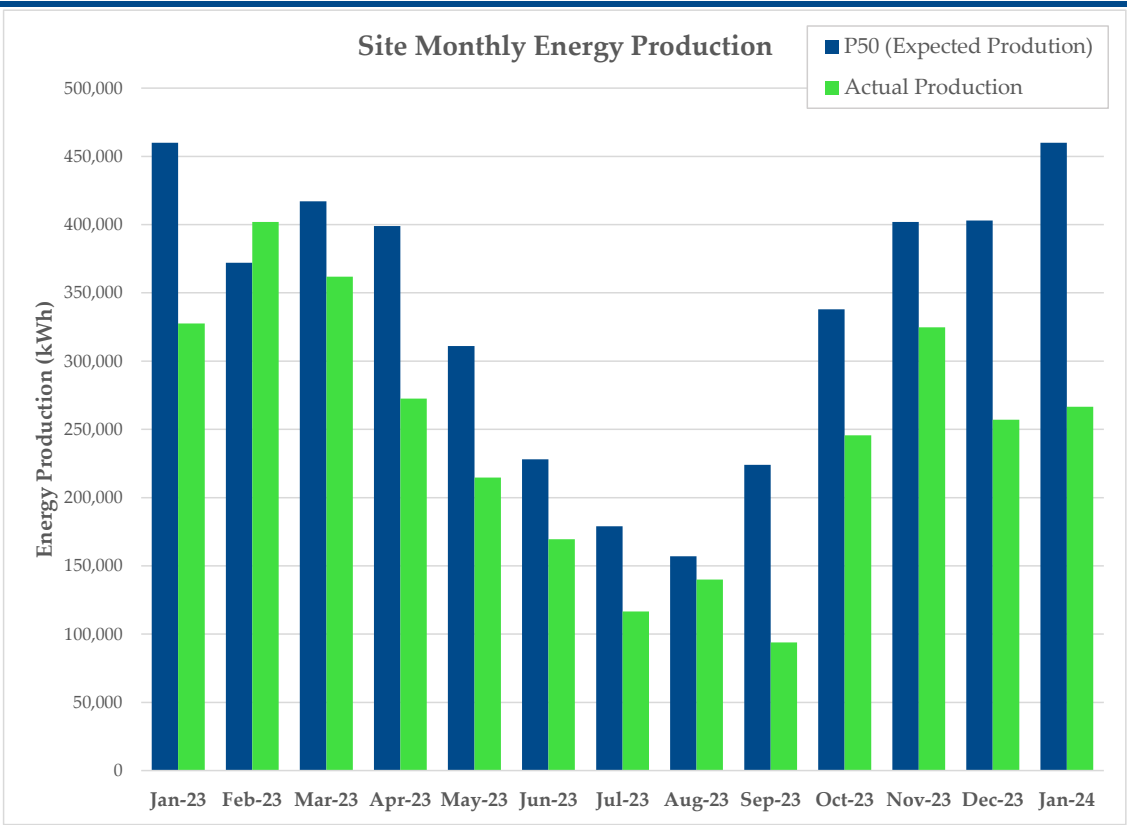

Monthly Report

January-2024



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2024	Goldwind 8 Year Maintenance	~15	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/22/2024-1/31/2024	Fleet Inspection Shutdown	Unplanned	227.12	H1

F. Turbine Availability & Downtime*

Availability	This Month	Year To Date
H1	99.75%	99.75%
Downtime (hr)	This Month	Year To Date
H1	230.43	230.43

G. Billed Data

Meter Reading (Date/Time)	1/27/2024 12:00 AM
Meter To Date Produced	25,956,744 kWh
Meter To Date Consumed	85,889 kWh
Last Reading Produced	25,670,737 kWh
Last Reading Consumed	84,649 kWh
Billed kWh	284,767 kWh
Next Meter Reading	2/27/2024 12:00 AM

H. Report Notes and Comments

*Downtime beginning January 22, 2024 is classified under the 'Other' category due to an ongoing root cause investigation within the fleet; this classification may be subject to reallocation at a later date.
