


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Apr-23	951,000	686,249	342,823	343,426
May-23	601,000	541,021	268,754	272,267
Jun-23	425,000	413,801	210,347	203,454
Jul-23	390,000	267,109	135,436	131,673
Aug-23	399,000	366,119	185,571	180,548
Sep-23	337,000	243,413	123,119	120,294
Oct-23	637,000	624,439	317,183	307,256
Nov-23	834,000	857,725	431,836	425,889
Dec-23	1,015,000	658,931	330,556	328,375
Jan-24	875,000	630,572	316,894	313,678
Feb-24	917,000	0	0	0
Mar-24	802,000	0	0	0
Apr-24	951,000	231,529	116,676	114,853
Production 2024 (ytd) (kWh)	3,545,000	862,101	433,570	428,531
Total Production (LTM) (kWh)	8,183,000	4,834,659	2,436,372	2,398,287
Capacity Factor (LTM)	18.35%			

B. Site Energy Production Graph

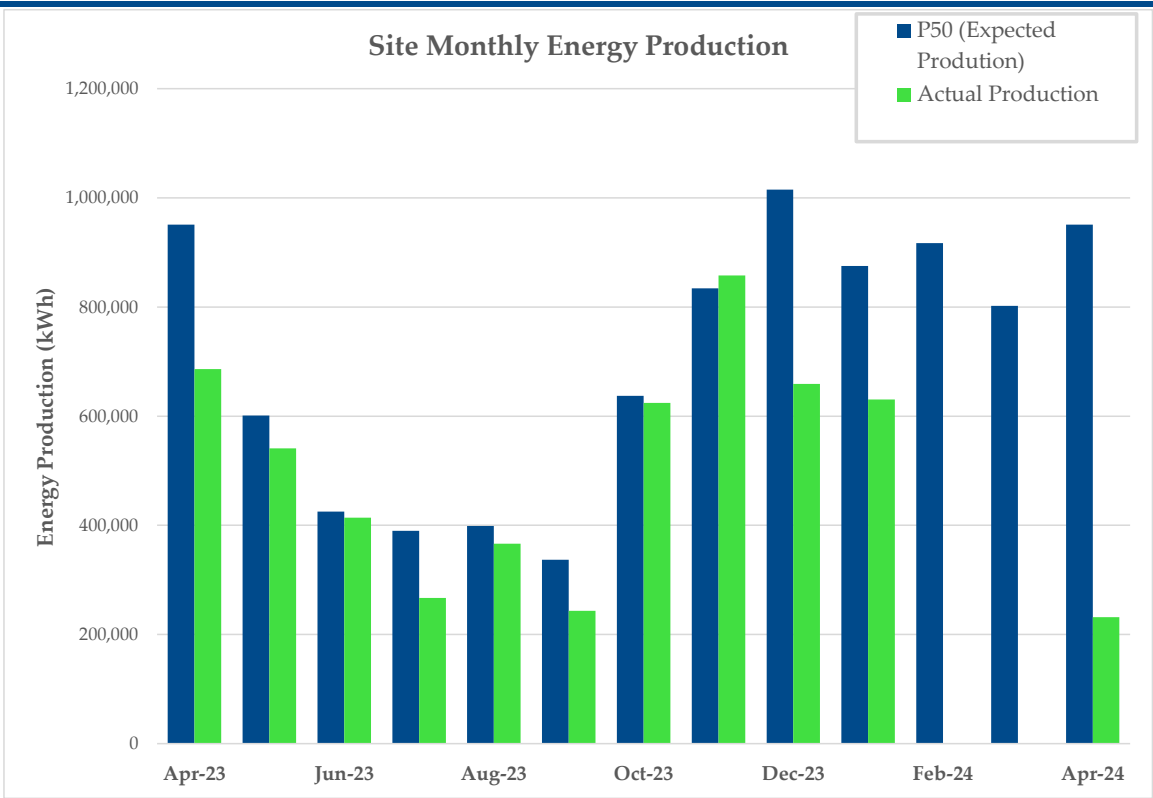

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2024	8.5 Year Preventive Maintenance	~8	W1
May-2024	8.5 Year Preventive Maintenance	~8	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/1/2024-4/22/2024	Fleet Inspection Shutdown	Unplanned	517.79	W1
4/1/2024-4/22/2024	Fleet Inspection Shutdown	Unplanned	513.17	W2

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
W1	517.79	2193.86
W2	513.17	2186.62
Total	1030.96	4380.48

G. Billed Data

Meter Reading (Date/Time)	4/29/2024 12:00 AM
Meter To Date Produced	61,648,727 kWh
Meter To Date Consumed	144,385 kWh
Last Reading Produced	61,466,530 kWh
Last Reading Consumed	121,125 kWh
Billed kWh	158,937 kWh
Next Meter Reading	5/29/2024 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, the project had no energy production February 2024 - March 2024.
