


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	Expected Production	Actual Production	WTG 1	WTG 2	WTG 3
Aug-23	559,508	555,831	128,322	211,051	216,458
Sep-23	603,085	353,794	138,579	132,576	82,639
Oct-23	967,926	1,001,240	338,432	337,485	325,323
Nov-23	1,362,692	1,373,200	473,833	450,348	449,019
Dec-23	1,254,397	1,184,353	403,749	399,895	380,709
Jan-24	1,290,968	1,381,482	471,543	462,558	447,381
Feb-24	1,170,349	1,107,267	415,523	340,449	351,295
Mar-24	1,227,217	1,574,190	537,888	515,417	520,885
Apr-24	1,438,497	1,440,355	491,796	461,645	486,914
May-24	980,450	836,173	284,799	275,439	275,935
Jun-24	649,158	897,472	318,609	299,454	279,409
Jul-24	618,687	494,646	168,488	159,103	167,055
Aug-24	559,508	495,719	172,033	156,575	167,111
Production 2024 (ytd) (kWh)	7,934,835	8,227,304	2,860,679	2,055,508	2,082,410
Total Production (LTM) (kWh)	12,122,935	12,139,891	4,215,272	3,990,944	3,933,675
Capacity Factor (LTM)	30.71%				

B. Site Energy Production Graph

August-2024

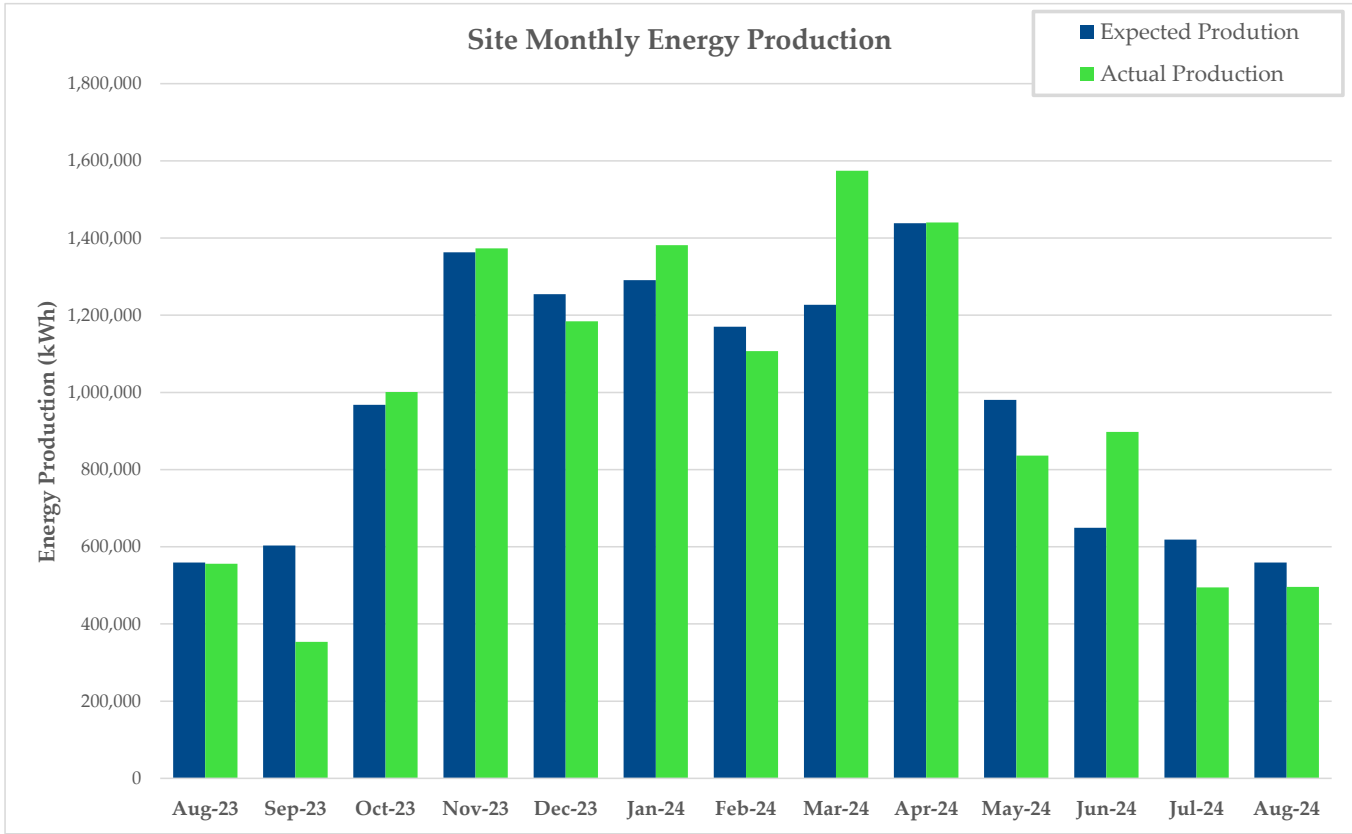

Monthly Report
August-2024

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2024	12 Year Maintenance	~15	WTG 1
October-2024	12 Year Maintenance	~15	WTG 2
October-2024	12 Year Maintenance	~15	WTG 3
1			

E. Actual Maintenance Events

Date	Event	Planned/ Unplanned	Duration (hrs)	Turbine
8/30/2024-8/31/2024	Grid Fault	Unplanned	19.08	WTG 1,WTG 2,WTG 3

F. Turbine Downtime ¹

Downtime (hr)	This Month	Year To Date
WTG 1	20.03	188.47
WTG 2	20.03	278.49
WTG 3	20.03	263.86
Total	60.09	730.82

G. Wind Speed & Capacity Factor ²

Wind Speed (mph)	This Month	2024 Annual
WTG 1	4.94	4.94
WTG 2	4.90	4.90
WTG 3	4.97	4.97
Estimated	11.09	13.39
Capacity Factor (%)	This Month	2024 Annual
WTG 1	15.42%	42.25%
WTG 2	14.03%	41.45%
WTG 3	14.97%	40.09%
Low Estimate	14.90%	28.72%

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² Wind Speed Pending
