



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Aug-23	157,000	139,977
Sep-23	224,000	93,945
Oct-23	338,000	245,587
Nov-23	402,000	324,788
Dec-23	403,000	257,014
Jan-24	460,000	266,509
Feb-24	372,000	77 ²
Mar-24	417,000	0 ²
Apr-24	399,000	71,938
May-24	311,000	176,362
Jun-24	228,000	182,891
Jul-24	179,000	130,160
Aug-24	157,000	115,765
Production 2024 (ytd) (kWh)	2,523,000	943,702
Total Production (LTM) (kWh)	3,890,000	1,865,036
Capacity Factor (LTM)	14.15%	

B. Site Energy Production Graph

August-2024

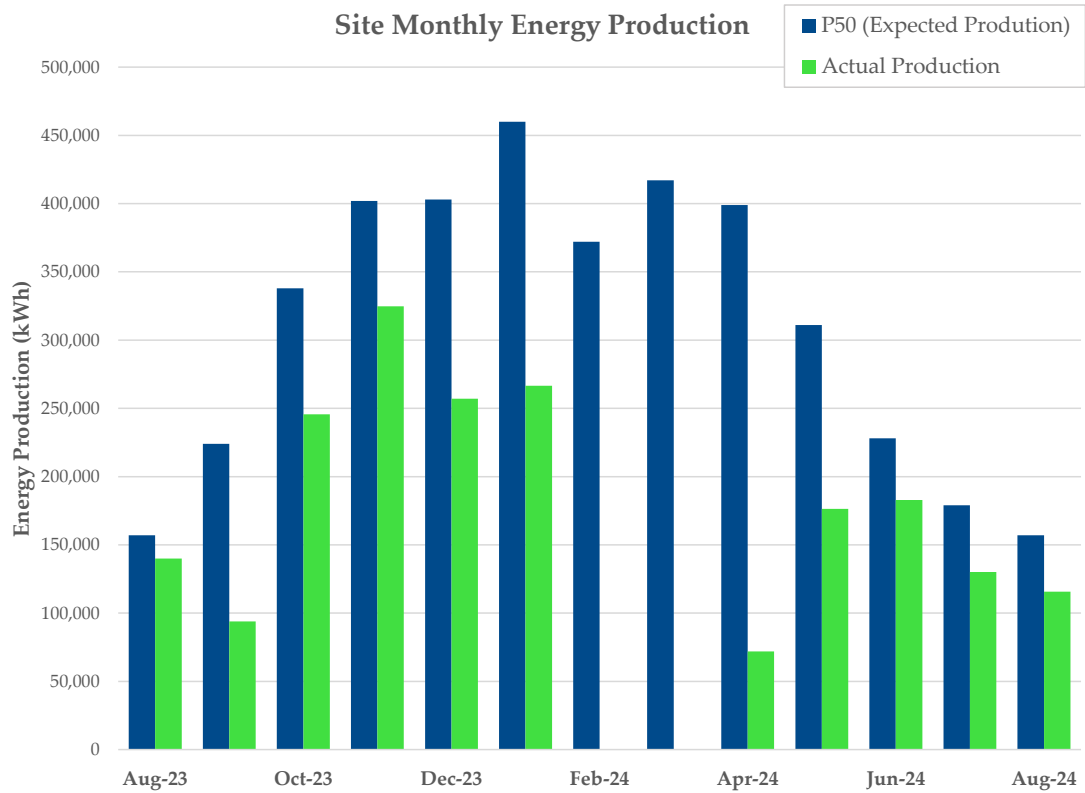

Monthly Report

August-2024



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2024	8 Year Preventive Maintenance	~15	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
8/6/2024	Weather Shutdown	Unplanned	4.11	H1
8/21/2024	Grid Event	Unplanned	4.24	H1
8/29/2024	8 Year Preventive Maintenance	Planned	4.72	H1

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
H1	18.78	2269.87

G. Billed Data

Meter Reading (Date/Time)	8/24/2024 12:00 AM
Meter To Date Produced	26,604,356 kWh
Meter To Date Consumed	103,190 kWh
Last Reading Produced	26,488,525 kWh
Last Reading Consumed	102,007 kWh
Billed kWh	114,648 kWh
Next Meter Reading	9/25/2024 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, the project had no energy production February 2024-March 2024 other than 77kWh for testing.
