


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	Expected Production	Actual Production	WTG A	WTG B	WTG C
Aug-23	577,992	642,748	209,098	212,029	221,621
Sep-23	631,697	463,267	154,792	153,657	154,818
Oct-23	1,003,602	1,091,106	381,773	348,712	360,621
Nov-23	1,395,914	1,358,931	475,875	461,556	421,500
Dec-23	1,278,858	1,094,994	354,430	371,945	368,619
Jan-24	1,332,437	1,291,710	437,812	434,202	419,696
Feb-24	1,157,019	1,212,723	415,829	388,526	408,368
Mar-24	1,242,761	1,577,430	527,008	516,861	533,561
Apr-24	1,447,248	1,470,775	495,877	478,795	496,103
May-24	1,010,966	862,575	288,229	287,713	286,633
Jun-24	668,411	942,158	314,570	308,308	319,280
Jul-24	638,097	496,566	168,933	163,396	164,237
Aug-24	577,992	501,947	169,754	169,011	163,182
Production 2024 (ytd) (kWh)	8,074,930	8,355,884	2,818,012	2,746,812	2,791,060
Total Production (LTM) (kWh)	12,385,000	12,364,182	4,184,882	4,082,682	4,096,618
Capacity Factor (LTM)	31.28%				

B. Site Energy Production Graph

August-2024

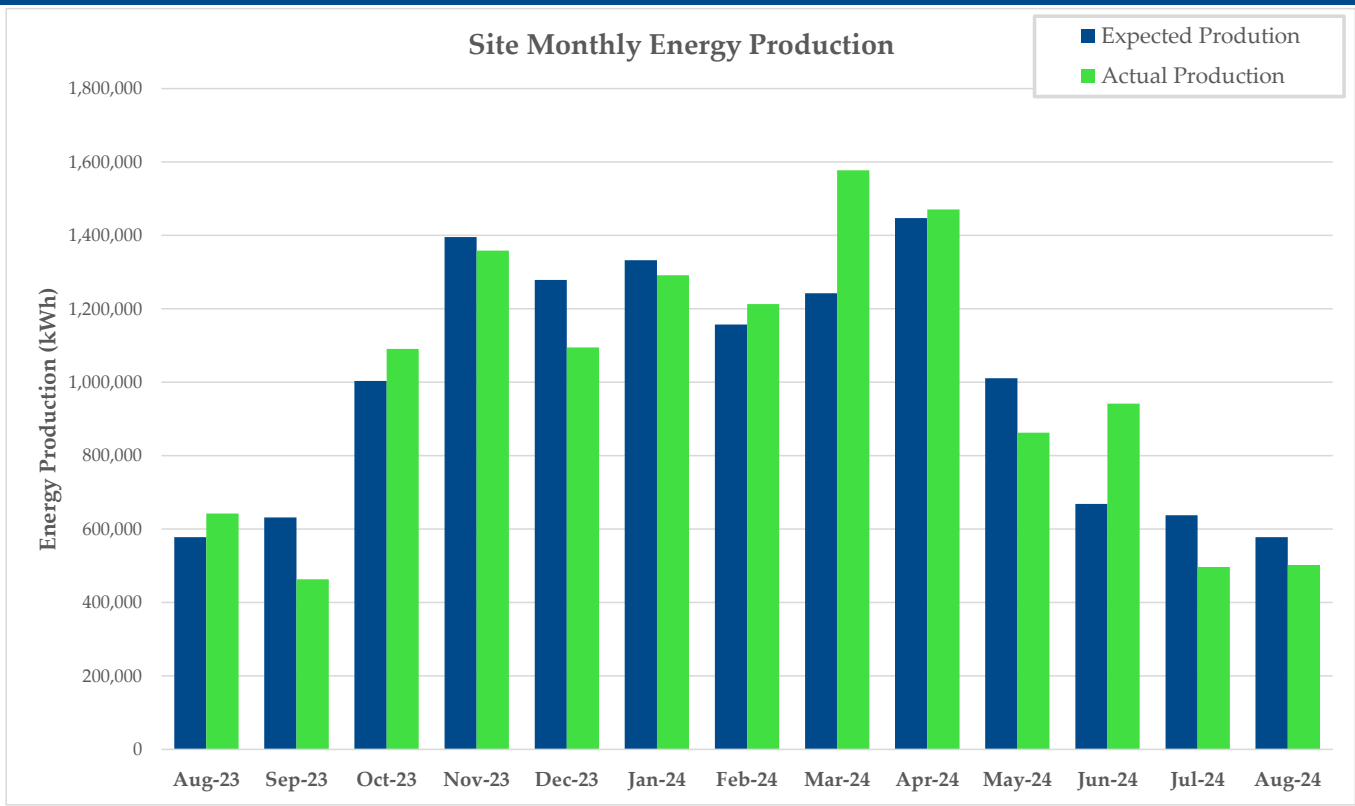

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2024	12 Year Maintenance	~15	WTG A
November-2024	12 Year Maintenance	~15	WTG B
November-2024	12 Year Maintenance	~15	WTG C

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
WTG A	1.39	162.89
WTG B	1.81	113.98
WTG C	2.24	145.88
Total	5.44	422.75

G. Wind Speed & Capacity Factor

Wind Speed (mph)	This Month	2022 Annual
WTG A	9.04	11.77
WTG B	8.93	11.53
WTG C	9.50	12.39
Estimated	11.09	13.39

Capacity Factor (%)	This Month	2022 Annual
WTG A	15.21%	32.08%
WTG B	15.14%	31.27%
WTG C	14.62%	31.77%
Low Estimate	14.90%	28.72%

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.
