


A. Site Energy Production Summary

		Energy Production (kWh)				
		Site		By Turbine		
		P50 (Expected Production)	Actual Production	W1	W2	W3
	Aug-23	449,000	398,914	133,449	128,288	137,177
	Sep-23	610,000	267,906	86,932	83,577	97,397
	Oct-23	990,000	700,059	243,485	220,958	235,616
	Nov-23	1,123,000	964,114	331,159	307,588	325,367
	Dec-23	1,153,000	869,834	302,229	280,586	287,019
	Jan-24	1,306,000	771,163	268,921	247,627	254,615
	Feb-24	1,137,000	0	0	0	0
	Mar-24	1,134,000	0	0	0	0
	Apr-24	1,176,000	269,672	87,026	88,258	94,388
	May-24	927,000	533,339	180,109	172,157	181,073
	Jun-24	634,000	512,583	178,220	152,008	182,355
	Jul-24	527,000	347,033	118,853	106,389	121,791
	Aug-24	449,000	293,672	100,620	93,127	99,925
Production 2024 (ytd) (kWh)		7,290,000	2,727,462	933,749	859,566	934,147
Total Production (LTM) (kWh)		11,166,000	5,529,375	1,897,554	1,752,275	1,879,546
Capacity Factor (LTM)		13.99%				

B. Site Energy Production Graph

August-2024

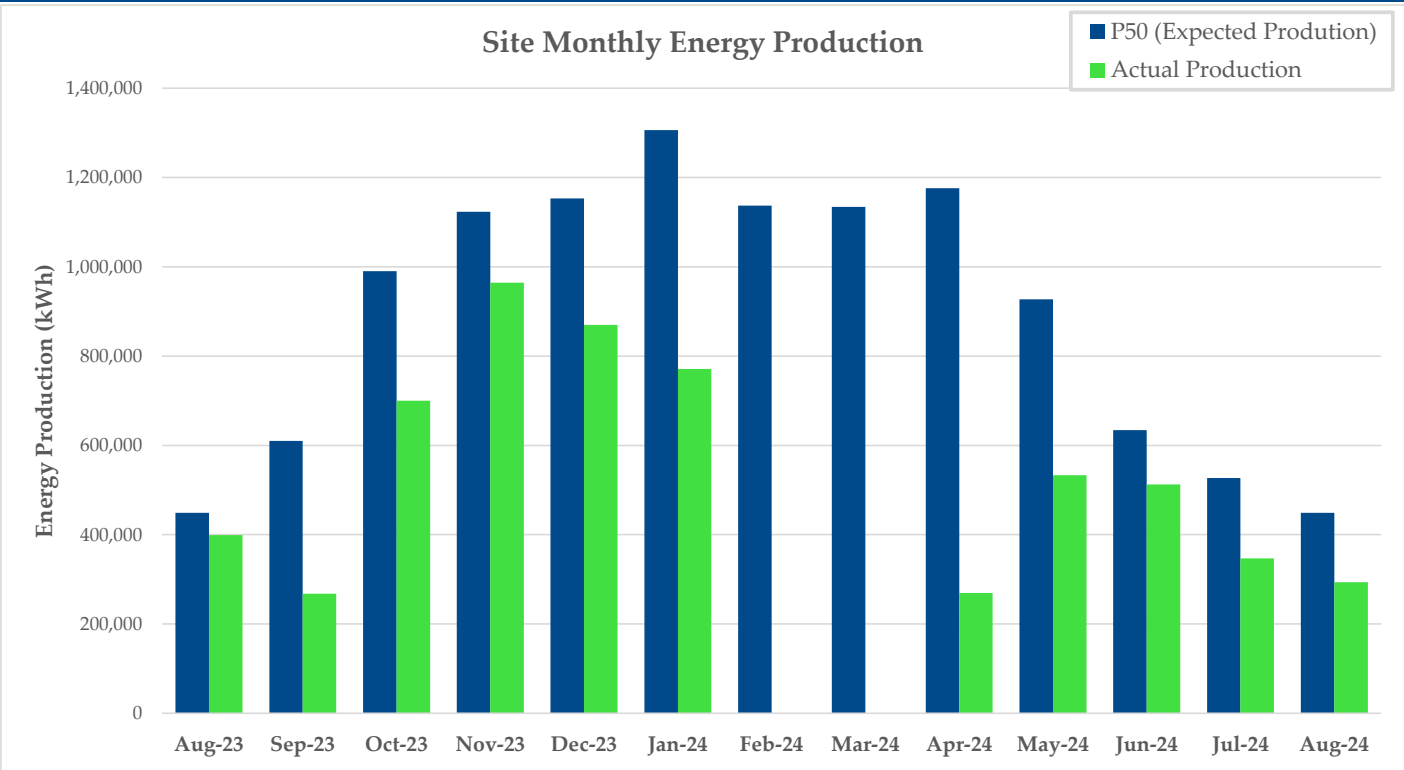

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2024	6.5 Year Preventive Maintenance	~8	W1
September-2024	6.5 Year Preventive Maintenance	~8	W2
September-2024	6.5 Year Preventive Maintenance	~8	W3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
W1	2.17	2214.40
W2	1.71	2282.55
W3	1.82	2250.95
Total	5.70	6747.90

G. Billed Data

Meter Reading (Date/Time)	8/21/2024 12:00 AM
Meter To Date Produced	59,140,855 kWh
Meter To Date Consumed	202,300 kWh
Last Reading Produced	58,835,602 kWh
Last Reading Consumed	197,834 kWh
Billed kWh	300,787 kWh
Next Meter Reading	9/21/2024 12:00 AM

H. Report Notes and Comments

¹Turbine Availability/Downtime Pending

²As a result of previously disclosed circumstances, the project had no energy prodction February 2024-March 2024.
