




A. Site Energy Production Summary

|                             | Energy Production (kWh) |                   |                                           |           |           |
|-----------------------------|-------------------------|-------------------|-------------------------------------------|-----------|-----------|
|                             | Site                    |                   | By Turbine                                |           |           |
|                             | Expected Production     | Actual Production | WTG A                                     | WTG B     | WTG C     |
| Apr-17                      | 1,447,248               | 1,676,860         | 570,960                                   | 544,340   | 561,560   |
| May-17                      | 1,010,966               | 1,309,614         | 447,560                                   | 424,304   | 437,750   |
| Jun-17                      | 668,411                 | 1,199,560         | 427,710                                   | 365,940   | 405,910   |
| Jul-17                      | 638,097                 | 608,374           | 208,860                                   | 199,814   | 199,700   |
| Aug-17                      | 577,992                 | 550,820           | 193,760                                   | 179,770   | 177,290   |
| Sep-17                      | 631,697                 | 605,096           | 208,710                                   | 201,632   | 194,754   |
| Oct-17                      | 1,003,602               | 1,223,590         | 422,370                                   | 411,740   | 389,480   |
| Nov-17                      | 1,395,914               | 1,441,140         | 493,690                                   | 470,470   | 476,980   |
| Dec-17                      | 1,278,858               | 1,521,630         | 522,010                                   | 495,750   | 503,870   |
| Jan-18                      | 1,332,437               | 1,726,420         | 585,680                                   | 568,390   | 572,350   |
| Feb-18                      | 1,157,019               | 1,303,000         | 447,860                                   | 426,380   | 428,760   |
| Mar-18                      | 1,242,761               | 1,576,970         | 530,020                                   | 505,480   | 541,470   |
| Apr-18                      | 1,447,248               | 1,316,810         | 462,450                                   | 405,270   | 449,090   |
| Production 2018 (ytd) (kWh) | 5,179,464               | 5,923,200         | 2,026,010                                 | 1,905,520 | 1,991,670 |
| Total Production (kWh)*     | 12,384,999              | 14,383,024        | 4,950,680                                 | 4,654,940 | 4,777,404 |
| Capacity Factor*            | 36.49%                  |                   | *Value calculated over the last 12 months |           |           |

B. Site Energy Production Graph

April-2018

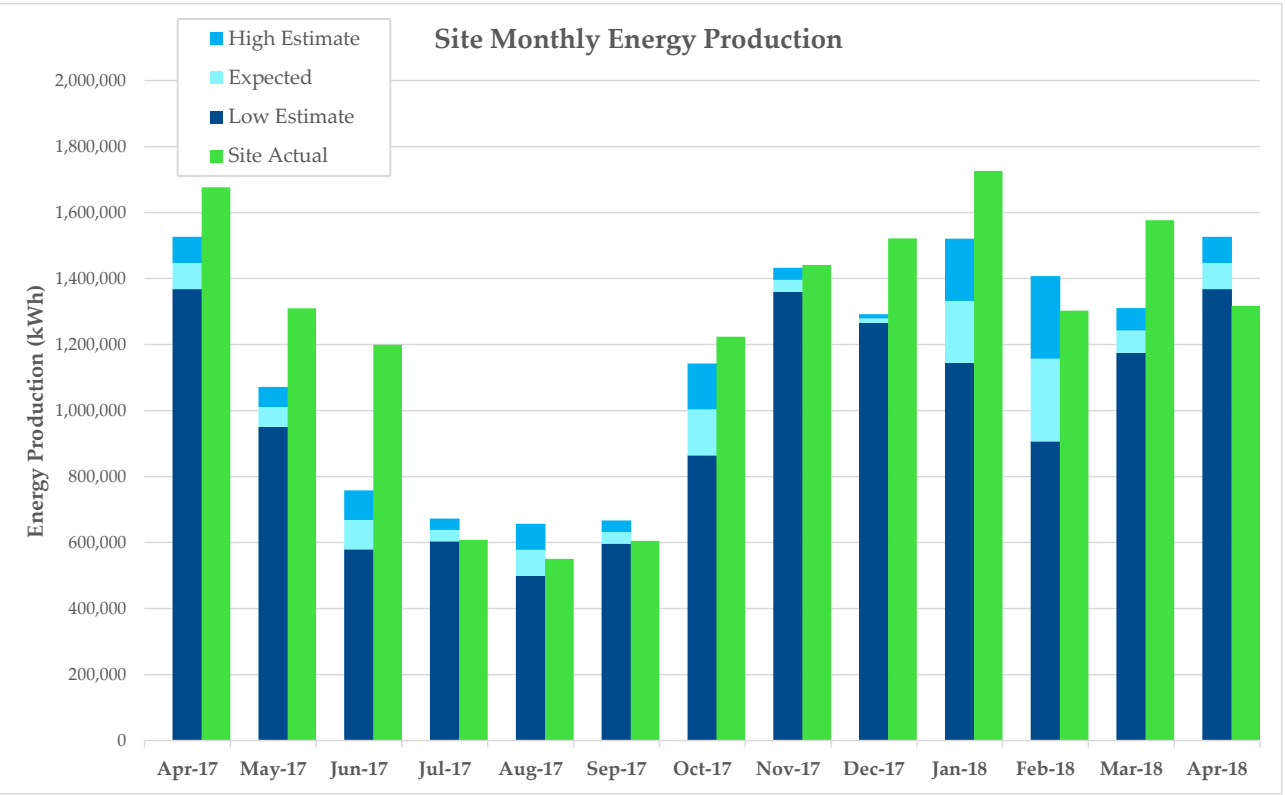

Monthly Report  
April-2018



C. Safety Summary

|                        | This Month | Project Cumulative |
|------------------------|------------|--------------------|
| Recordable Incident(s) | 0          | 0                  |
| Near Miss(es)          | 0          | 0                  |

D. Planned Maintenance Events\*

| Date      | Event                       | Duration (hr) | Turbine |
|-----------|-----------------------------|---------------|---------|
| June-2018 | Goldwind 6 Year Maintenance | ~15           | WTG A   |
| June-2018 | Goldwind 6 Year Maintenance | ~15           | WTG B   |
| June-2018 | Goldwind 6 Year Maintenance | ~15           | WTG C   |

E. Actual Maintenance Events - April 2018

| Date      | Event                                   | Planned/Unplanned | Duration (hr) | Turbine |
|-----------|-----------------------------------------|-------------------|---------------|---------|
| 4/15/2018 | Grid current unsymmetric error - Sunday | Unplanned         | 18.64         | WTG B   |
| 4/16/2018 | Grid current unsymmetric error          | Unplanned         | 11.05         | WTG B   |
| 4/23/2018 | Re-torque stiffener                     | Unplanned         | 5.14          | WTG A   |
| 4/24/2018 | Re-torque stiffener                     | Unplanned         | 4.84          | WTG C   |
| 4/27/2018 | Re-torque stiffener                     | Unplanned         | 4.37          | WTG B   |

F. Turbine Availability & Downtime

| Availability (%) | This Month | Year to Date |
|------------------|------------|--------------|
| WTG A            | 99.26%     | 98.68%       |
| WTG B            | 97.37%     | 98.70%       |
| WTG C            | 99.33%     | 99.83%       |
| Avg              | 98.65%     | 99.07%       |

| Downtime (hr) | This Month | Year to Date |
|---------------|------------|--------------|
| WTG A         | 6.76       | 91.75        |
| WTG B         | 38.46      | 110.74       |
| WTG C         | 7.52       | 61.17        |
| Total         | 52.74      | 263.66       |

G. Wind Speed & Capacity Factor

| Wind Speed (mph) | This Month | 2018 Annual |
|------------------|------------|-------------|
| WTG A            | 13.26      | 14.03       |
| WTG B            | 13.09      | 13.92       |
| WTG C            | 13.97      | 14.62       |
| Estimated        | 16.62      | 13.39       |

| Capacity Factor (%) | This Month | 2018 Annual |
|---------------------|------------|-------------|
| WTG A               | 42.82%     | 46.90%      |
| WTG B               | 37.53%     | 44.11%      |
| WTG C               | 41.58%     | 46.10%      |
| Low Estimate        | 42.22%     | 45.70%      |

H. Report Notes and Comments
