



BALL CORPORATION - ZEPHYR WIND PROJECT


North Findlay Wind Campus, Findlay, OH

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Apr-17	1,453,000	1,263,804	425,766	415,442	422,596
May-17	924,000	1,123,269	395,614	347,574	380,081
Jun-17	645,000	952,539	334,400	300,615	317,524
Jul-17	586,000	453,808	163,793	151,302	138,713
Aug-17	614,000	448,585	157,969	145,785	144,831
Sep-17	529,000	440,963	153,200	143,235	144,528
Oct-17	992,000	1,058,436	362,133	353,715	342,588
Nov-17	1,295,000	458,432	161,489	151,599	145,344
Dec-17	1,565,000	1,254,048	438,743	412,984	402,321
Jan-18	1,325,000	1,462,888	465,096	513,360	484,432
Feb-18	1,391,000	1,063,264	366,030	354,111	343,123
Mar-18	1,229,000	1,271,280	440,697	415,334	415,249
Apr-18	1,453,000	1,062,956	353,238	350,019	359,699
Production 2018 (ytd) (kWh)	5,398,000	4,860,388	1,625,061	1,632,824	1,602,503
Total Production (kWh)*	12,548,000	11,050,468	3,792,402	3,639,633	3,618,433
Capacity Factor*	28.03%		*Value calculated over the last 12 months		

B. Site Energy Production Graph

April-2018

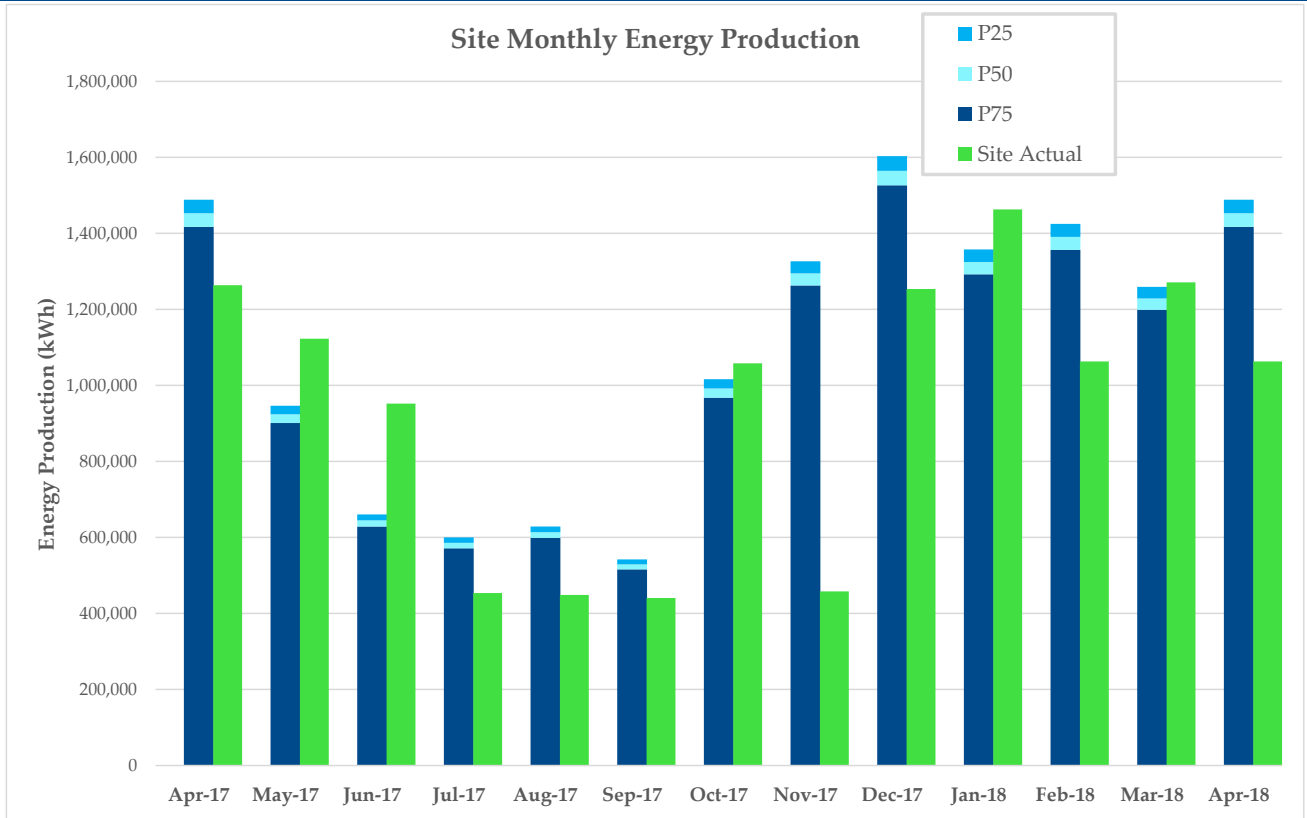

Monthly Report

April-2018



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2018	Goldwind 2.5 Year Maintenance	~8	Z1
September-2018	Goldwind 2.5 Year Maintenance	~8	Z2
September-2018	Goldwind 2.5 Year Maintenance	~8	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/2/2018	Goldwind 2 Year Maintenance	Planned	6.31	Z3
4/5/2018	Goldwind 2 Year Maintenance	Planned	6.68	Z2
4/5/2018	Goldwind 2 Year Maintenance	Planned	10.16	Z3
4/6/2018	Goldwind 2 Year Maintenance	Planned	2.12	Z2
4/9/2018	Goldwind 2 Year Maintenance	Planned	6.43	Z1
4/9/2018	Goldwind 2 Year Maintenance	Planned	0.75	Z2
4/9/2018	Goldwind 2 Year Maintenance	Planned	0.62	Z3
4/13/2018	Goldwind 2 Year Maintenance	Planned	5.28	Z1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
Z1	99.56%	96.91%
Z2	99.89%	99.97%
Z3	100.00%	99.57%
Avg	99.82%	98.82%

Downtime (hr)	This Month	Year To Date
Z1	20.91	154.44
Z2	11.98	59.62
Z3	18.76	106.04
Total	51.65	320.10

G. Billed Data

Meter Reading (Date/Time)	4/18/2018 12:00 AM
Meter To Date Produced	26,309,580 kWh
Meter To Date Consumed	29,532 kWh
Last Reading Produced	24,909,774 kWh
Last Reading Consumed	28,816 kWh
Billed kWh	1,399,090 kWh
Next Meter Reading	5/18/2018 12:00 AM

H. Report Notes and Comments
