



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Project	
	P50	Actual YTD
May-16	311,000	222,331
Jun-16	228,000	194,723
Jul-16	179,000	112,289
Aug-16	157,000	133,798
Sep-16	224,000	160,959
Oct-16	338,000	312,037
Nov-16	402,000	369,112
Dec-16	403,000	400,649
Jan-17	460,000	402,596
Feb-17	372,000	406,678
Mar-17	417,000	434,411
Apr-17	399,000	412,306
May-17	311,000	335,979
2017 Annual	3,890,000	1,991,970
Rolling 12 month Capacity Factor:		27.97%

B. Site Energy Production Graph

May-2017

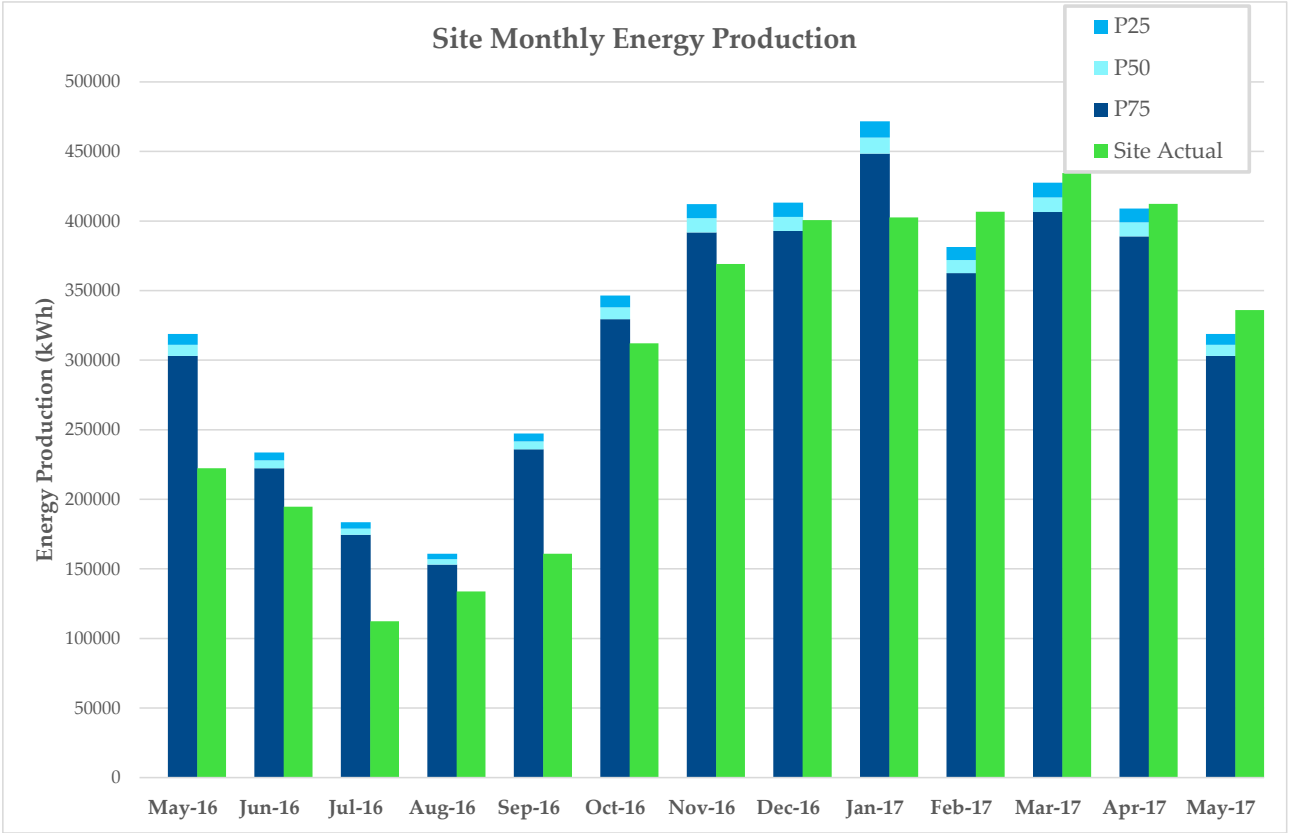

Monthly Report

May-2017



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s):	0	0
Near Miss(es):	0	0

D. Planned Maintenance Events

Date	Event	Duration (hrs)	Wind Turbine
August-2017	Goldwind 1.5 year maintenance	~8	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Wind Turbine
4/10/2017	Grid Fault	Unplanned	4.55	H1

F. Turbine Availability & Downtime

Availability	This Month	Year To Date
WTG	99.97%	98.78%
Downtime (hrs)	This Month	Year To Date
WTG	9.57	137.60

G. Billed Data

Meter Read Date & Time	5/26/2017 12:00 AM
Meter To Date Produced	4,490,322 kWh
Meter To Date Consumed	15,517 kWh
Last Reading Produced	4,140,776 kWh
Last Reading Consumed	14,951 kWh
Billed kWh	348,981 kWh
Next Meter Reading	6/27/2017 12:00 AM

H. Report Notes and Comments

- Before April-2016, actual YTD production and Capacity Factor are based on Meter Read - Net Production
- Starting in April-2016, all future YTD production and Capacity Factor information will be based on SCADA Data - Gross Production
