


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Jan-24	455,000	329,993
Feb-24	478,000	0
Mar-24	422,000	0
Apr-24	499,000	113,878
May-24	318,000	259,723
Jun-24	222,000	260,126
Jul-24	201,000	113,237
Aug-24	211,000	0
Sep-24	182,000	0
Oct-24	341,000	0
Nov-24	445,000	279,948
Dec-24	537,000	475,185
Jan-25	455,000	522,801
Production 2025 (ytd) (kWh)	455,000	522,801
Total Production (LTM) (kWh)	4,311,000	2,024,898
Capacity Factor (LTM)	15.37%	

B. Site Energy Production Graph

January-2025

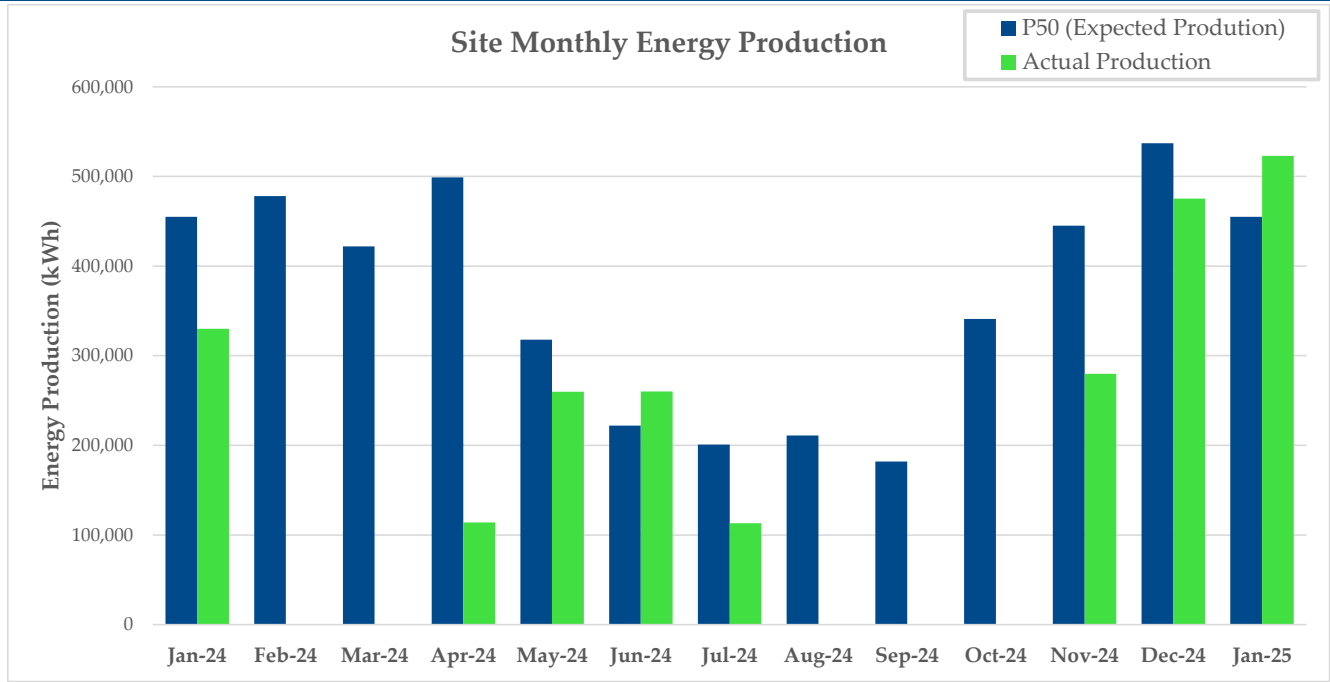

Monthly Report
January-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2025	6.5 Year Preventive Maintenance	~8	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
1/1/2025	Grid Fault	Unplanned	13.73	W1
1/7/2025	6.5 Year Preventive Maintenance	Planned	1.95	W1

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
W1	26.29	26.29

G. Billed Data

Meter Reading (Date/Time)	2/1/2025 12:00 AM
Meter To Date Produced	25,693,496 kWh
Meter To Date Consumed	141,273 kWh
Last Reading Produced	25,177,230 kWh
Last Reading Consumed	140,746 kWh
Billed kWh	515,739 kWh
Next Meter Reading	3/1/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, the project had no energy production February 2024 - March 2024.

³ Turbine down due to utility substation catastrophic event 7/20/2024-11/9/2024.
