



BALL CORPORATION - ZEPHYR WIND PROJECT 1.0

North Findlay Wind Campus, Findlay, OH

Monthly Report

February-2025



ONE POWER COMPANY


AN INDUSTRIAL POWER COMPANY

A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Feb-24	1,310,000	0	0	0	0
Mar-24	1,140,000	0	0	0	0
Apr-24	1,359,000	290,385	101,675	110,982	77,728
May-24	856,000	675,531	232,841	224,129	218,561
Jun-24	599,000	666,365	228,319	222,302	215,744
Jul-24	549,000	408,393	144,779	135,803	127,811
Aug-24	559,000	396,364	137,674	134,332	124,358
Sep-24	482,000	468,646	179,579	178,791	110,276
Oct-24	916,000	815,845	288,194	271,762	255,889
Nov-24	1,203,000	856,131	346,454	195,160	314,517
Dec-24	1,475,000	1,183,437	338,701	436,335	408,401
Jan-25	1,260,000	1,498,704	519,090	499,488	480,126
Feb-25	1,310,000	777,633	278,062	278,866	220,705
Production 2025 (ytd) (kWh)	2,570,000	2,276,337	797,152	778,354	700,831
Total Production (LTM) (kWh)	11,708,000	8,037,434	2,795,368	2,687,950	2,554,116
Capacity Factor (LTM)	20.39%				

B. Site Energy Production Graph

February-2025

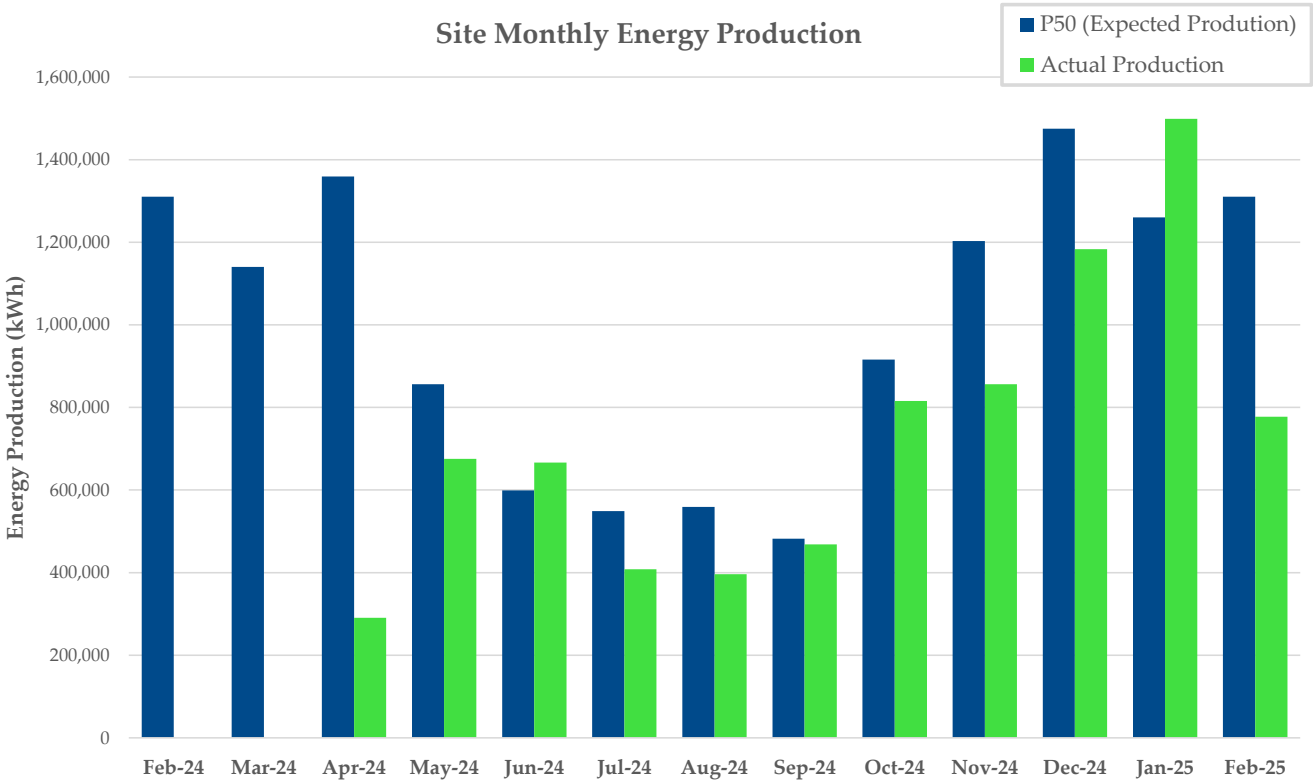

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
March-2025	8.5 Year Turbine Preventive Maintenance	~8	Z1
March-2025	8.5 Year Turbine Preventive Maintenance	~8	Z2
March-2025	8.5 Year Turbine Preventive Maintenance	~8	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/3/2025	8.5 Year Turbine Preventive Maintenance	Planned	1.41	Z1
2/3/2025	8.5 Year Turbine Preventive Maintenance	Planned	1.36	Z2
2/6/2025	Weather Shutdown	Unplanned	4.79	Z1, Z2, Z3
2/8/2025-2/9/2025	Weather Shutdown	Unplanned	24.49	Z1, Z2, Z3
2/10/2025	Weather Shutdown	Unplanned	11.98	Z1
2/10/2025	Weather Shutdown	Unplanned	1.49	Z2
2/10/2025	Weather Shutdown	Unplanned	11.73	Z3
2/12/2025	8.5 Year Turbine Preventive Maintenance	Planned	1.99	Z1
2/12/2025	8.5 Year Turbine Preventive Maintenance	Planned	1.91	Z2
2/12/2025	8.5 Year Turbine Preventive Maintenance	Planned	2.89	Z3
2/12/2025-2/15/2025	Weather Shutdown	Unplanned	69.04	Z3
2/13/2025	Weather Shutdown	Unplanned	7.39	Z1
2/13/2025	Weather Shutdown	Unplanned	8.92	Z2
2/16/2025-2/17/2025	Weather Shutdown	Unplanned	27.48	Z1
2/16/2025-2/17/2025	Weather Shutdown	Unplanned	27.55	Z2
2/16/2025-2/17/2025	Weather Shutdown	Unplanned	27.87	Z3
2/17/2025-2/18/2025	Turbine Fault	Unplanned	28.82	Z1
2/25/2025	8.5 Year Turbine Preventive Maintenance	Planned	7.20	Z1
2/26/2025	8.5 Year Turbine Preventive Maintenance	Planned	7.98	Z1
2/27/2025-2/28/2025	Turbine Fault	Unplanned	38.26	Z3

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
Z1	126.94	129.23
Z2	73.45	76.30
Z3	166.03	166.87
Total	366.42	372.40

G. Billed Data

Meter Reading (Date/Time)	2/19/2025 12:00 AM
Ball 1.0 Production (This Period)	922,365 kWh
Ball 1.0 Consumption (This Period)	1,747 kWh
Billed kWh	920,618 kWh
Next Meter Reading	3/20/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, the project had no energy production February 2024 - March 2024.

³ Z1 derated to 1000 kW for 4.32 hours on Dec 17
