


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	W1	W2	W3
Feb-24	1,137,000	0	0	0	0
Mar-24	1,134,000	0	0	0	0
Apr-24	1,176,000	269,672	87,026	88,258	94,388
May-24	927,000	533,339	180,109	172,157	181,073
Jun-24	634,000	512,583	178,220	152,008	182,355
Jul-24	527,000	347,033	118,853	106,389	121,791
Aug-24	449,000	293,672	100,620	93,127	99,925
Sep-24	610,000	401,369	130,058	125,317	145,994
Oct-24	990,000	624,977	226,024	151,986	246,967
Nov-24	1,123,000	1,012,898	346,441	326,379	340,078
Dec-24	1,153,000	890,936	306,203	296,619	288,114
Jan-25	1,306,000	1,219,137	428,208	389,061	401,868
Feb-25	1,137,000	646,378	234,980	200,956	210,442
Production 2025 (ytd) (kWh)	2,443,000	1,865,515	663,188	590,017	612,310
Total Production (LTM) (kWh)	11,166,000	6,751,994	2,336,742	2,102,257	2,312,995
Capacity Factor (LTM)	17.13%				

B. Site Energy Production Graph

February-2025

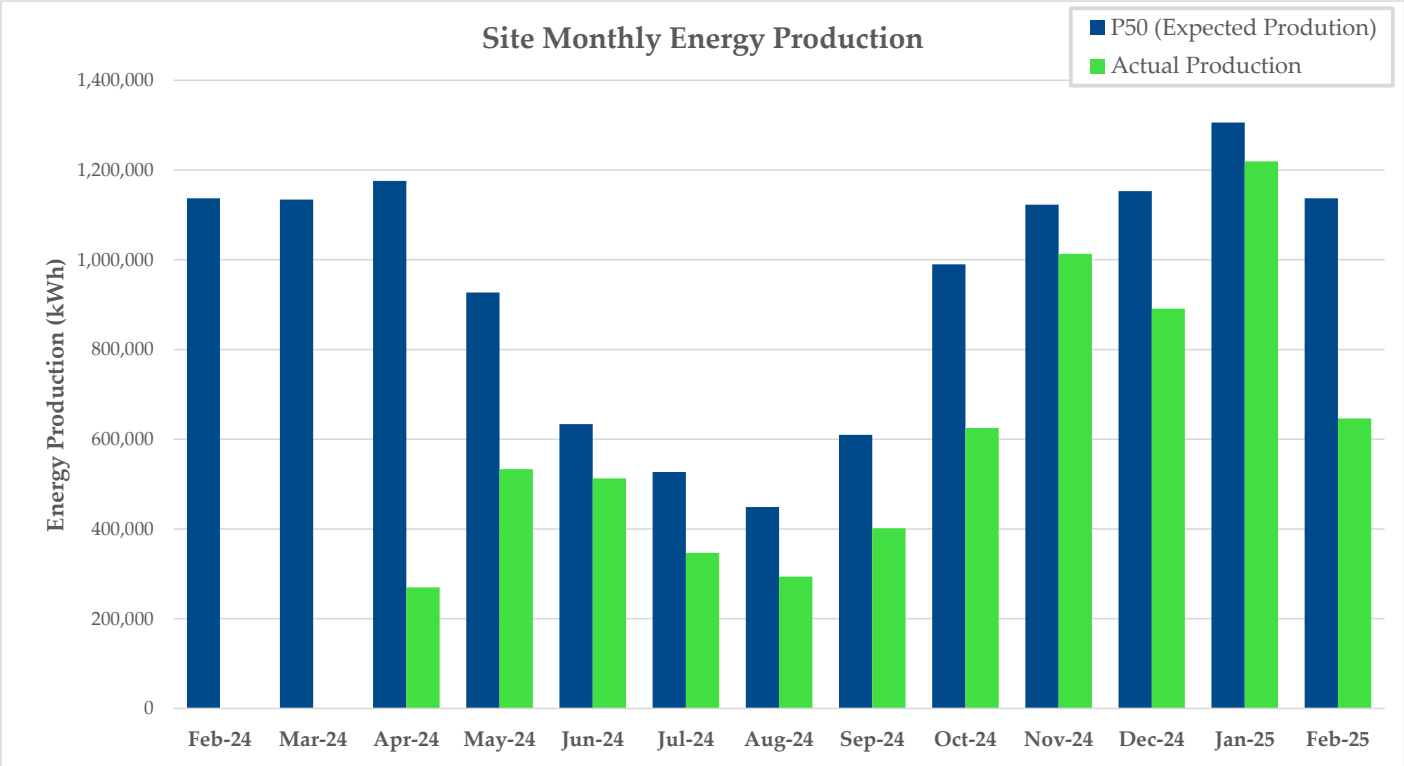

Monthly Report
February-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2025	7 Year Preventive Maintenance	~15	W1
April-2025	7 Year Preventive Maintenance	~15	W1
April-2025	7 Year Preventive Maintenance	~15	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/6/2025	Weather shutdown	Unplanned	7.14	W1, W2, W3
2/8/2025-2/10/2025	Weather shutdown	Unplanned	45.48	W1, W2, W3
2/12/2025-2/13/2025	Weather shutdown	Unplanned	19.09	W1
2/12/2025-2/13/2025	Weather shutdown	Unplanned	19.47	W2
2/13/2025-2/14/2025	Weather shutdown	Unplanned	20.69	W3
2/13/2025-2/14/2025	Turbine Fault	Unplanned	21.05	W2
2/16/2025-2/17/2025	Weather shutdown	Unplanned	26.7	W1,W2
2/16/2025-2/18/2025	Weather shutdown	Unplanned	51.49	W3
2/21/2025	7 Year Preventive Maintenance	Planned	3.12	W1,W2,W3

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
W1	103.87	111.79
W2	126.61	128.61
W3	131.64	134.06
Total	362.12	374.46

G. Billed Data

Meter Reading (Date/Time)	2/21/2025 12:00 AM
Meter To Date Produced	63,615,615 kWh
Meter To Date Consumed	217,107 kWh
Last Reading Produced	62,795,996 kWh
Last Reading Consumed	215,001 kWh
Billed kWh	817,513 kWh
Next Meter Reading	3/21/2025 12:00 AM

H. Report Notes and Comments

¹Turbine Availability/Downtime Pending

²As a result of previously disclosed circumstances, the project had no energy prodction February 2024-March 2024.

³ W1 derated to 1000 kW for 14.17 hrs on Oct 29 and Oct 31

³ W2 derated to 800 kW for 21.6 hrs on Oct 23 and Oct 24

³W2 derated to 1000 kW for 48.01 hrs on Oct 29, Oct 30,and Oct 31

³W1 derated to 1000 kW for 41.8 hrs Nov 4 - Nov 6, and Nov 20 - Nov 21

³W3 derated to 1000 kW for 25 hrs Nov 5 - Nov 6

³W1 derated to 1000 kW for 24.35 hrs Dec 4 - Dec 5

³W1 derated to 1000 kW for 17.27 hrs Dec 16-Dec 17

³W1 derated to 1000 kW for 21.45 hrs Jan 28-Jan 29

³W1 derated to 1000 kW for 23.16 hrs Feb 27-Feb 28
