


A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Feb-24	478,000	0 ²
Mar-24	422,000	0 ²
Apr-24	499,000	113,878
May-24	318,000	259,723
Jun-24	222,000	260,126
Jul-24	201,000	113,237
Aug-24	211,000	0 ³
Sep-24	182,000	0 ³
Oct-24	341,000	0 ³
Nov-24	445,000	279,948 ³
Dec-24	537,000	475,185
Jan-25	455,000	522,801
Feb-25	478,000	267,129
Production 2025 (ytd) (kWh)	933,000	789,930
Total Production (LTM) (kWh)	4,311,000	2,292,027
Capacity Factor (LTM)	17.44%	

B. Site Energy Production Graph

February-2025

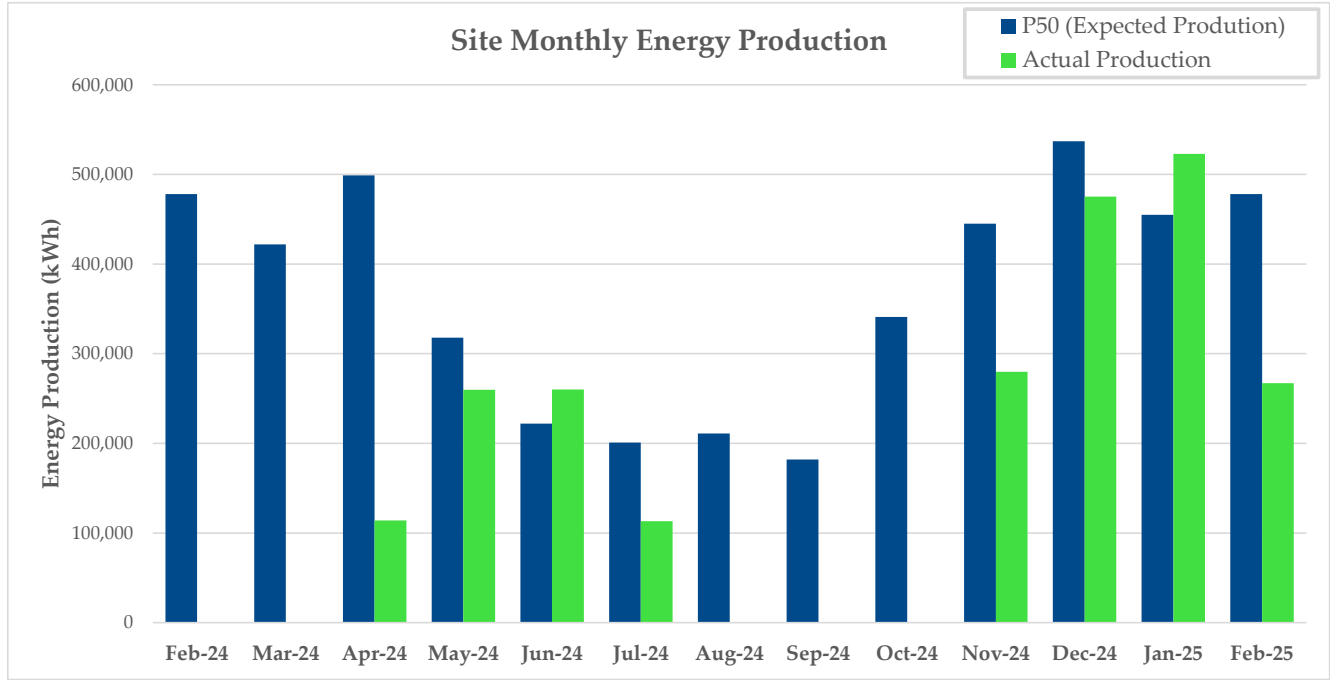

Monthly Report
February-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
May-2025	6.5 Year Preventive Maintenance	~8	W1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
2/4/2025-2/5/2025	Grid Fault	Unplanned	21.31	W1
2/6/2025	Weather Shutdown	Unplanned	7.39	W1
2/8/2025-2/10/2025	Weather Shutdown	Unplanned	43.94	W1
2/12/2025-2/14/2025	Weather Shutdown	Unplanned	40.39	W1
2/16/2025-2/17/2025	Weather Shutdown	Unplanned	29.86	W1
2/18/2025-2/19/2025	Grid Fault	Unplanned	15.82	W1
2/27/2025	6.5 Year Preventive Maintenance	Planned	0.75	W1
2/27/2025	Grid Fault	Unplanned	6.60	W1

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
W1	169.71	196.00

G. Billed Data

Meter Reading (Date/Time)	3/1/2025 12:00 AM
Meter To Date Produced	25,956,850 kWh
Meter To Date Consumed	143,427 kWh
Last Reading Produced	25,693,496 kWh
Last Reading Consumed	141,273 kWh
Billed kWh	261,200 kWh
Next Meter Reading	4/1/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, the project had no energy production February 2024 - March 2024.

³ Turbine down due to utility substation catastrophic event 7/20/2024-11/9/2024.
